

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete	11/14		Dece
									11	
1		Establish Team Structures / Organization	10 days	Fri 12/3/10	Thu 12/16/10		100%			
2		Identify Team Roles	1 day	Fri 12/3/10	Fri 12/3/10		100%			
3		Define Team Values and Norms	1 wk	Fri 12/3/10	Thu 12/9/10	2	100%			
4		Finish Team Norms and Values	0 days	Thu 12/9/10	Thu 12/9/10	3	100%			
5		Establish Meeting Times	1 hr	Fri 12/3/10	Fri 12/3/10	2	100%			
6		Establish Preliminary Schedule	2 wks	Fri 12/3/10	Thu 12/16/10	5	100%			
7		Identify Customer Needs and Engineering Specs	11 days	Fri 12/3/10	Fri 12/17/10		100%			
8		Meet with Project Sponser	1 day	Fri 12/3/10	Fri 12/3/10		100%			
9		Customer Needs Document	1 wk	Mon 12/6/10	Fri 12/10/10	8	100%			
10		Develop Engineering Specs Document	1 wk	Mon 12/13/10	Fri 12/17/10	9	100%			
11		Develop Project Unknowns Document	1 wk	Mon 12/6/10	Fri 12/10/10	8	100%			
12		System Level Design Review	22 days	Mon 12/20/10	Tue 1/18/11		100%			

Project: Senior Design Prelim
Date: Mon 2/21/11

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete	11/14		Dece
									11	
13		Sythesize Various Concepts Documentation	2 wks	Mon 12/20/10	Fri 12/31/10	10,11	100%			
14		Risks Assesment Document	4 days	Mon 1/10/11	Thu 1/13/11	13FS+1 wk	100%			
15		Concept Evaluation Documentation	2 wks	Mon 12/20/10	Fri 12/31/10	13SS	100%			
16		System Analysis Documentation	1 wk	Mon 1/3/11	Fri 1/7/11	13FS+4 days	100%			
17		System Design Documentation	1 wk	Thu 1/6/11	Wed 1/12/11	15FS+3 days,13	100%			
18		Determine if the Design Meets Customer Needs	2 days	Thu 1/13/11	Fri 1/14/11	17	100%			
19		Prepare for Systems Level Design Review	1 day	Thu 1/13/11	Thu 1/13/11	18SS,6,4	100%			
20		Systems Level Design Review	1 day	Fri 1/14/11	Fri 1/14/11	19	100%			
21		Review Outcome of System Design Review	1 day	Tue 1/18/11	Tue 1/18/11	20	100%			
22		Detailed Design Review	22 days	Mon 1/17/11	Tue 2/15/11		100%			
23		Begin Detailed Design	3.4 wks	Wed 1/19/11	Thu 2/10/11	21	100%			

Project: Senior Design Prelim
Date: Mon 2/21/11

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete	11/14		Dece
									11	
24		Complete Subsystems Interface Specifications	1 wk	Wed 1/19/11	Tue 1/25/11	21	100%			
25		Evaluate Design Options compared to Eng Specs	1 wk	Wed 1/26/11	Tue 2/1/11	24	100%			
26		Budget Planning	3.5 wks	Mon 1/17/11	Wed 2/9/11	13	100%			
27		Detailed Design Review	1 day	Fri 2/11/11	Fri 2/11/11	26,25,24,23	100%			
28		Review Outcome of Detailed Design Review	1 day	Tue 2/15/11	Tue 2/15/11	27FS+1 day	100%			
29		Project Review	10 days?	Wed 2/16/11	Tue 3/1/11		52%			
30		Prepare for Project Review	3 days	Wed 2/16/11	Fri 2/18/11	28	100%			
31		Project Review	0.75 days	Mon 2/21/11	Mon 2/21/11	30	0%			


Project: Senior Design Prelim
Date: Mon 2/21/11

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete	11/14		Dece
									11	
32		Evaluate outcomes of Project Review	1 day	Tue 2/22/11	Tue 2/22/11	31	0%			
33		Prepare for MSDII	1 day?	Tue 3/1/11	Tue 3/1/11	32	0%			


Project: Senior Design Prelim
Date: Mon 2/21/11

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

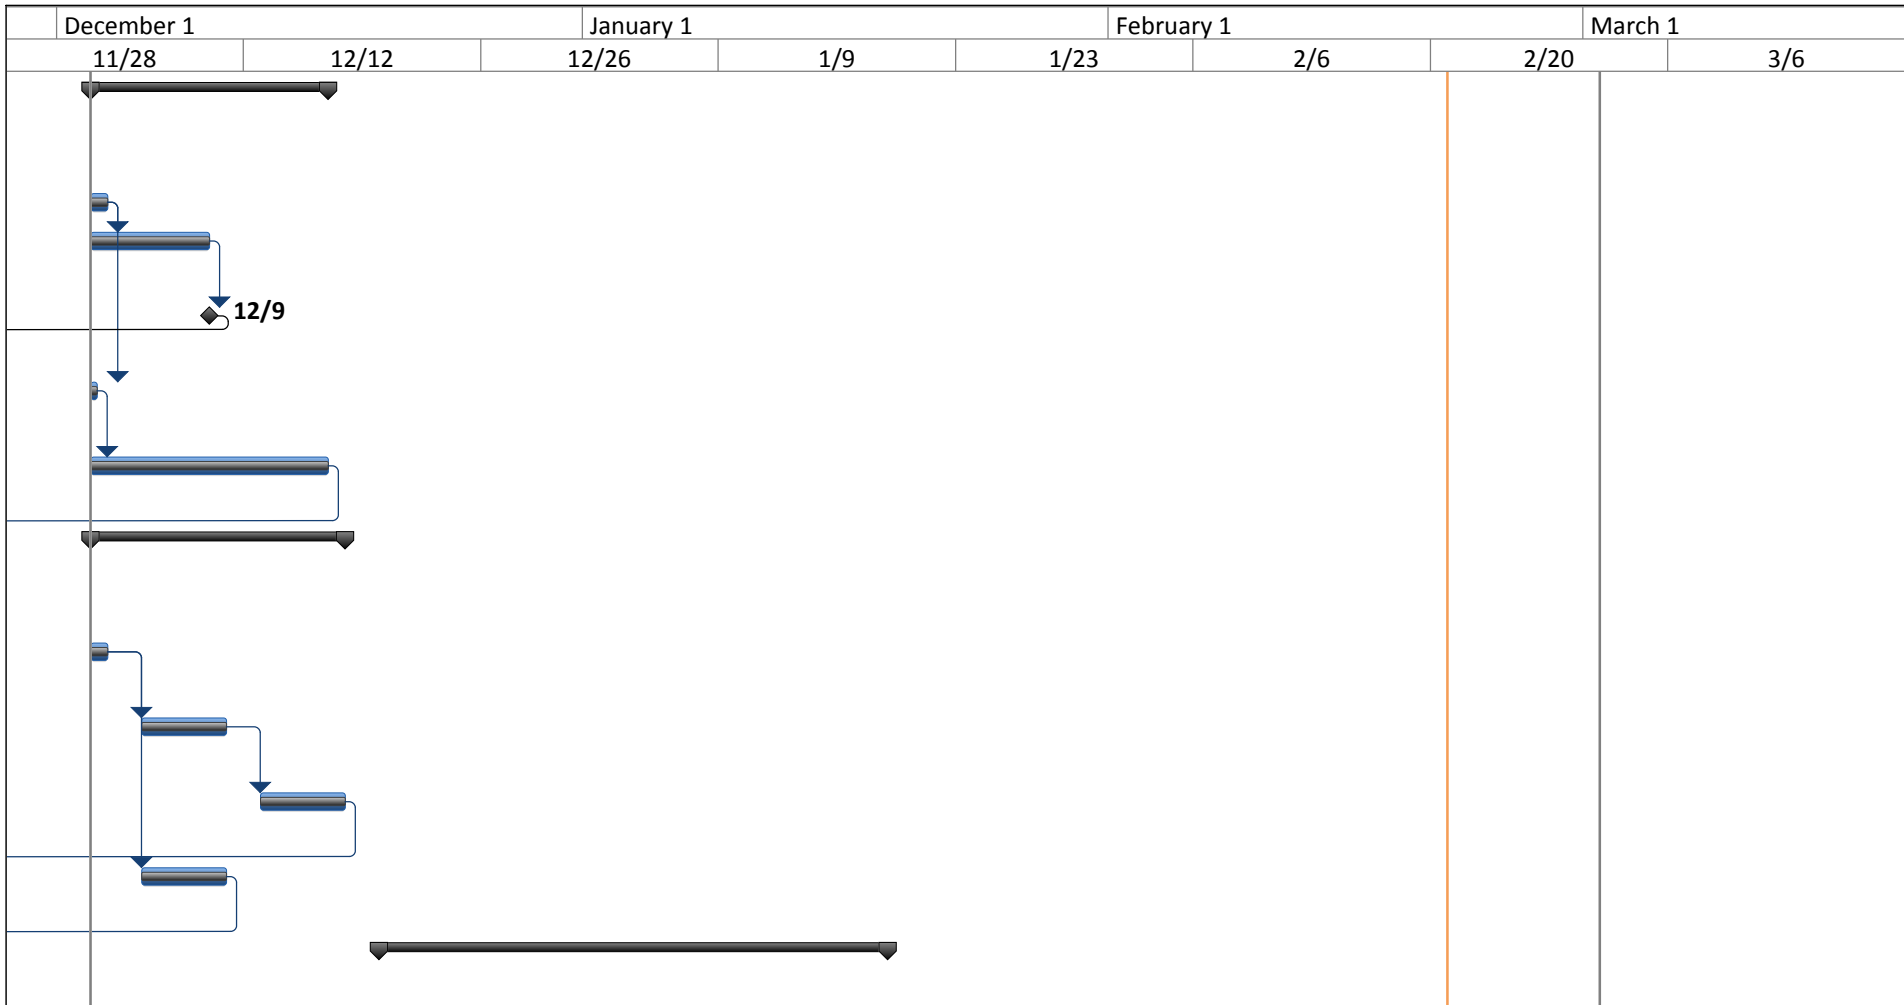


Project: Senior Design Prelim
 Date: Mon 2/21/11

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

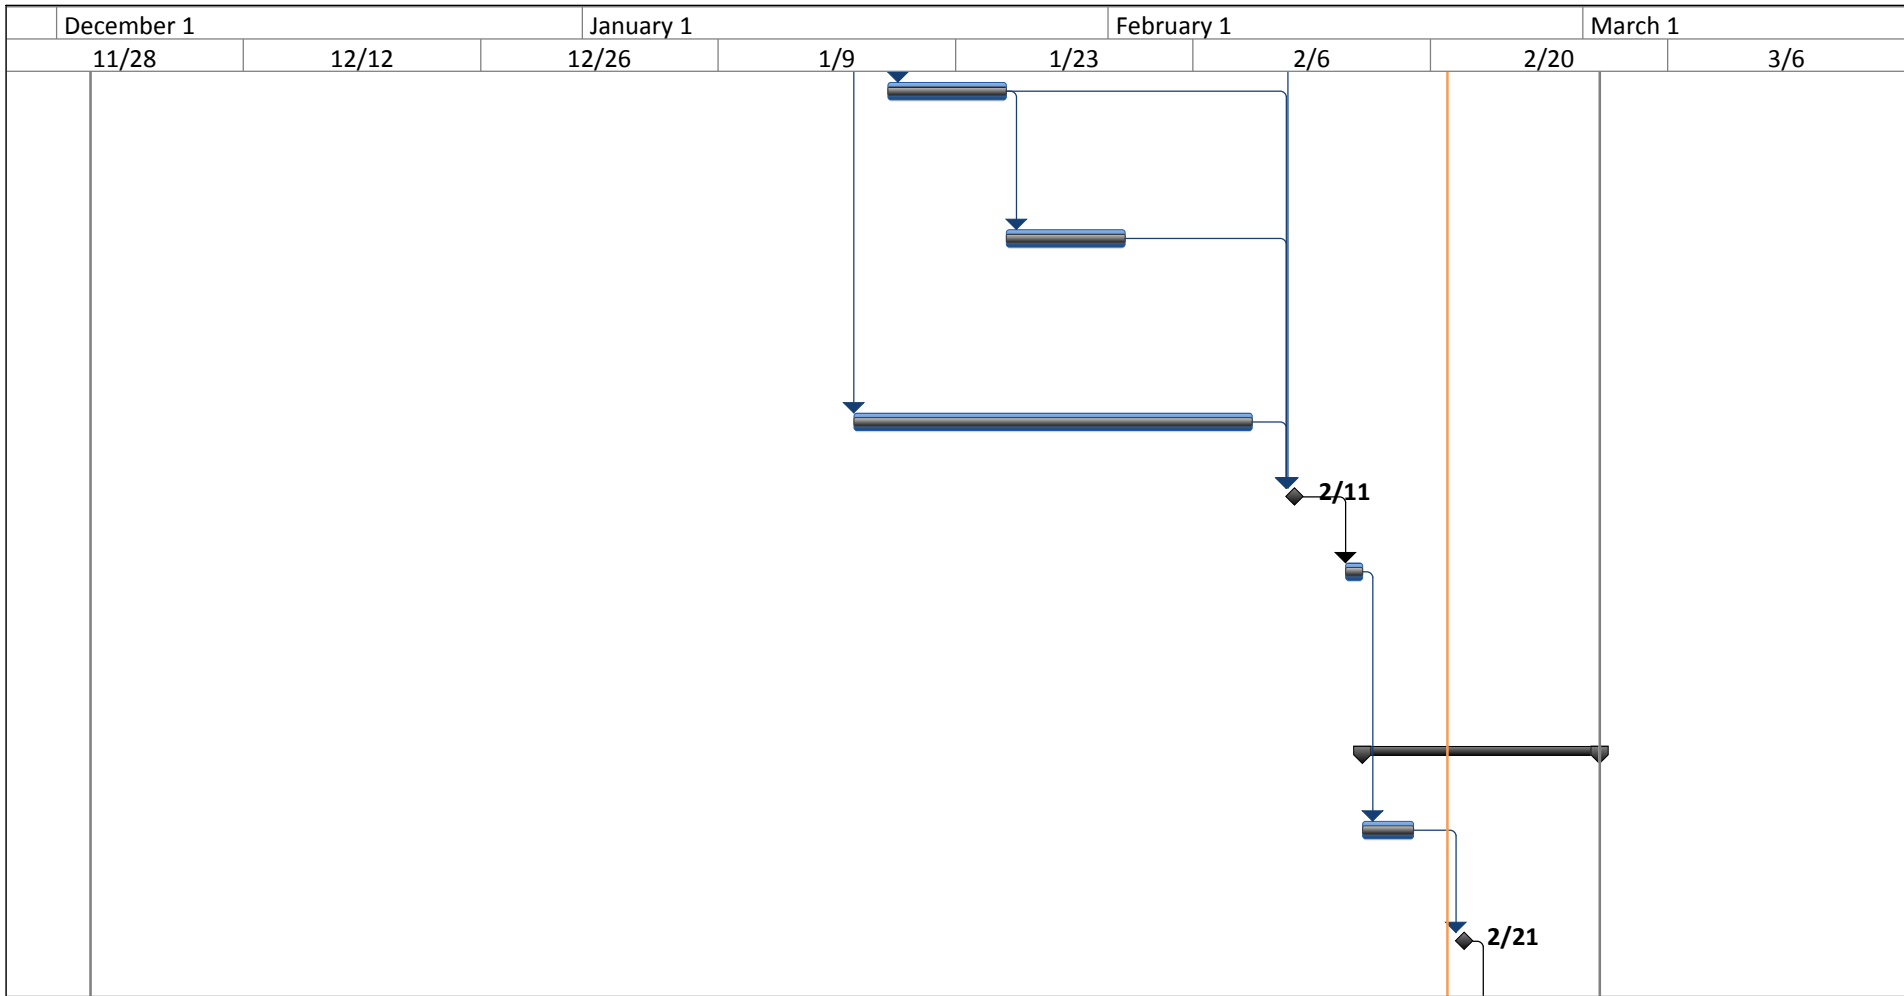

Project: Senior Design Prelim
Date: Mon 2/21/11

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

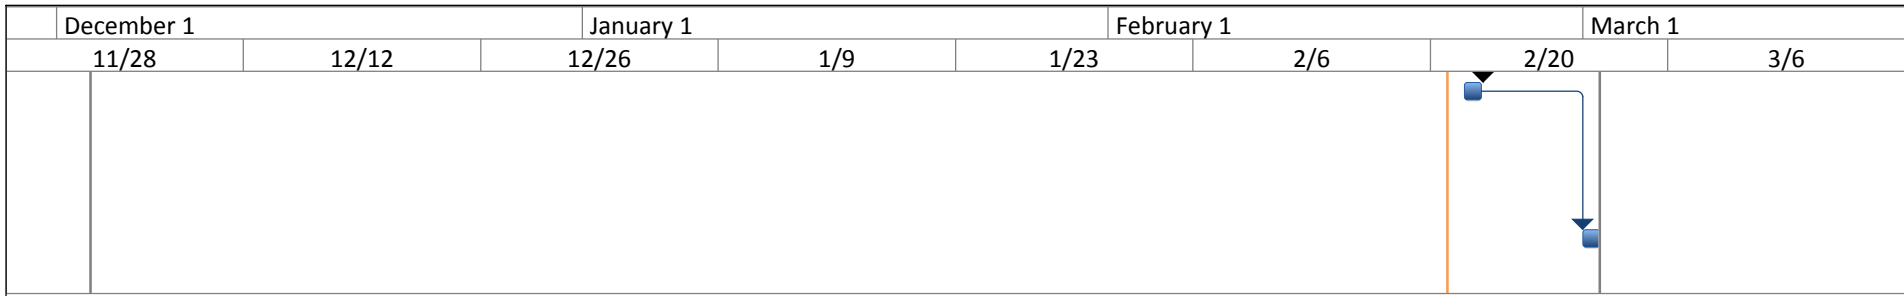

Project: Senior Design Prelim Date: Mon 2/21/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
