




















ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Sun Dec	Mon Dec	Tue Dec	Wed De	Thu Dec
							S	M	T	W	T
1	Start of Winter Quarter	0 days	Mon 12/4/06	Mon 12/4/06				◆ 12/4			
2	Project Selection	4 days	Mon 12/4/06	Thu 12/7/06	1	DPM					
3	Workshop 1:	0.97 days	Fri 12/8/06	Fri 12/8/06							
4	Course Objectives	45 mins	Fri 12/8/06	Fri 12/8/06	2						
5	Ice Breaker	45 mins	Fri 12/8/06	Fri 12/8/06	4	Team					
6	Customer Meeting	1.5 hrs	Fri 12/8/06	Fri 12/8/06	5	Team					
7	Project Background	1 hr	Fri 12/8/06	Fri 12/8/06	6						
8	Roles and Responsibilities	45 mins	Fri 12/8/06	Fri 12/8/06	7	Team					
9	Needs Assessment	2 hrs	Fri 12/8/06	Fri 12/8/06	8	Team					
10	One Page Project Summa	30 mins	Fri 12/8/06	Fri 12/8/06	9	Team					
11	Days Summary	15 mins	Fri 12/8/06	Fri 12/8/06	10	11					
12	5 minute presentation	15 mins	Fri 12/8/06	Fri 12/8/06	11	PM					
13	Needs Assesment	3 days	Tue 12/12/06	Thu 12/14/06							
14	Customer Meeting	2 hrs	Tue 12/12/06	Tue 12/12/06	12	Mike,Brian,Jeff					
15	Project Schedule	2 days	Wed 12/13/06	Thu 12/14/06	14	Mike					
16	Research ADA Regulations	2 days	Wed 12/13/06	Thu 12/14/06		Myong					
17	Familiarization with Pro-E (2 days	Wed 12/13/06	Thu 12/14/06		Dave					
18	Benchmark mechanisms/ r	2 days	Wed 12/13/06	Thu 12/14/06		Brain					
19	Benchmark materials	2 days	Wed 12/13/06	Thu 12/14/06		Alicia					
20	Familiarization with Pro-E (2 days	Wed 12/13/06	Thu 12/14/06		Jeff					
21	Workshop 2:	0.69 days	Fri 12/15/06	Fri 12/15/06							
22	Customer Needs to Specs	1 hr	Fri 12/15/06	Fri 12/15/06	20,19,18,17,16,15						
23	Review Needs Assessmen	1 hr	Fri 12/15/06	Fri 12/15/06	22	Team					
24	Specification Development	2.5 hrs	Fri 12/15/06	Fri 12/15/06	23	Team					
25	Days Summary	30 mins	Fri 12/15/06	Fri 12/15/06	24	Team					
26	5 minute presentation	30 mins	Fri 12/15/06	Fri 12/15/06	25	Mike					
27	Specification and Initial Conc	4 days	Mon 12/18/06	Thu 12/21/06							
28	Brainstrom Alternate Soluti	1 day	Mon 12/18/06	Mon 12/18/06	26	Team					
29	Brainstorm/Organize/Reco	1 day	Tue 12/19/06	Tue 12/19/06	28	Team					
30	Translate Needs into Quan	1 day	Wed 12/20/06	Wed 12/20/06	29	Team					
31	Develop Intitial Test Docun	1 day	Thu 12/21/06	Thu 12/21/06	30	Team					


Project: 3 wk schedule Date: Fri 12/22/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	






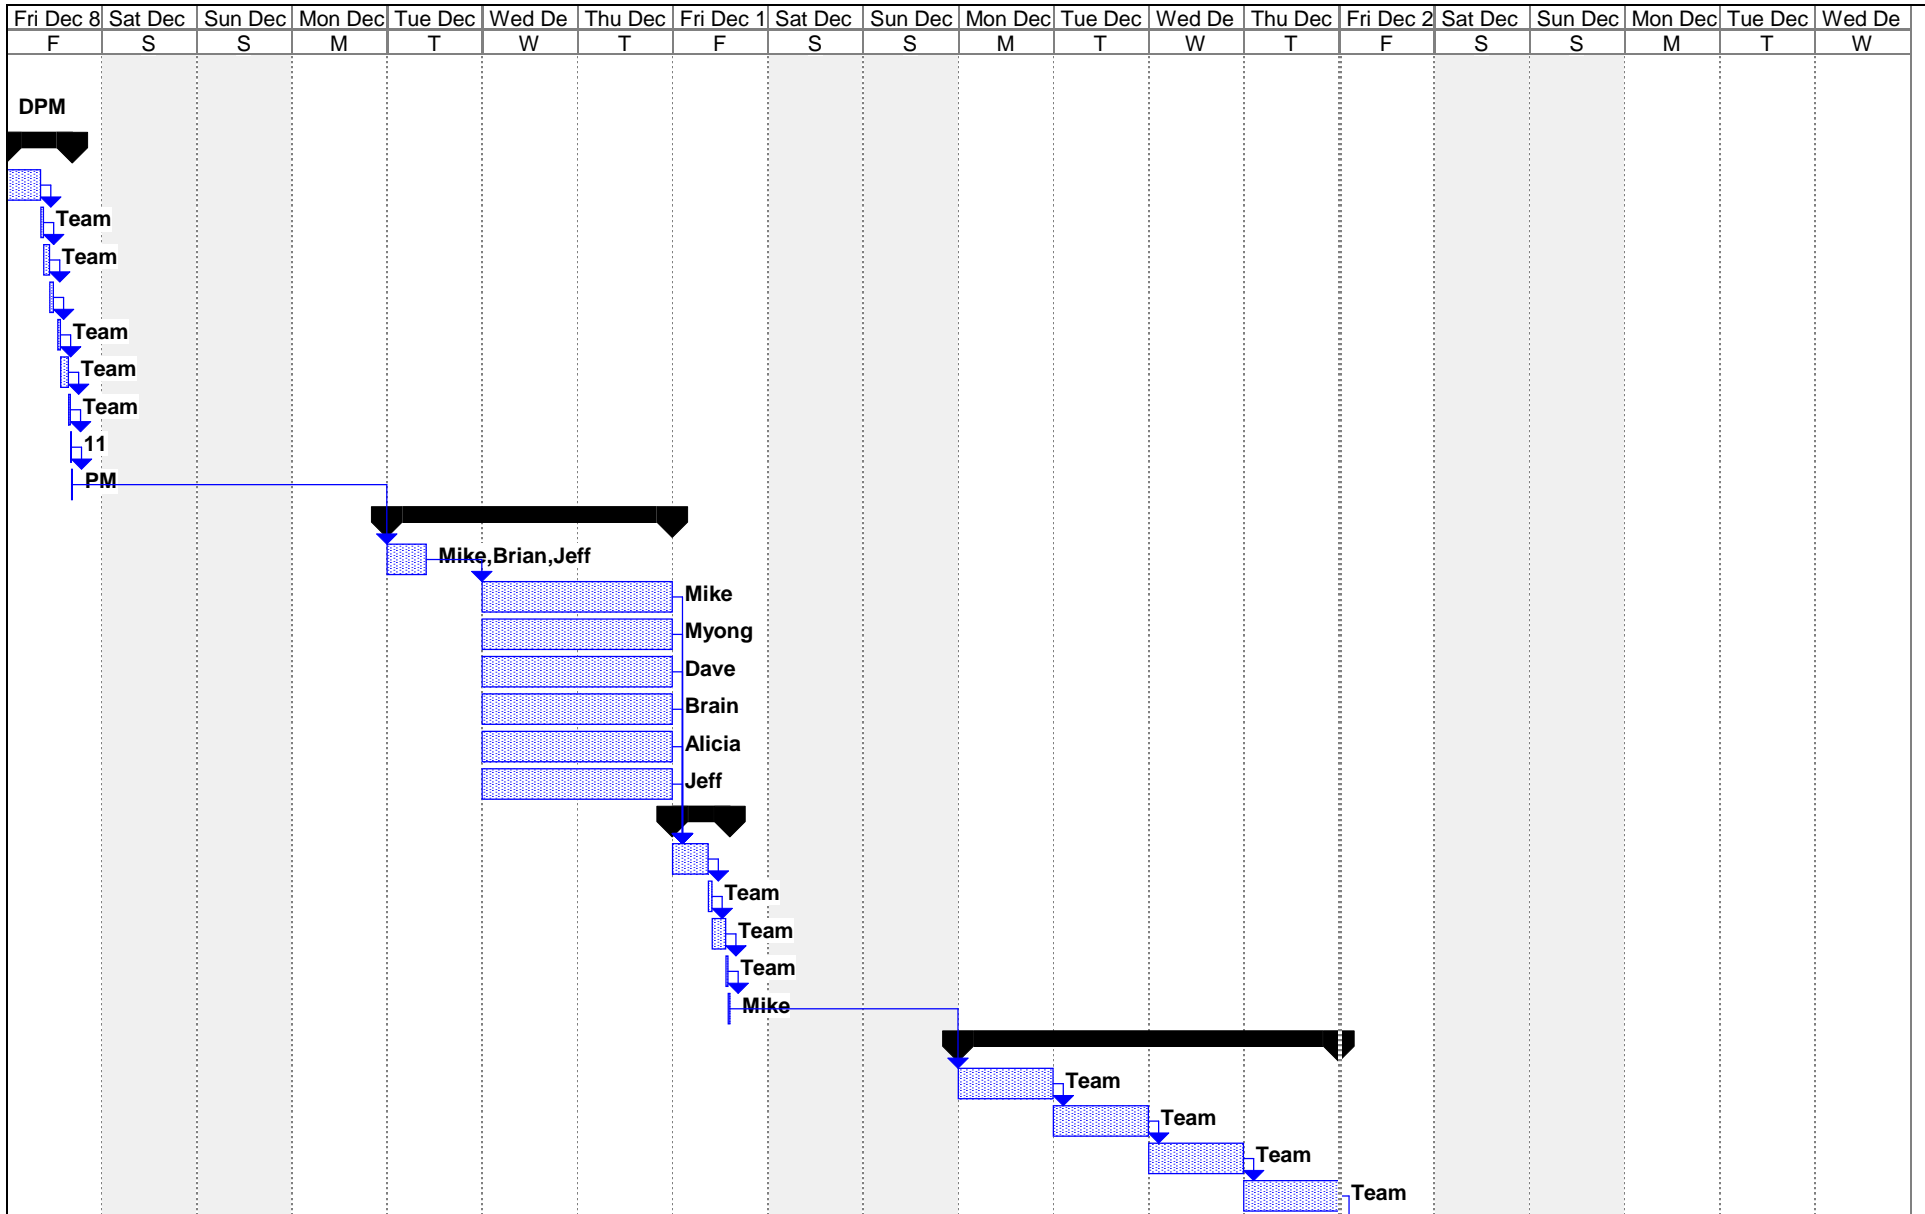

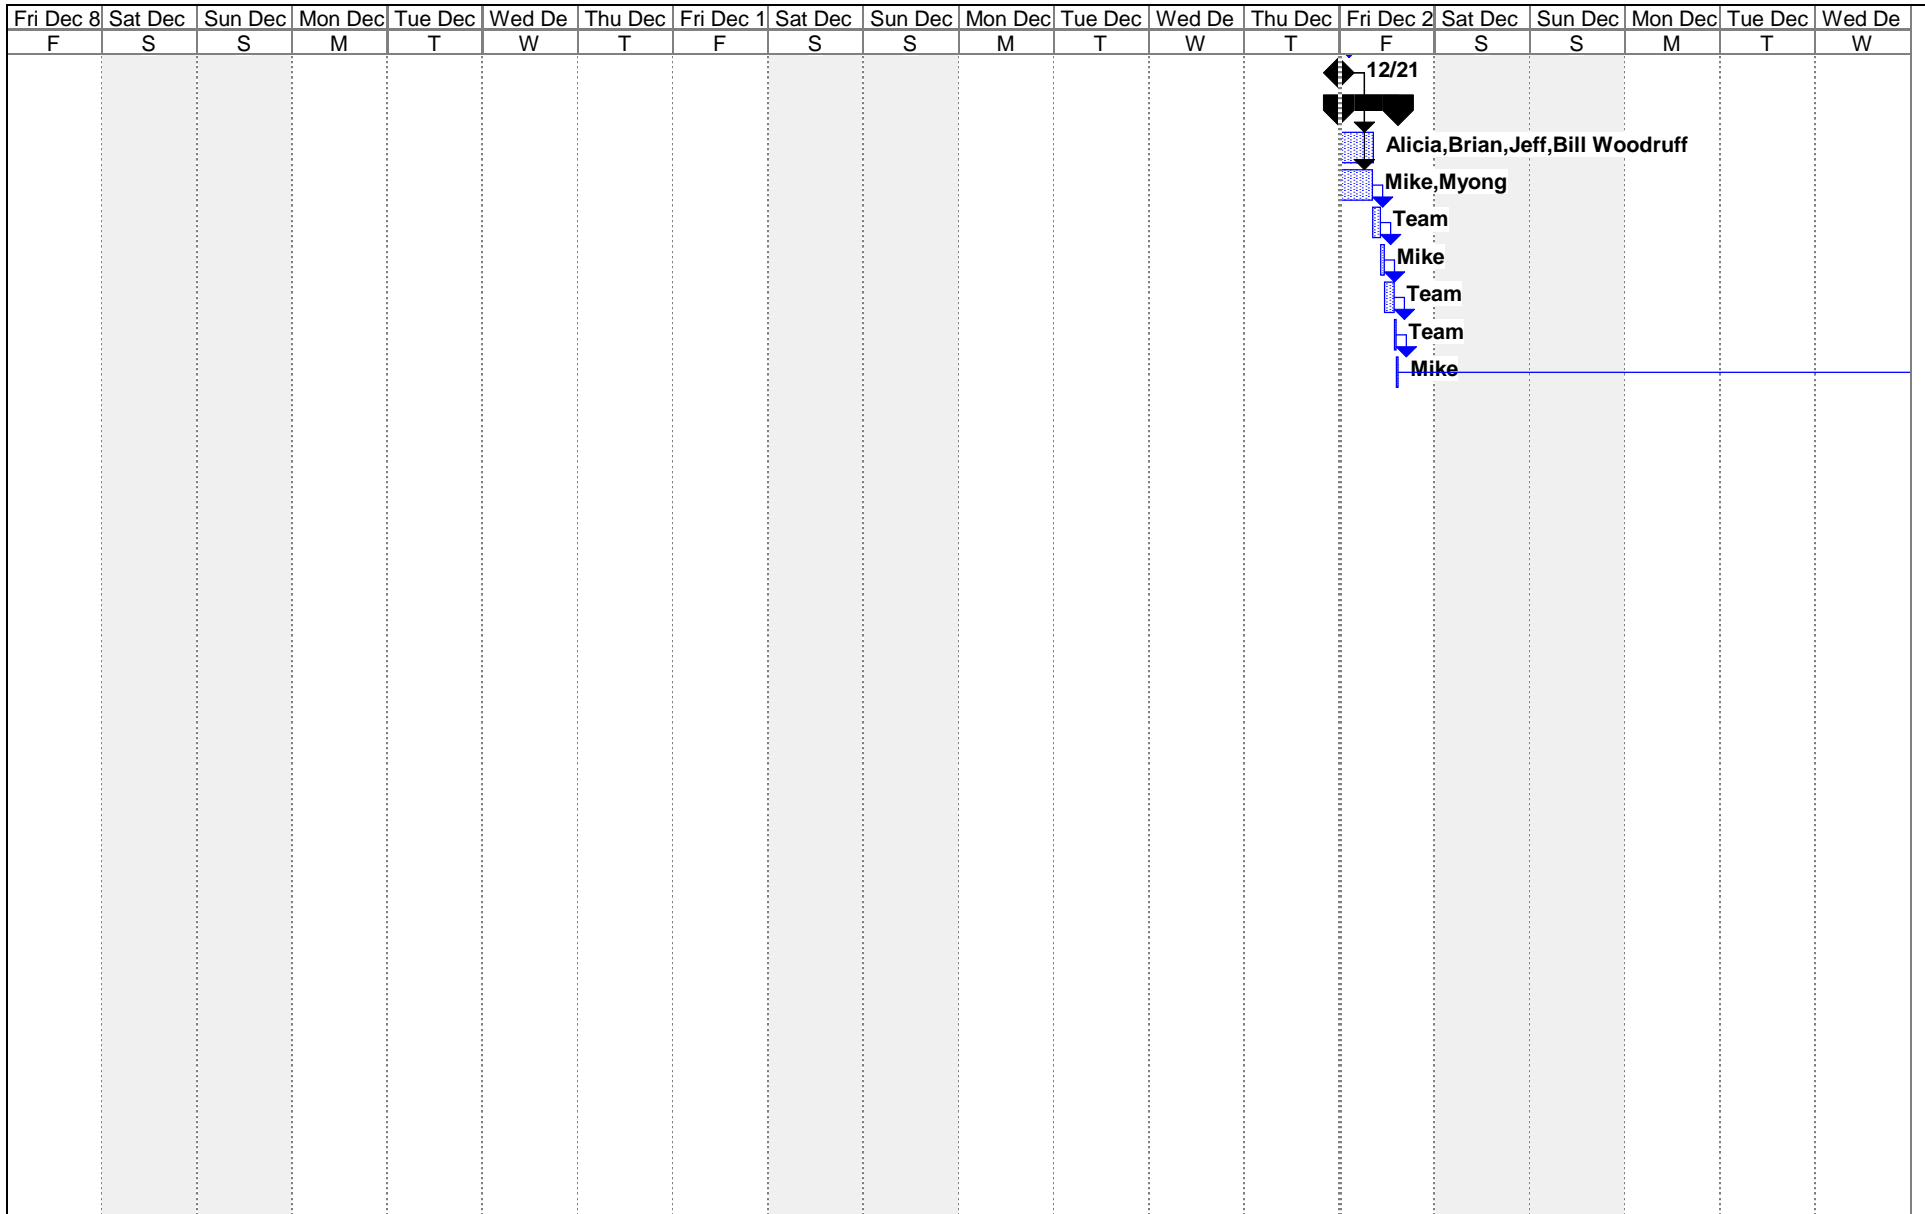

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Sun Dec	Mon Dec	Tue Dec	Wed De	Thu Dec
							S	M	T	W	T
32	Needs and Specifications I	0 days	Thu 12/21/06	Thu 12/21/06	31	Team					
33	Workshop 3:	0.75 days	Fri 12/22/06	Fri 12/22/06							
34	Ancor/Base Meeting	0.75 hrs	Fri 12/22/06	Fri 12/22/06	32	Alicia,Brian,Jeff,Bill W					
35	Team Presentations- Spec	0.5 hrs	Fri 12/22/06	Fri 12/22/06	32	Mike,Myong					
36	Concept Generation Exerci	2 hrs	Fri 12/22/06	Fri 12/22/06	35	Team					
37	WIKI/EDGE Tutorial	1 hr	Fri 12/22/06	Fri 12/22/06	36	Mike					
38	Concept Generation	1.5 hrs	Fri 12/22/06	Fri 12/22/06	37	Team					
39	Days Summary	30 mins	Fri 12/22/06	Fri 12/22/06	38	Team					
40	5 minute presentation	30 mins	Fri 12/22/06	Fri 12/22/06	39	Mike					
41	Workshop 4:	0.84 days	Fri 1/12/07	Fri 1/12/07							
42	Team Presentations- Conc	1 hr	Fri 1/12/07	Fri 1/12/07	40	Team					
43	Workshop Overview	1.25 hrs	Fri 1/12/07	Fri 1/12/07	42	Bailey					
44	Concept Dev. And Selectic	2 hrs	Fri 1/12/07	Fri 1/12/07	43	Team					
45	Concept Dev. And Selectic	1.5 hrs	Fri 1/12/07	Fri 1/12/07	44	Team					
46	Days Summary	30 mins	Fri 1/12/07	Fri 1/12/07	45	Team					
47	5 minute presentaions	30 mins	Fri 1/12/07	Fri 1/12/07	46	Mike					
48	Concept Analysis	5 days?	Mon 1/15/07	Fri 1/19/07	47						
49	Materials	3 days	Mon 1/15/07	Wed 1/17/07		Alicia					
50	Stress Analysis	3 days	Mon 1/15/07	Wed 1/17/07		Jeff					
51	Mechanics/Manufacturing	3 days	Mon 1/15/07	Wed 1/17/07		Brian					
52	Systems Integration	3 days	Mon 1/15/07	Wed 1/17/07		Dave					
53	Ergonomics	3 days	Mon 1/15/07	Wed 1/17/07		Myong					
54	Support All Analysis	3 days	Mon 1/15/07	Wed 1/17/07		Mike					
55	Prepare for Concept Selec	1 day?	Wed 1/17/07	Wed 1/17/07		Mike					
56	Concept Selection	1 day?	Thu 1/18/07	Thu 1/18/07	49,50,51,52,53,54	Team					
57	Concept Review	1 day?	Fri 1/19/07	Fri 1/19/07	56	Team					
58	Embodiment Design	3.8 wks	Mon 1/22/07	Thu 2/15/07	57	Team					
59	Cost Analysis	2.8 wks	Mon 1/29/07	Thu 2/15/07	57	Team					
60	Technical Design Review	1 day?	Fri 2/16/07	Fri 2/16/07	58,59	Team					
61	Implement Change Ideas For	4 days	Mon 2/19/07	Thu 2/22/07	60	Team					
62	Project Review	1 day?	Fri 2/23/07	Fri 2/23/07	61	Team					

Project: 3 wk schedule Date: Fri 12/22/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	













Project: 3 wk schedule Date: Fri 12/22/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	










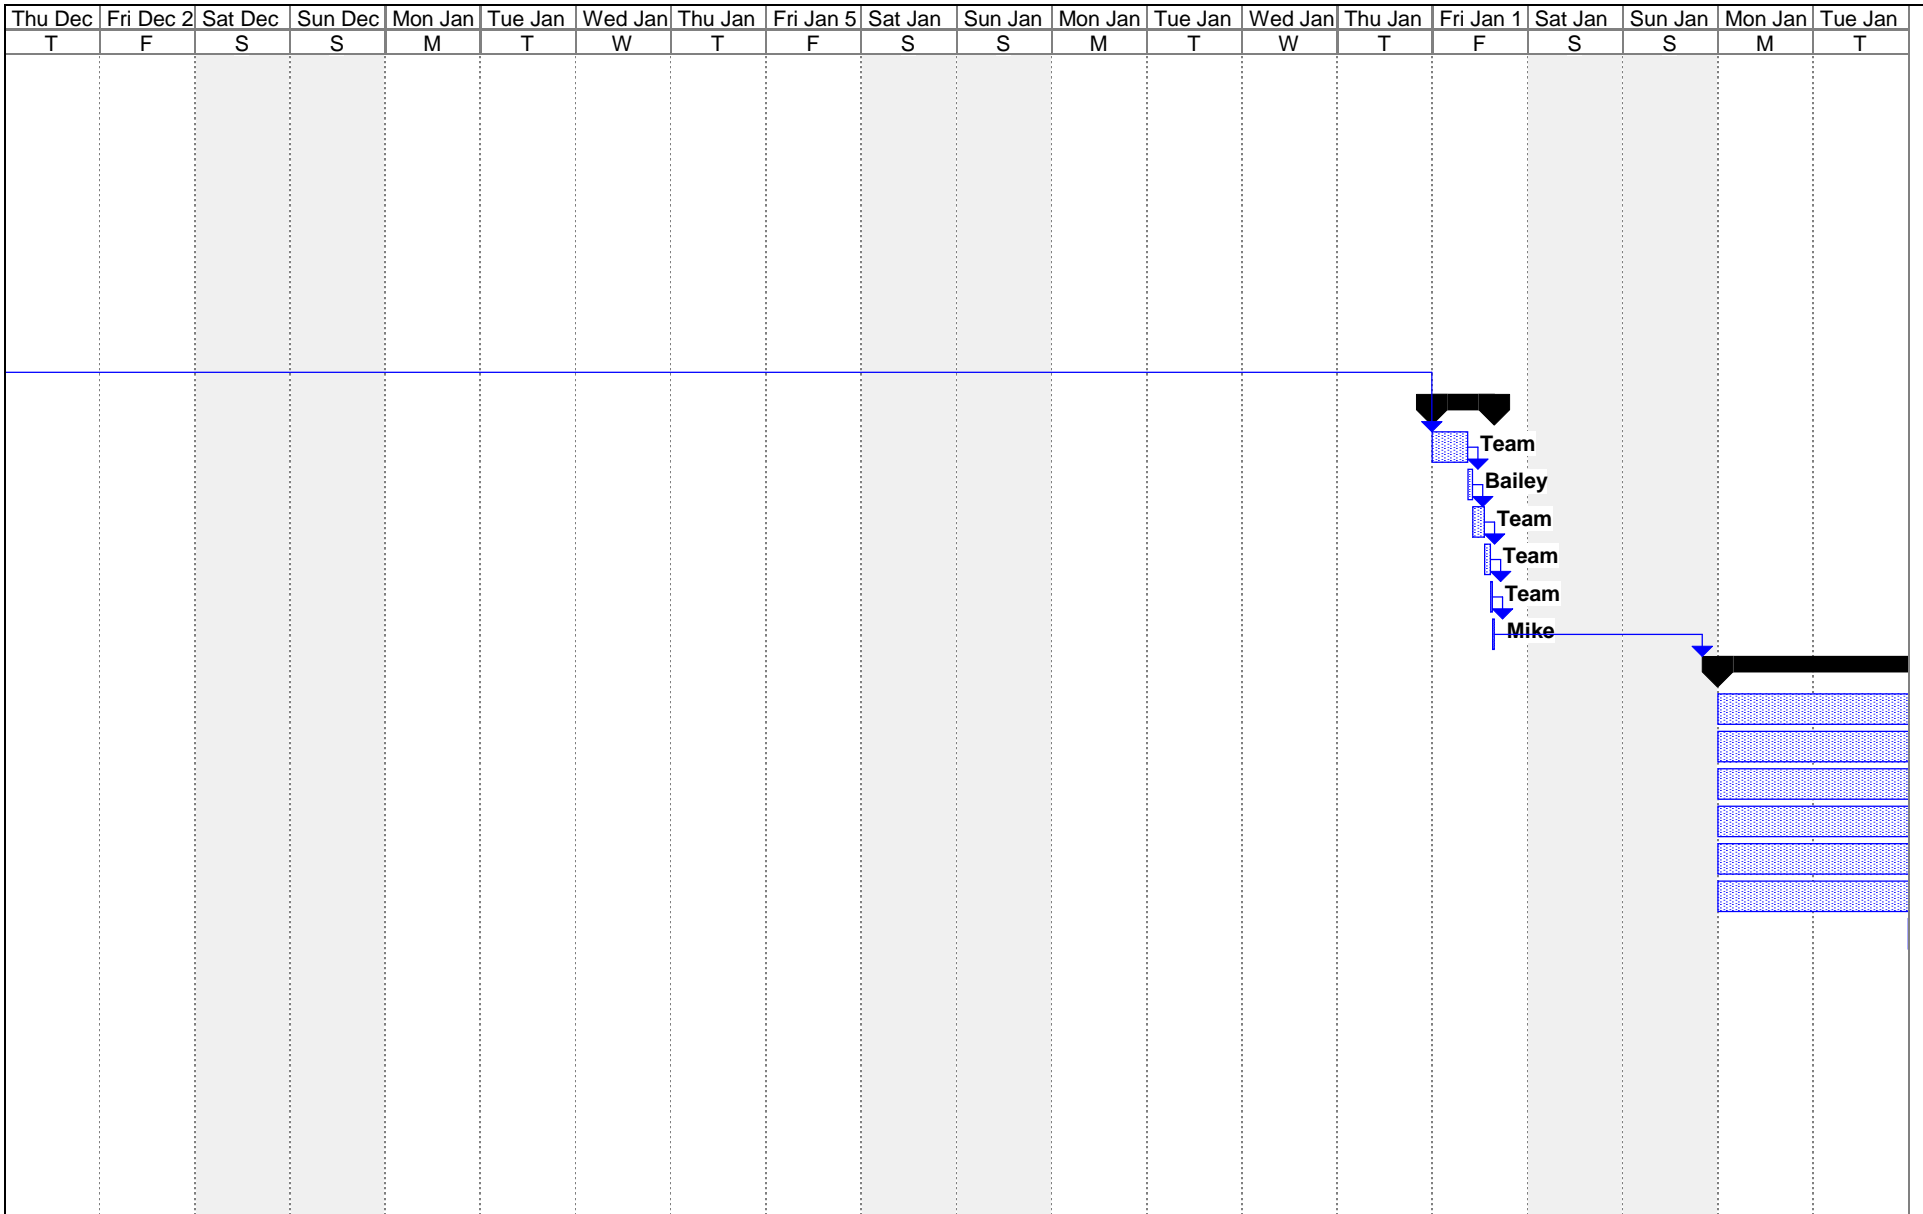

Project: 3 wk schedule Date: Fri 12/22/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	










Thu Dec	Fri Dec 2	Sat Dec	Sun Dec	Mon Jan	Tue Jan	Wed Jan	Thu Jan	Fri Jan 5	Sat Jan	Sun Jan	Mon Jan	Tue Jan	Wed Jan	Thu Jan	Fri Jan 1	Sat Jan	Sun Jan	Mon Jan	Tue Jan
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T


Project: 3 wk schedule Date: Fri 12/22/06	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 



Project: 3 wk schedule Date: Fri 12/22/06	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

Wed Jan	Thu Jan	Fri Jan 1	Sat Jan	Sun Jan	Mon Jan	Tue Jan	Wed Jan	Thu Jan	Fri Jan 2	Sat Jan	Sun Jan	Mon Jan	Tue Jan	Wed Jan	Thu Feb	Fri Feb 2	Sat Feb	Sun Feb	Mon Feb
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M




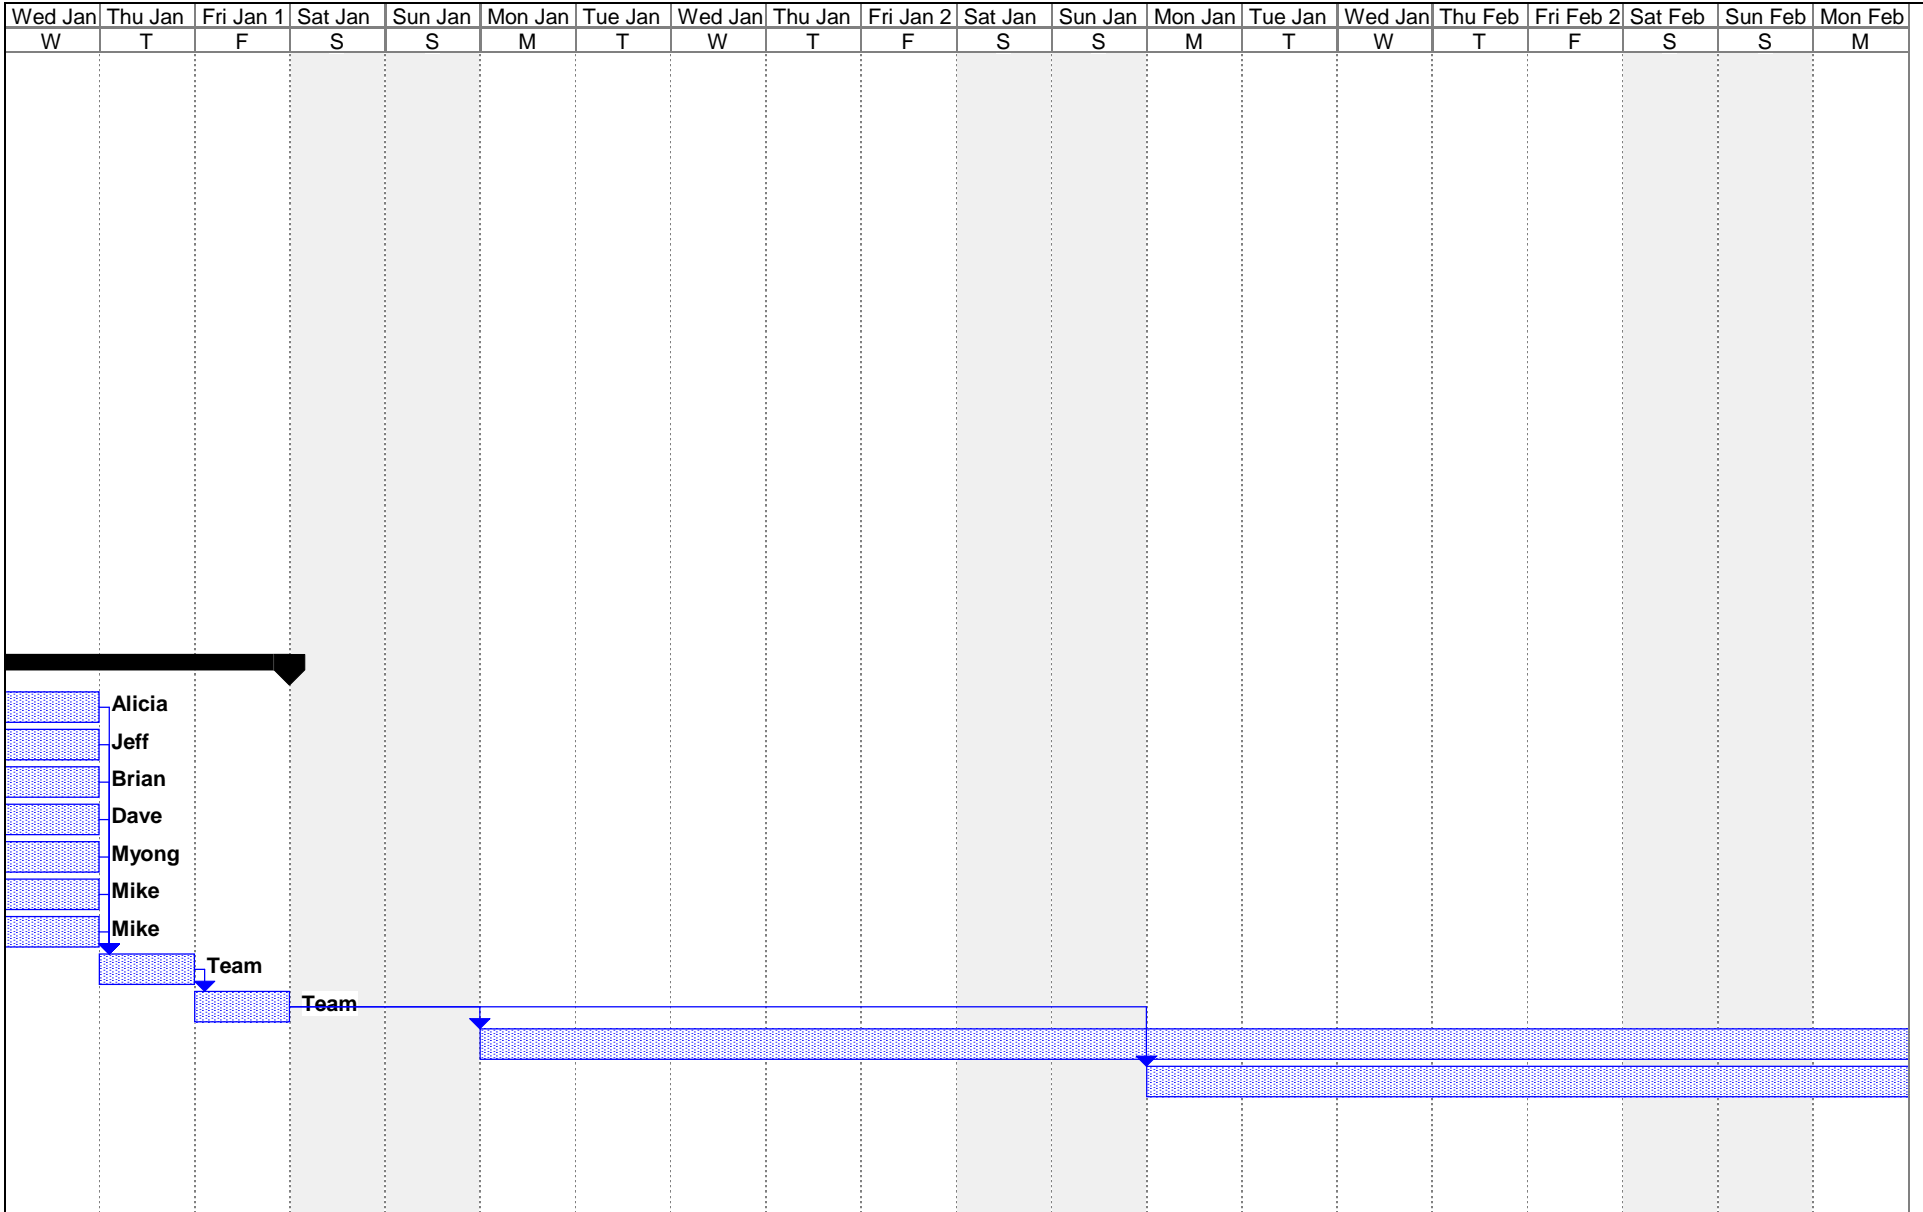





Project: 3 wk schedule Date: Fri 12/22/06	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 












Project: 3 wk schedule
Date: Fri 12/22/06

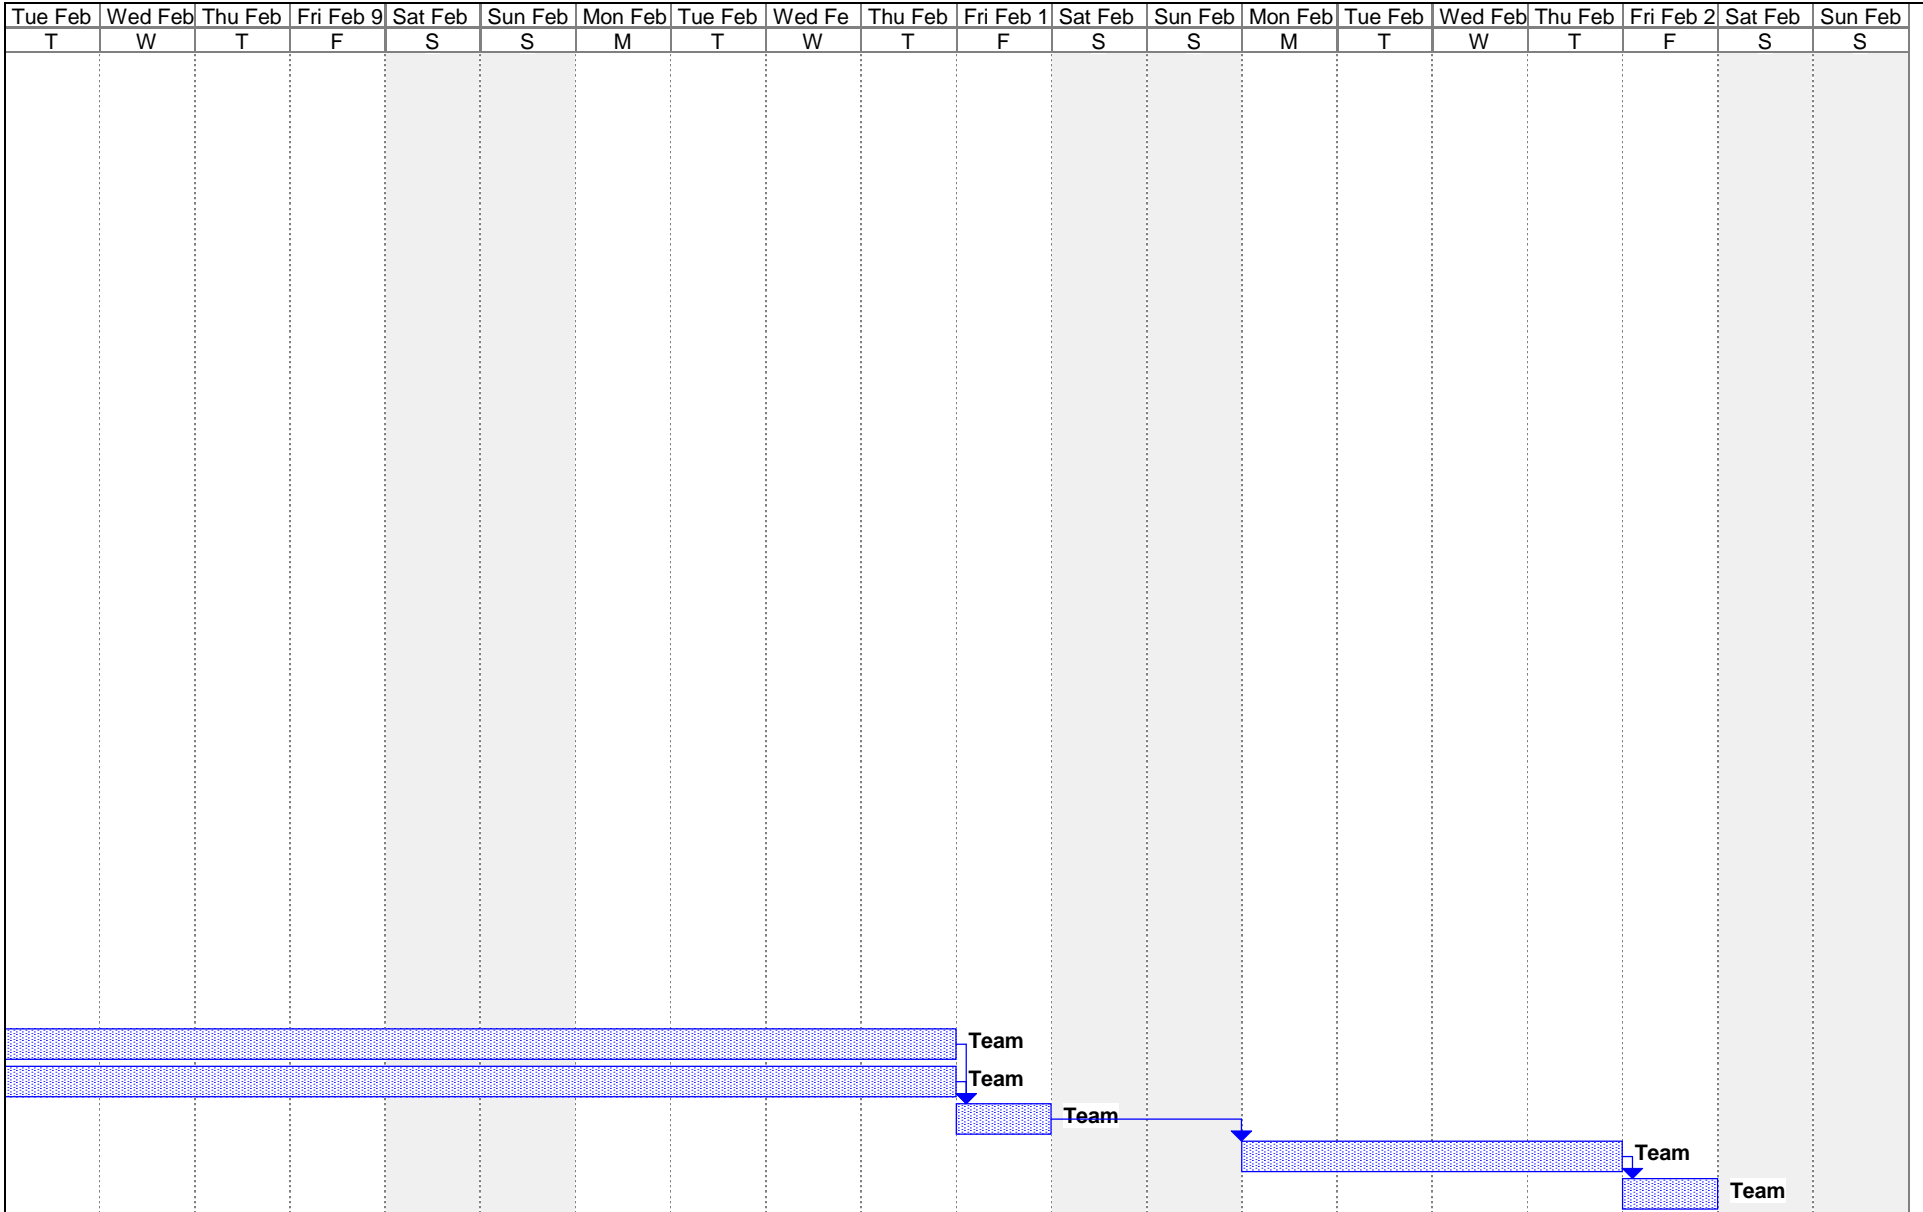Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Tue Feb	Wed Feb	Thu Feb	Fri Feb 9	Sat Feb	Sun Feb	Mon Feb	Tue Feb	Wed Fe	Thu Feb	Fri Feb 1	Sat Feb	Sun Feb	Mon Feb	Tue Feb	Wed Feb	Thu Feb	Fri Feb 2	Sat Feb	Sun Feb
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

Project: 3 wk schedule Date: Fri 12/22/06	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 



Project: 3 wk schedule Date: Fri 12/22/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
