


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Week 1							Week 2		
							Mar 9, '08							Mar 16, '08		
							S	M	T	W	T	F	S	S	M	
1	Week 1	5 days	Mon 3/10/08	Fri 3/14/08												
2	Mechanical Design overhaul	4 days	Mon 3/10/08	Thu 3/13/08		Drive,Steer,Yoke,Platf										
3	Respond to DDR Action Items	8 days	Mon 3/10/08	Wed 3/19/08												
4	Develop Final Test Plan	5 days	Mon 3/10/08	Fri 3/14/08												
5	Order Parts for Development MM	1 day	Fri 3/14/08	Fri 3/14/08	2											
6	Week 2	5 days	Mon 3/17/08	Fri 3/21/08	1											
7	Close Action Items	2 days	Thu 3/20/08	Fri 3/21/08	3											
8	Procedures for Assembly/Manufacturing Plan Done	5 days	Mon 3/17/08	Fri 3/21/08												
9	Machine Development MM	5 days	Mon 3/17/08	Fri 3/21/08	5	Drive,Steer,Yoke,Platf										
10	Build Test Stand and Platform	5 days	Mon 3/17/08	Fri 3/21/08	5,4	Platform										
11	Assemble Electronic Prototype	3 days	Mon 3/17/08	Wed 3/19/08	5	Electronics,Controls										
51	Begin Electronic Prototype Testing	2 days	Thu 3/20/08	Fri 3/21/08	11	Electronics,Controls										
12	Week 3	5 days	Mon 3/24/08	Fri 3/28/08	6											
14	Assemble Development MM & Platform	5 days?	Mon 3/24/08	Fri 3/28/08	9	Drive,Steer,Yoke,Platf										
15	Demonstrate Functioning Electronic Prototype	5 days?	Mon 3/24/08	Fri 3/28/08	51	Electronics,Controls										
52	Demonstrate Functioning GUI	5 days?	Mon 3/24/08	Fri 3/28/08	51	Controls										
16	Week 4	5 days	Mon 3/31/08	Fri 4/4/08	12											
18	Integrated Mechanical & Electrical Subsystems int	4 days?	Mon 3/31/08	Thu 4/3/08	14,15											
53	Address System Concerns in System Integration	1 day?	Fri 4/4/08	Fri 4/4/08	18											
19	Week 5	5 days	Mon 4/7/08	Fri 4/11/08	16											
21	Test Development Setup with GUI Control	1 day?	Mon 4/7/08	Mon 4/7/08	18											
17		5 days?	Mon 3/24/08	Fri 3/28/08	8											
54	Document Testing	1 day?	Mon 4/7/08	Mon 4/7/08	53											
23	Week 6	5 days	Mon 4/14/08	Fri 4/18/08	19											
25	Evaluate Performance of Development Setup	1 day?	Mon 4/14/08	Mon 4/14/08	21											
26	Revise Design for Final MMs	3 days?	Tue 4/15/08	Thu 4/17/08	25											
55	Order Parts for Final MMs	1 day?	Fri 4/18/08	Fri 4/18/08	26											
27	Week 7	5 days	Mon 4/21/08	Fri 4/25/08	23											
29	Machine Final MMs	10 days?	Mon 4/21/08	Fri 5/2/08	55	Drive,Steer,Yoke,Platf										
30	Verify & Validate Functionality of Controls & Electr	5 days?	Mon 4/21/08	Fri 4/25/08	25											
56	Prepare Technical Paper	9 days?	Mon 4/21/08	Thu 5/1/08												
32	Prepare for Functional & Performance Review	9 days?	Mon 4/21/08	Thu 5/1/08												




Project: MSD_II_Schedule.mpp Date: Tue 2/26/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Week 1							Week 2	
							Mar 9, '08							Mar 16, '08	
							S	M	T	W	T	F	S	S	M
31	Week 8	5 days	Mon 4/28/08	Fri 5/2/08	27										
34	75% Technical Paper due	1 day?	Fri 5/2/08	Fri 5/2/08	56										
47	"Writing Good Conference Papers" Workshop	1 day?	Fri 5/2/08	Fri 5/2/08											
36	Functional & Performance Review	1 day?	Fri 5/2/08	Fri 5/2/08	32										
37	Prepare Poster	9 days?	Mon 4/28/08	Thu 5/8/08											
35	Week 9	5 days	Mon 5/5/08	Fri 5/9/08	31										
48	Posters due	1 day?	Fri 5/9/08	Fri 5/9/08	37										
40	Build remaining MMs	5 days?	Mon 5/5/08	Fri 5/9/08	29										
41	Complete Technical Paper	1 day?	Fri 5/9/08	Fri 5/9/08	34										
42	Prepare for Presentation	9 days?	Mon 5/5/08	Thu 5/15/08											
39	Week 10	5 days	Mon 5/12/08	Fri 5/16/08	35										
43	Evaluate Completion of Design Documentation	2 days?	Mon 5/12/08	Tue 5/13/08											
44	Complete Detailed Documentation of Project	1 day?	Wed 5/14/08	Wed 5/14/08	43										
45	Objective Evaluation of Project Success and Failure	4 days?	Mon 5/12/08	Thu 5/15/08											
57	Prepare "RP1 Tutorial" Recommendations for Future	1 day?	Fri 5/16/08	Fri 5/16/08	45										
49	Project Presentation	1 day?	Fri 5/16/08	Fri 5/16/08	42										
50	Poster Session	1 day?	Fri 5/16/08	Fri 5/16/08	48										
46	Finals Week	4 days	Mon 5/19/08	Thu 5/22/08	39										
58	Organize Design History on EDGE	3 days?	Mon 5/19/08	Wed 5/21/08											

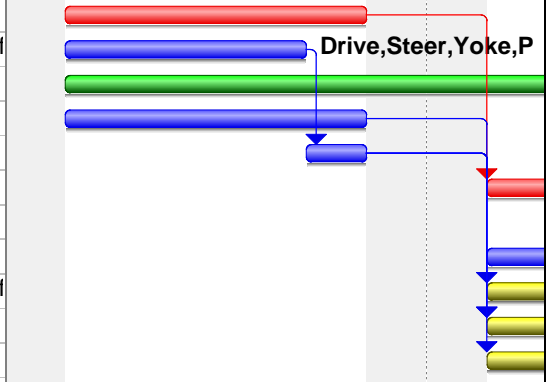



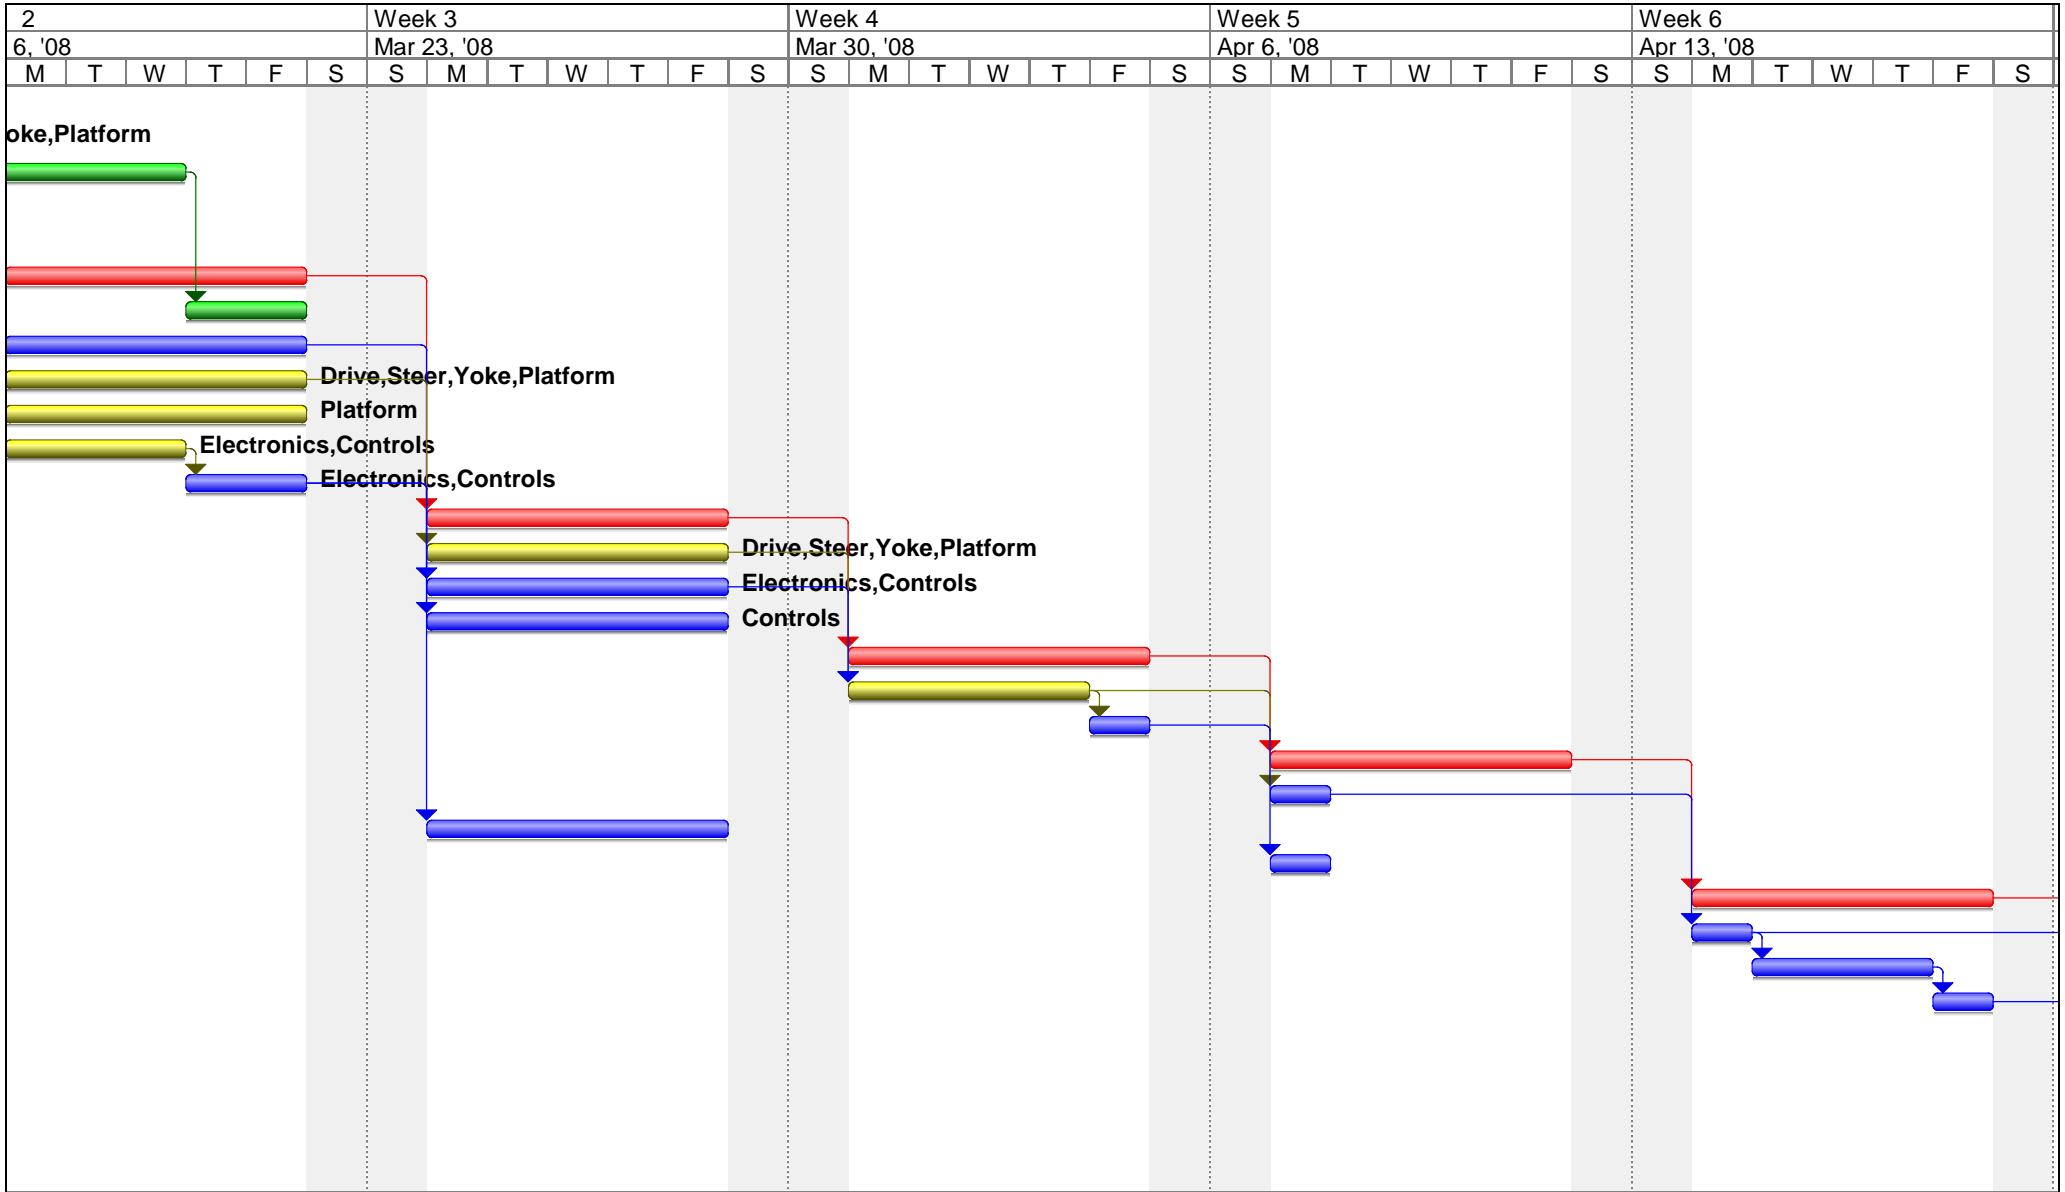




Project: MSD_II_Schedule.mpp
Date: Tue 2/26/08


Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Project: MSD_II_Schedule.mpp Date: Tue 2/26/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

2							Week 3							Week 4							Week 5							Week 6						
6, '08							Mar 23, '08							Mar 30, '08							Apr 6, '08							Apr 13, '08						
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	

Project: MSD_II_Schedule.mpp Date: Tue 2/26/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

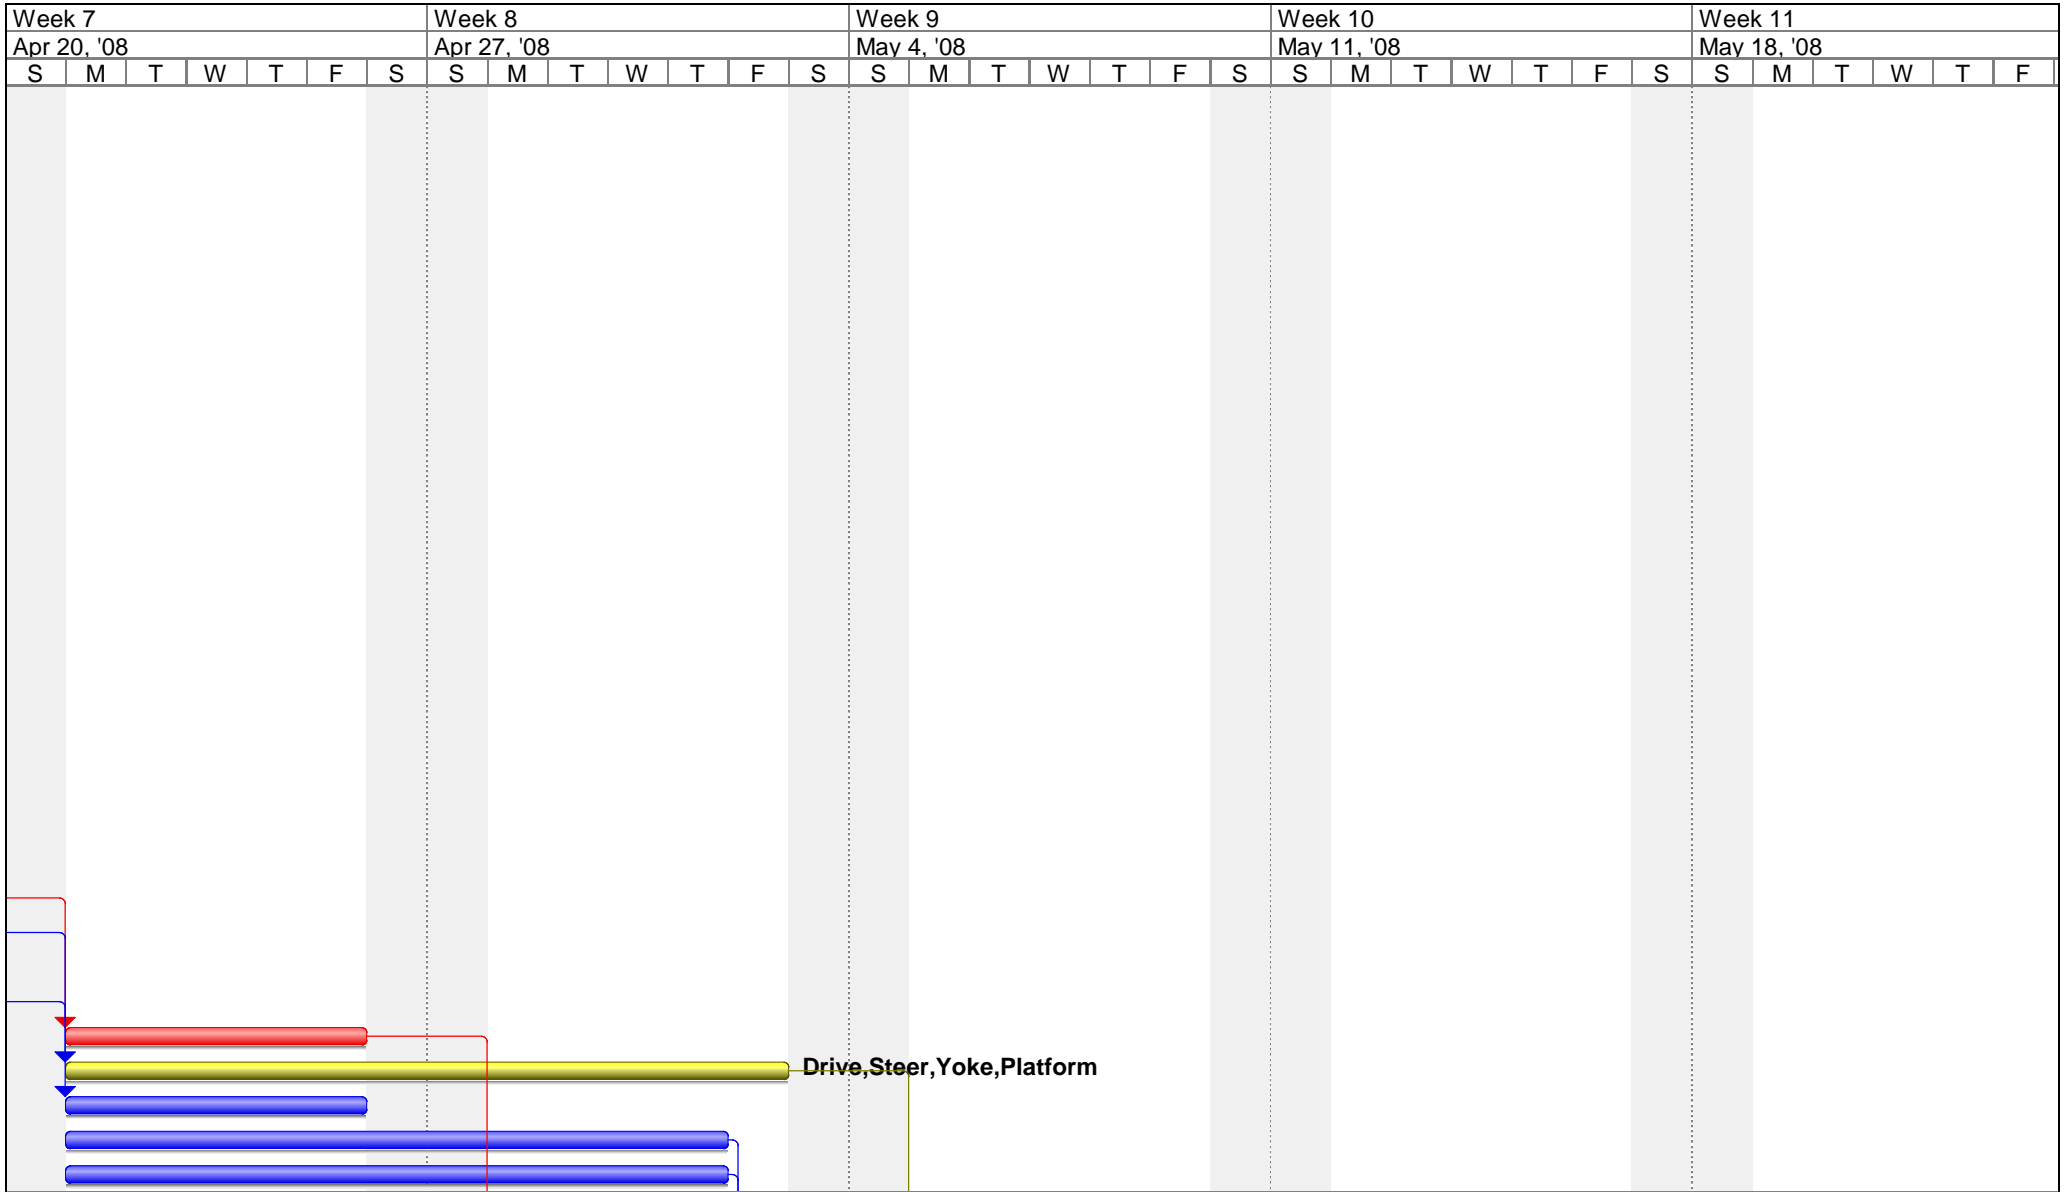

Project: MSD_II_Schedule.mpp Date: Tue 2/26/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

