


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 30, '08							Dec 7, '08			
							S	M	T	W	T	F	S	S	M	T	
1	Start of Winter Quarter	0 days	Mon 12/1/08	Mon 12/1/08													
2	<b>Week 1 (Get To know your customer and te</b>	<b>4 days</b>	<b>Mon 12/1/08</b>	<b>Thu 12/4/08</b>	<b>1</b>												
3	Course Logistics	1 hr	Mon 12/1/08	Mon 12/1/08		Team											
4	Meet with Customer(Bob Brinkman)	1 hr	Tue 12/2/08	Tue 12/2/08	3	Brad,Deborah,Michelle											
5	<b>Team Meeting (Project Background, as</b>	<b>0.09 days</b>	<b>Wed 12/3/08</b>	<b>Wed 12/3/08</b>													
6	Ice Breakers	10 mins	Wed 12/3/08	Wed 12/3/08		Team											
7	Project Background	20 mins	Wed 12/3/08	Wed 12/3/08		Team,Dr. Marshall											
8	Preliminary Needs Assessment	45 mins	Wed 12/3/08	Wed 12/3/08		Team											
9	Assign Deliverables	10 mins	Wed 12/3/08	Wed 12/3/08		Team											
10	Team Norms/Values	1.5 hrs	Wed 12/3/08	Wed 12/3/08	5	Team											
11	1 Page Project Summary	2 hrs	Thu 12/4/08	Thu 12/4/08	5	Alex,Michelle,Nick											
12	2 Quarter Schedue/Milestones	3.5 hrs	Thu 12/4/08	Thu 12/4/08	5	Deborah,Sean											
13	Investigate local wheelchair distributors	1 hr	Thu 12/4/08	Thu 12/4/08	5	Sean											
14	Project Intro Presentation	45 mins	Wed 12/3/08	Wed 12/3/08	5	Brad											
15	Friday Workshop	1 day	Fri 12/5/08	Fri 12/5/08		Team											
16	Contact Jack Allen to set-up Meeting	10 mins	Fri 12/5/08	Fri 12/5/08		Deborah											
17	Meet with Dr. Marshall(Status Update)	1 hr	Fri 12/5/08	Fri 12/5/08		Team											
18																	
19	<b>Week 2: Translating Needs to Specs</b>	<b>4.38 days</b>	<b>Mon 12/8/08</b>	<b>Fri 12/12/08</b>	<b>2</b>												
20	Benchmark Wheelchairs in Area	2 hrs	Mon 12/8/08	Mon 12/8/08		Team											
21	Meet Customer(J. Allen)	1 hr	Tue 12/9/08	Tue 12/9/08													
22	Team Meeting/Status Report	1 hr	Wed 12/10/08	Wed 12/10/08		Team,Dr. Marshall											
23	Needs Assessment (final)	0.33 hrs	Wed 12/10/08	Wed 12/10/08	8,20	Brad,Alex,Deborah											
24	Review Concept Generation Material	1 hr	Wed 12/10/08	Wed 12/10/08	23	Team											
25	Develop Specifications	1.5 hrs	Thu 12/11/08	Thu 12/11/08	24	Team											
26	1 Page Project Summary	20 mins	Wed 12/10/08	Wed 12/10/08	22	Brad											
27	Update 2 Quarter Schedule	30 mins	Thu 12/11/08	Thu 12/11/08	22	Deborah,Sean											
28	Benchmarking Report	1 hr	Thu 12/11/08	Thu 12/11/08	20	Michelle,Nick,Sean											
29	WBS &Team Roles (final)	20 mins	Fri 12/12/08	Fri 12/12/08	22	Brad											
30	<b>Friday Workshop</b>	<b>0.38 days</b>	<b>Fri 12/12/08</b>	<b>Fri 12/12/08</b>	<b>22</b>	<b>Team</b>											
31	Generate Concepts	3 hrs	Fri 12/12/08	Fri 12/12/08	22	Team											
32	Contact Physical Therapist to set-up	10 mins	Fri 12/12/08	Fri 12/12/08	22	Team											
33																	
34	Week 3 : Concept Generation and Developme	4.5 days	Mon 12/15/08	Fri 12/19/08	19												
35	Project Updates	20 mins	Mon 12/15/08	Mon 12/15/08		Team											
36	<b>Team Meeting</b>	<b>0.19 days</b>	<b>Mon 12/15/08</b>	<b>Mon 12/15/08</b>		<b>Team</b>											
37	Discuss Concepts	1.5 hrs	Mon 12/15/08	Mon 12/15/08		Team											
38	Invite the customer(conference call) about selk	1 hr	Mon 12/15/08	Mon 12/15/08		Brad											







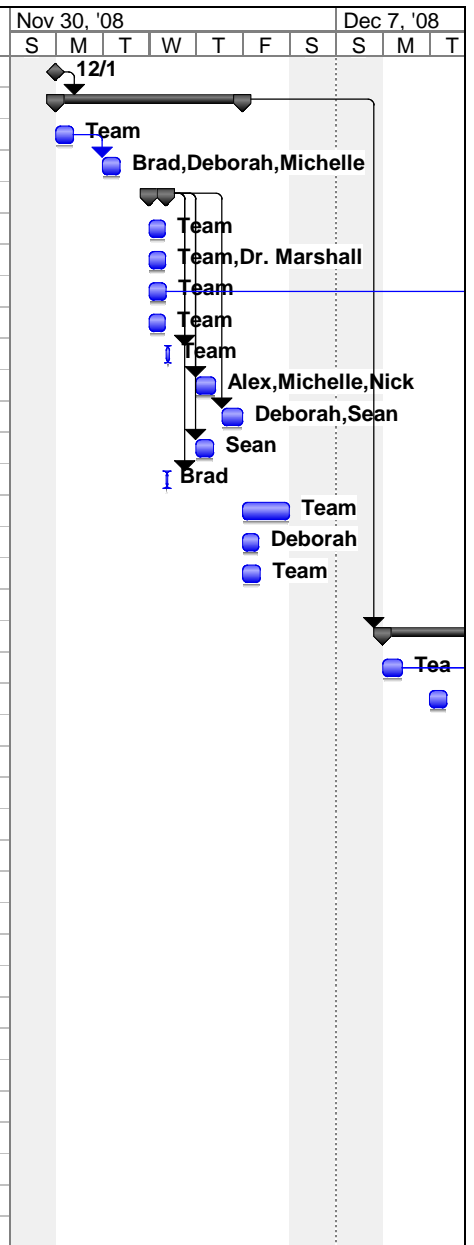




Project: MSD\_2quarter\_schedule  
Date: Thu 12/11/08

Task Milestone External Tasks










Split Summary External Milestone

Progress Project Summary Deadline










ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 30, '08							Dec 7, '08				
							S	M	T	W	T	F	S	S	M	T		
39	Final Specs	2 hrs	Wed 12/17/08	Wed 12/17/08		Team												
40	<b>Friday's Workshop</b>	<b>0.5 days</b>	<b>Fri 12/19/08</b>	<b>Fri 12/19/08</b>	<b>36</b>	<b>Team</b>												
41	Finalize Project Plan	3 hrs	Fri 12/19/08	Fri 12/19/08		Team												
42	Select Concept	2 hrs	Fri 12/19/08	Fri 12/19/08		Team												
43	Meet with Dr. Marshall	1 hr	Fri 12/19/08	Fri 12/19/08	41,42	Dr. Marshall												
44	Week 4: System Level Design	4.56 days	Mon 1/5/09	Fri 1/9/09	34													
45	Project Updates	30 mins	Mon 1/5/09	Mon 1/5/09														
46	Team Meeting	0.25 days	Mon 1/5/09	Mon 1/5/09	43	Team												
47	<b>Invite Faculty and Participants to Design Review</b>	<b>0.13 days</b>	<b>Mon 1/5/09</b>	<b>Mon 1/5/09</b>		<b>Brad</b>												
48	System Level Design	2 hrs	Mon 1/5/09	Mon 1/5/09														
49	Engineering Analysis	3 hrs	Tue 1/6/09	Tue 1/6/09		Alex,Michelle,Nick												
50																		
51	<b>Risk Analysis</b>	3 hrs	Wed 1/7/09	Wed 1/7/09		Brad,Deborah,Sean												
52	Contact Customer(Update)	30 mins	Fri 1/9/09	Fri 1/9/09		Brad												
53	Update 2 Quarter Schedule	1 hr	Wed 1/7/09	Wed 1/7/09		Sean,Deborah												
54	<b>Friday Workshop</b>	<b>0.5 days</b>	<b>Fri 1/9/09</b>	<b>Fri 1/9/09</b>	<b>49,51,52,53</b>	<b>Team</b>												
55	<b>Present System Level Design</b>	2.5 hrs	Fri 1/9/09	Fri 1/9/09														
56	Prepare for wk 5 Design Review	3 hrs	Fri 1/9/09	Fri 1/9/09														
57	Meet with Dr. Marshall(update)	1 hr	Fri 1/9/09	Fri 1/9/09	55,56	Team,Dr. Marshall												
58	Planning for Week 5	1.5 hrs	Fri 1/9/09	Fri 1/9/09		Team												
59	<b>Week 5: System Level Design Review</b>	<b>4.19 days</b>	<b>Mon 1/12/09</b>	<b>Fri 1/16/09</b>	<b>44</b>													
60	Revise, Compile and Distribute Agenda/Docs	2 hrs	Mon 1/12/09	Mon 1/12/09	58	Team												
61	Prepare and Plan for Design Review	2 hrs	Wed 1/14/09	Wed 1/14/09	58	Team												
62	Develop Plan for Next 3 Weeks	1.5 hrs	Thu 1/15/09	Thu 1/15/09	58	Team												
63	<b>Friday Workshop</b>	<b>0.19 days</b>	<b>Fri 1/16/09</b>	<b>Fri 1/16/09</b>	<b>60,61,62</b>													
64	<b>Design Review</b>	1 hr	Fri 1/16/09	Fri 1/16/09		Team												
65	Sit in on a design review	1 hr	Fri 1/16/09	Fri 1/16/09														
66	Compile Design Review	1 hr	Fri 1/16/09	Fri 1/16/09														
67	Meet with Dr. Marshall	30 mins	Fri 1/16/09	Fri 1/16/09	64,65,66	Team,Dr. Marshall												
68	<b>Week 6 and 7: System Level Design Contribution</b>	<b>4.25 days</b>	<b>Mon 1/26/09</b>	<b>Fri 1/30/09</b>	<b>59</b>													
69	Contact Customer(update)	30 mins	Mon 1/26/09	Mon 1/26/09	67	Brad												
70	<b>Team Meeting</b>	<b>0.06 days</b>	<b>Mon 1/26/09</b>	<b>Mon 1/26/09</b>	<b>67</b>	<b>Team</b>												
71	Project Updates	30 mins	Mon 1/26/09	Mon 1/26/09														
72	Delgate Deliverables	30 mins	Mon 1/26/09	Mon 1/26/09														
73	<b>BOM/Drawings and Schematics</b>	2 hrs	Tue 1/27/09	Tue 1/27/09		Nick,Michelle,Alex												
74	<b>Risk Assessment and Feasibility</b>	2 hrs	Wed 1/28/09	Wed 1/28/09		Sean,Deborah,Brad												
75	<b>Friday Workshop</b>	<b>0.25 days</b>	<b>Fri 1/30/09</b>	<b>Fri 1/30/09</b>	<b>71,72,73,74</b>													
76	Review Detailed Design Progress Report	2 hrs	Fri 1/30/09	Fri 1/30/09		Team,Dr. Marshall												

Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	










ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 30, '08							Dec 7, '08				
							S	M	T	W	T	F	S	S	M	T		
77	Team Review	1 hr	Fri 1/30/09	Fri 1/30/09		Team												
78	<b>Week 8: Detail Design</b>	<b>4.31 days</b>	<b>Mon 2/2/09</b>	<b>Fri 2/6/09</b>	<b>68</b>													
79	Contact Customer(update)	30 mins	Mon 2/2/09	Mon 2/2/09	77	Brad												
80	Invite Faculty/ Participants to Detailed De	30 mins	Mon 2/2/09	Mon 2/2/09	77	Team												
81	<b>Team Meeting</b>	<b>0.13 days</b>	<b>Mon 2/2/09</b>	<b>Mon 2/2/09</b>	<b>77</b>	<b>Team</b>												
82	Project Updates	30 mins	Mon 2/2/09	Mon 2/2/09														
83	Discuss Gaps	1 hr	Mon 2/2/09	Mon 2/2/09														
84	Finalize Data Package	2 hrs	Wed 2/4/09	Wed 2/4/09		Team												
85	<b>Friday's Workshop</b>	<b>0.31 days</b>	<b>Fri 2/6/09</b>	<b>Fri 2/6/09</b>		<b>Team</b>												
86	Present Readiness for Detailed Desi	2 hrs	Fri 2/6/09	Fri 2/6/09	82,83,84													
87	Update Docs for Week 9 Design Rev	1 hr	Fri 2/6/09	Fri 2/6/09														
88	Meet with Dr. Marshall	30 mins	Fri 2/6/09	Fri 2/6/09	86,87	Team,Dr. Marshall												
89	<b>Week 9: Detailed Design Review</b>	<b>4.19 days</b>	<b>Mon 2/9/09</b>	<b>Fri 2/13/09</b>	<b>78</b>													
90	Revise, Compile and Distribute Agenda/C	2 hrs	Mon 2/9/09	Mon 2/9/09	88	Team												
91	<b>Prepare and Plan for Design Review</b>	<b>0.25 days</b>	<b>Wed 2/11/09</b>	<b>Wed 2/11/09</b>	<b>88</b>													
92	Project Updates	30 mins	Mon 2/9/09	Mon 2/9/09														
93	<b>Team Meeting</b>	<b>0.13 days</b>	<b>Mon 2/9/09</b>	<b>Mon 2/9/09</b>	<b>88</b>	<b>Team</b>												
94																		
95	<b>Design Review</b>	1 hr	Fri 2/13/09	Fri 2/13/09		Team												
96	<b>Friday Workshop</b>	<b>0.19 days</b>	<b>Fri 2/13/09</b>	<b>Fri 2/13/09</b>	<b>90,91,102,92,101</b>	<b>Team</b>												
97	Sit in on a design review	1 hr	Fri 2/13/09	Fri 2/13/09														
98	Compile Design Review	1 hr	Fri 2/13/09	Fri 2/13/09														
99																		
100	Meet with Dr. Marshall	30 mins	Fri 2/13/09	Fri 2/13/09	95	Team,Dr. Marshall												
101	Discuss Gaps	1 hr	Mon 2/9/09	Mon 2/9/09														
102	Schedule Time/Location for Design Revi	30 mins	Mon 2/9/09	Mon 2/9/09	88													
103	<b>Week 10: Mid-Project Review</b>	<b>4.13 days</b>	<b>Mon 2/16/09</b>	<b>Fri 2/20/09</b>	<b>89</b>													
104	Prepare for Project Review	2.5 hrs	Mon 2/16/09	Mon 2/16/09	100	Team												
105	<b>Friday Workshop</b>	<b>0.13 days</b>	<b>Fri 2/20/09</b>	<b>Fri 2/20/09</b>	<b>104,108,109</b>	<b>Team</b>												
106	Sit In On Project Review	1 hr	Fri 2/20/09	Fri 2/20/09														
107	<b>Project Review</b>	1 hr	Fri 2/20/09	Fri 2/20/09														
108	Develop Preliminary Schedule for MSD II	1.5 hrs	Wed 2/18/09	Wed 2/18/09	100	Team												
109	Develop Preliminary Test Plan for Design	1 hr	Wed 2/18/09	Wed 2/18/09	100	Team												
110	<b>Week 11: Documentation</b>	<b>4.13 days</b>	<b>Mon 2/23/09</b>	<b>Fri 2/27/09</b>	<b>103</b>													
111	Update Preliminary test plan	1 hr	Mon 2/23/09	Mon 2/23/09		Team												
112	Update Schedule for MSD II	1 hr	Tue 2/24/09	Tue 2/24/09		Team												
113	Finalize and Upload all documentation	45 mins	Wed 2/25/09	Wed 2/25/09		Team												
114	<b>Start of Spring Quarter</b>	<b>0 days</b>	<b>Mon 3/9/09</b>	<b>Mon 3/9/09</b>														


Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 30, '08							Dec 7, '08				
							S	M	T	W	T	F	S	S	M	T		
115	Close out MSD I A.I's	1 hr	Mon 3/9/09	Mon 3/9/09		Team												
116	Resolve remaining design issues	1.5 hrs	Tue 3/10/09	Tue 3/10/09		Team												
117	<b>Week 1: Closure on MSD I/Construction</b>	<b>4.13 days</b>	<b>Mon 3/9/09</b>	<b>Fri 3/13/09</b>	114													
118	Construction	3 hrs	Wed 3/11/09	Wed 3/11/09		Team												
119	<b>Week 2: Closure on MSD I/Construction</b>	<b>0.38 days</b>	<b>Fri 3/13/09</b>	<b>Fri 3/13/09</b>	117													
120	Close out MSD I A.I's	1 hr	Fri 3/13/09	Fri 3/13/09		Team												
121	Resolve remaining design issues	1.5 hrs	Fri 3/13/09	Fri 3/13/09		Team												
122	Construction	3 hrs	Fri 3/13/09	Fri 3/13/09		Team												
123	Meet with Dr. Marshall	1 hr	Fri 3/13/09	Fri 3/13/09	115,116,118	Team,Dr. Marshall												
124	<b>Week 3: Final Test Plan, Assembly/Manufac</b>	<b>22.13 days</b>	<b>Wed 2/18/09</b>	<b>Fri 3/20/09</b>														
125	Construction	3 hrs	Mon 3/16/09	Mon 3/16/09		Team												
126	Finalize Test & Assembly Plans	2.5 hrs	Wed 2/18/09	Wed 2/18/09		Team												
127	Meet with Dr. Marshall	1 hr	Fri 3/20/09	Fri 3/20/09	125,126	Team,Dr. Marshall												
128	<b>Week 4: Final Test Plan, Assembly/Manufac</b>	<b>3.13 days</b>	<b>Tue 3/24/09</b>	<b>Fri 3/27/09</b>	124													
129	Construction	3 hrs	Tue 3/24/09	Tue 3/24/09		Team												
130	Finalize Test & Assembly Plans	2.5 hrs	Wed 3/25/09	Wed 3/25/09		Team												
131	Meet with Dr. Marshall	1 hr	Fri 3/27/09	Fri 3/27/09	129,130	Team,Dr. Marshall												
132	Meet with Marshall( update)	1 hr	Fri 2/27/09	Fri 2/27/09	111,112,113	Team,Dr. Marshall												
133	Meet with Dr. Marshall	1 hr	Fri 3/13/09	Fri 3/13/09	115,116,118	Team,Dr. Marshall												
134	<b>Week 5: Construction/ Testing/D-Bug</b>	<b>4.13 days</b>	<b>Mon 3/30/09</b>	<b>Fri 4/3/09</b>	128	<b>Team</b>												
135	Final Construction	3 hrs	Mon 3/30/09	Mon 3/30/09		Team												
136	Testing/De-Bug	3 hrs	Tue 3/31/09	Tue 3/31/09		Team												
137	Meet with Dr. Marshall	1 hr	Fri 4/3/09	Fri 4/3/09	135,136	Team,Dr. Marshall												
138	<b>Week 6: Testing/De-Bug</b>	<b>3.13 days</b>	<b>Tue 4/7/09</b>	<b>Fri 4/10/09</b>	134	<b>Team</b>												
139	Testing/ De-Bug	3 hrs	Tue 4/7/09	Tue 4/7/09		Team												
140	Funtionality and Robustness	2.5 hrs	Thu 4/9/09	Thu 4/9/09		Team												
141	Meet with Dr. Marshall	1 hr	Fri 4/10/09	Fri 4/10/09	139,140	Team,Dr. Marshall												
142	<b>Week 7: Finalize Testing</b>	<b>4.13 days</b>	<b>Mon 4/13/09</b>	<b>Fri 4/17/09</b>	138	<b>Team</b>												
143	Finalize Testing/De-Bug	3.5 hrs	Mon 4/13/09	Mon 4/13/09		Team												
144	Finalize Funtionality and Robustness	3.5 hrs	Wed 4/15/09	Wed 4/15/09		Team												
145	Prepare for Funtion Performance Review	2 hrs	Wed 4/15/09	Wed 4/15/09		Team												
146	Meet with Dr. Marshall	1 hr	Fri 4/17/09	Fri 4/17/09	143,144,145	Team,Dr. Marshall												
147	<b>Week 8: Prepare for Final Project Review</b>	<b>4.13 days</b>	<b>Mon 4/20/09</b>	<b>Fri 4/24/09</b>	142	<b>Team</b>												
148	Poster	2.5 hrs	Mon 4/20/09	Mon 4/20/09		Team												
149	Technical Paper	5 hrs	Wed 4/22/09	Wed 4/22/09		Team												
150	Documentation	3 hrs	Thu 4/23/09	Thu 4/23/09		Team												
151	Meet with Dr. Marshall	1 hr	Fri 4/24/09	Fri 4/24/09	148,149,150	Team,Dr. Marshall												
152	<b>Week 9: Prepare for Final Project Review c</b>	<b>4.63 days</b>	<b>Mon 4/27/09</b>	<b>Fri 5/1/09</b>	147	<b>Team</b>												

Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 30, '08							Dec 7, '08			
							S	M	T	W	T	F	S	S	M	T	
153	Poster	1 hr	Mon 4/27/09	Mon 4/27/09		Team											
154	Technical Paper	4 hrs	Tue 4/28/09	Tue 4/28/09		Team											
155	Documentation	2 hrs	Wed 4/29/09	Wed 4/29/09		Team											
156	Meet with Dr. Marshall	1 hr	Fri 5/1/09	Fri 5/1/09	165	Team,Dr. Marshall											
157	Project Review	2 hrs	Fri 5/1/09	Fri 5/1/09	153,154,155	Team											
158	Technical Paper	4 hrs	Mon 5/4/09	Mon 5/4/09		Team											
159	Documentation	1.5 hrs	Tue 5/5/09	Tue 5/5/09		Team											
160	Project Review	2 hrs	Fri 5/8/09	Fri 5/8/09		Team											
161	Prepare for Field Demo.	2 hrs	Wed 5/6/09	Wed 5/6/09		Team											
162	Meet with Dr. Marshall	1 hr	Fri 5/8/09	Fri 5/8/09	158,159,160,161	Team,Dr. Marshall											
163	Week 11: Field Demo, Finalize Documentat	4.13 days	Mon 5/11/09	Fri 5/15/09	164	Team											
164	<b>Week 10: Prepare for Final Project Review</b>	<b>4.38 days</b>	<b>Mon 5/4/09</b>	<b>Fri 5/8/09</b>	<b>152</b>	<b>Team</b>											
165	Function Performance Review	2 hrs	Fri 5/1/09	Fri 5/1/09	157	Team											
166	Field Demo	1 hr	Mon 5/11/09	Mon 5/11/09		Team											
167	Finalize Documentation	2.5 hrs	Tue 5/12/09	Tue 5/12/09		Team											
168	Close out with Dr. Marshall	1 hr	Fri 5/15/09	Fri 5/15/09	166,167	Team,Dr. Marshall											

Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

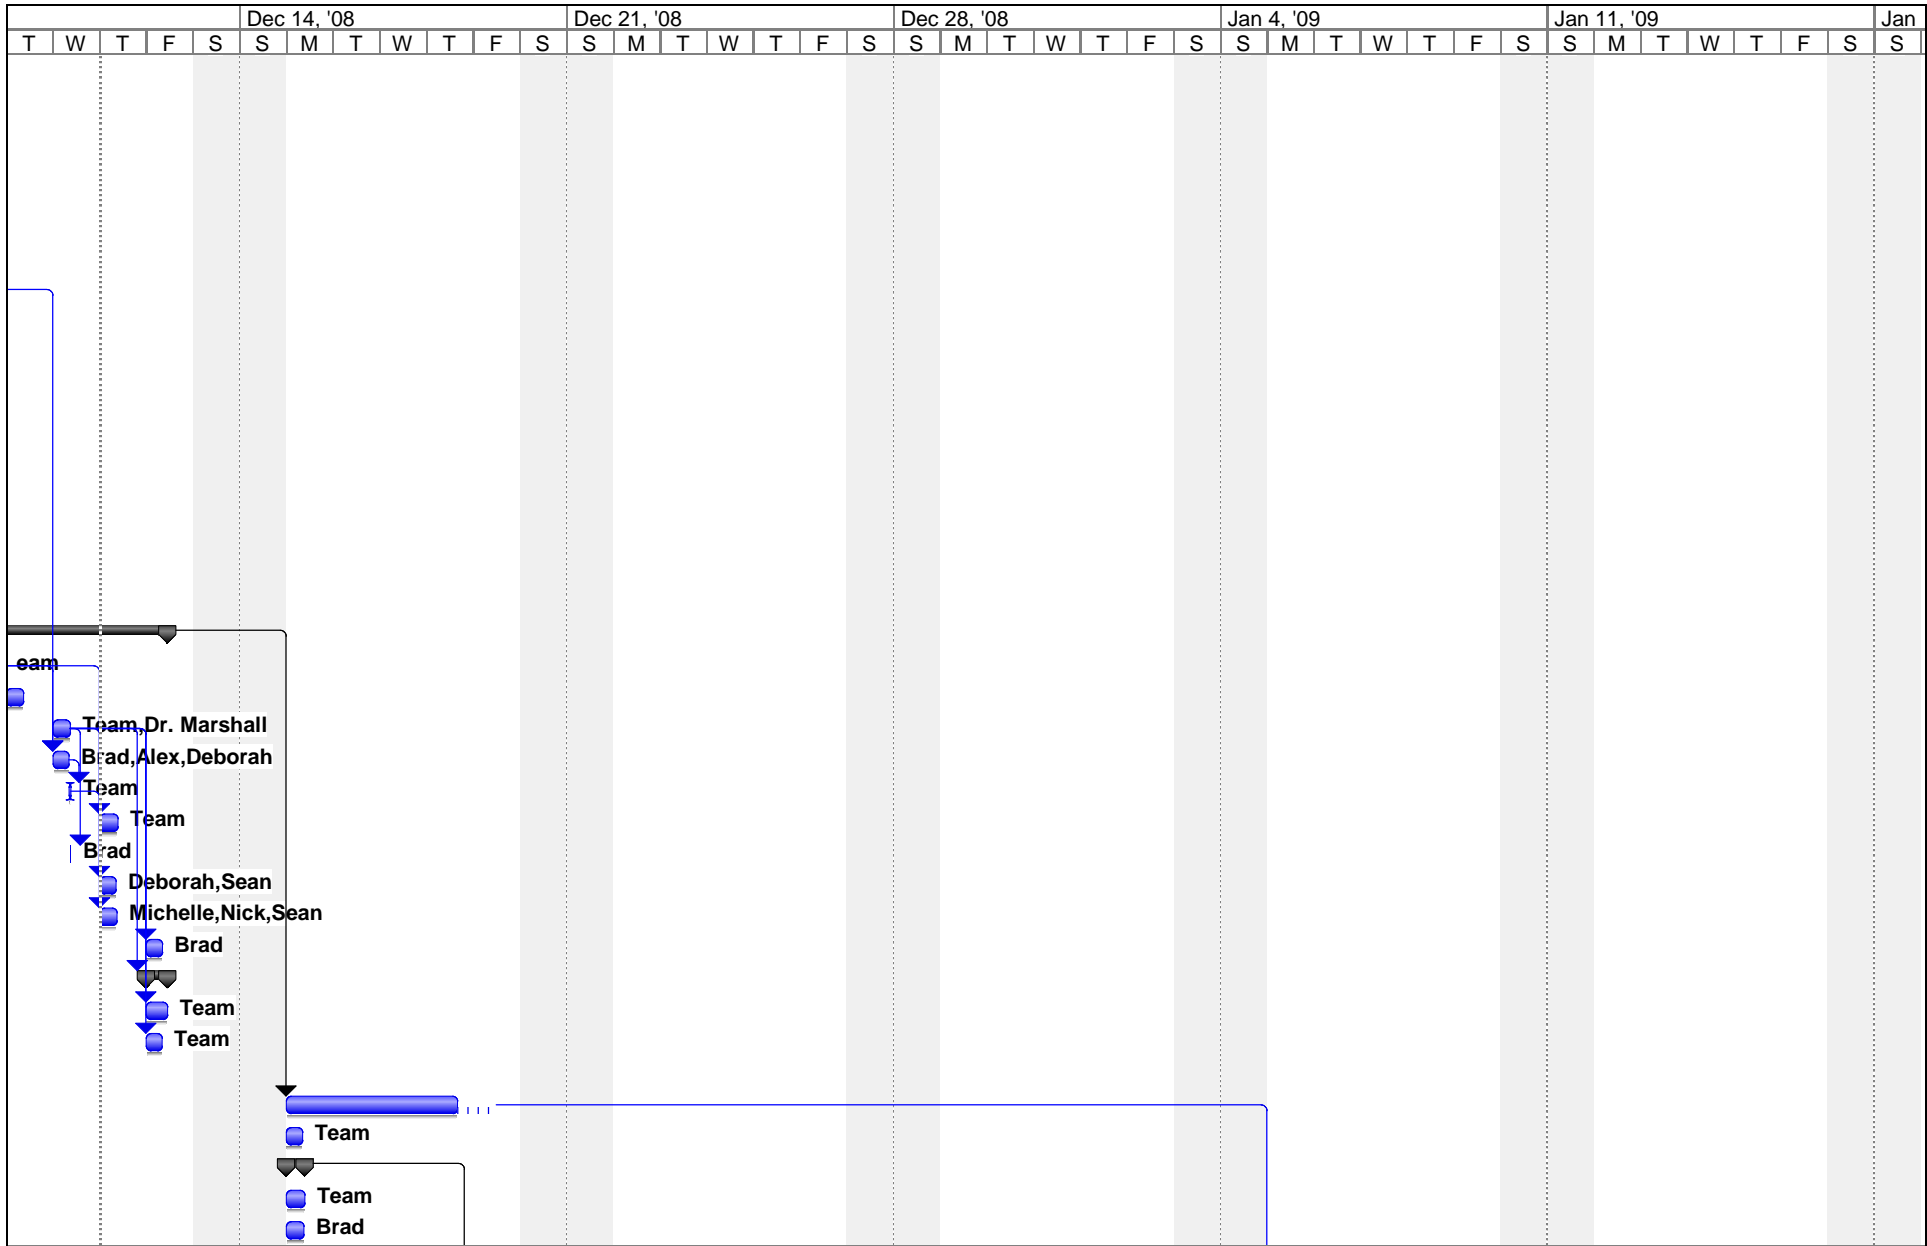

Project: MSD\_2quarter\_schedule  
 Date: Thu 12/11/08



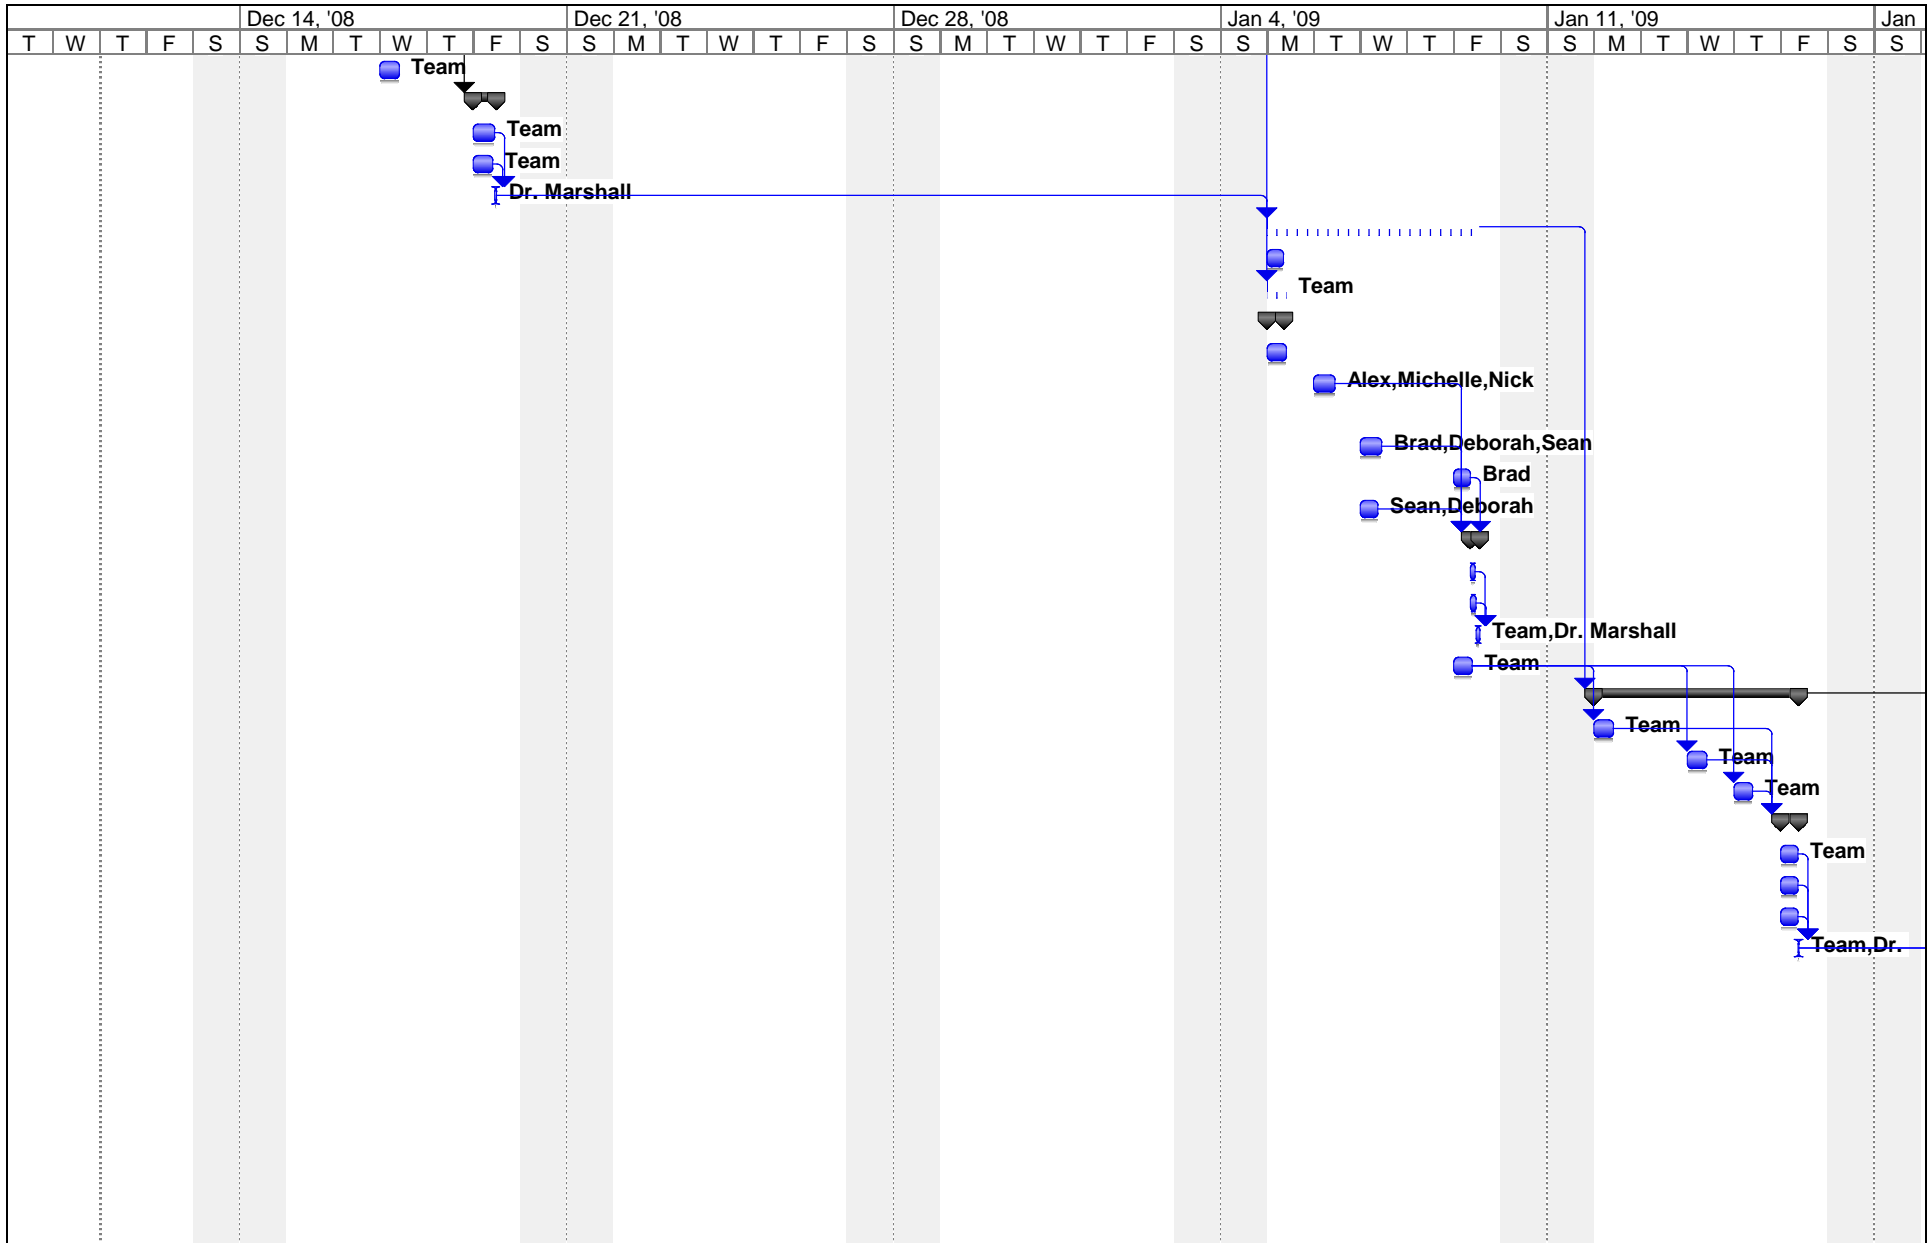






Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	




Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	









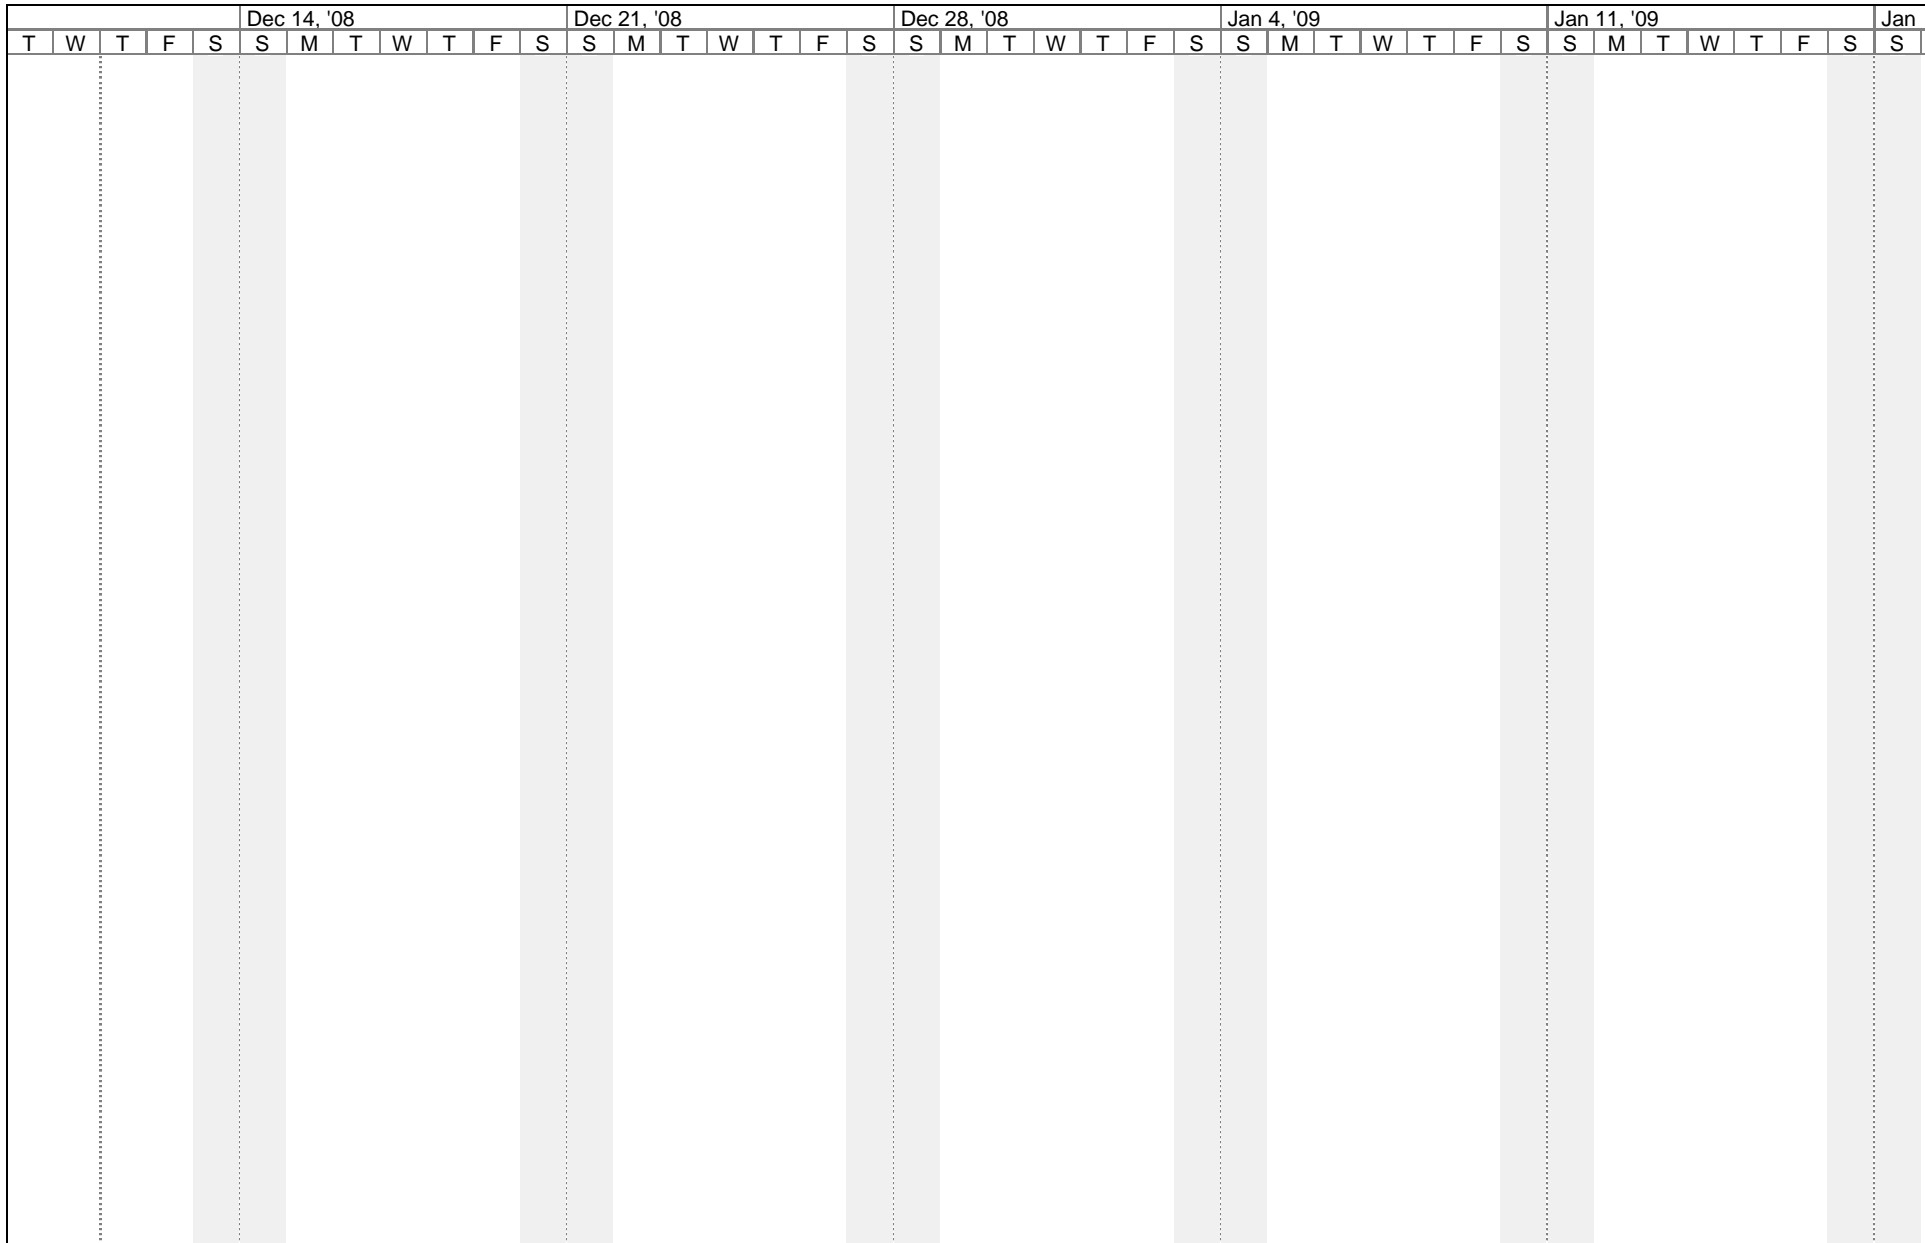


Project: MSD\_2quarter\_schedule  
 Date: Thu 12/11/08

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	














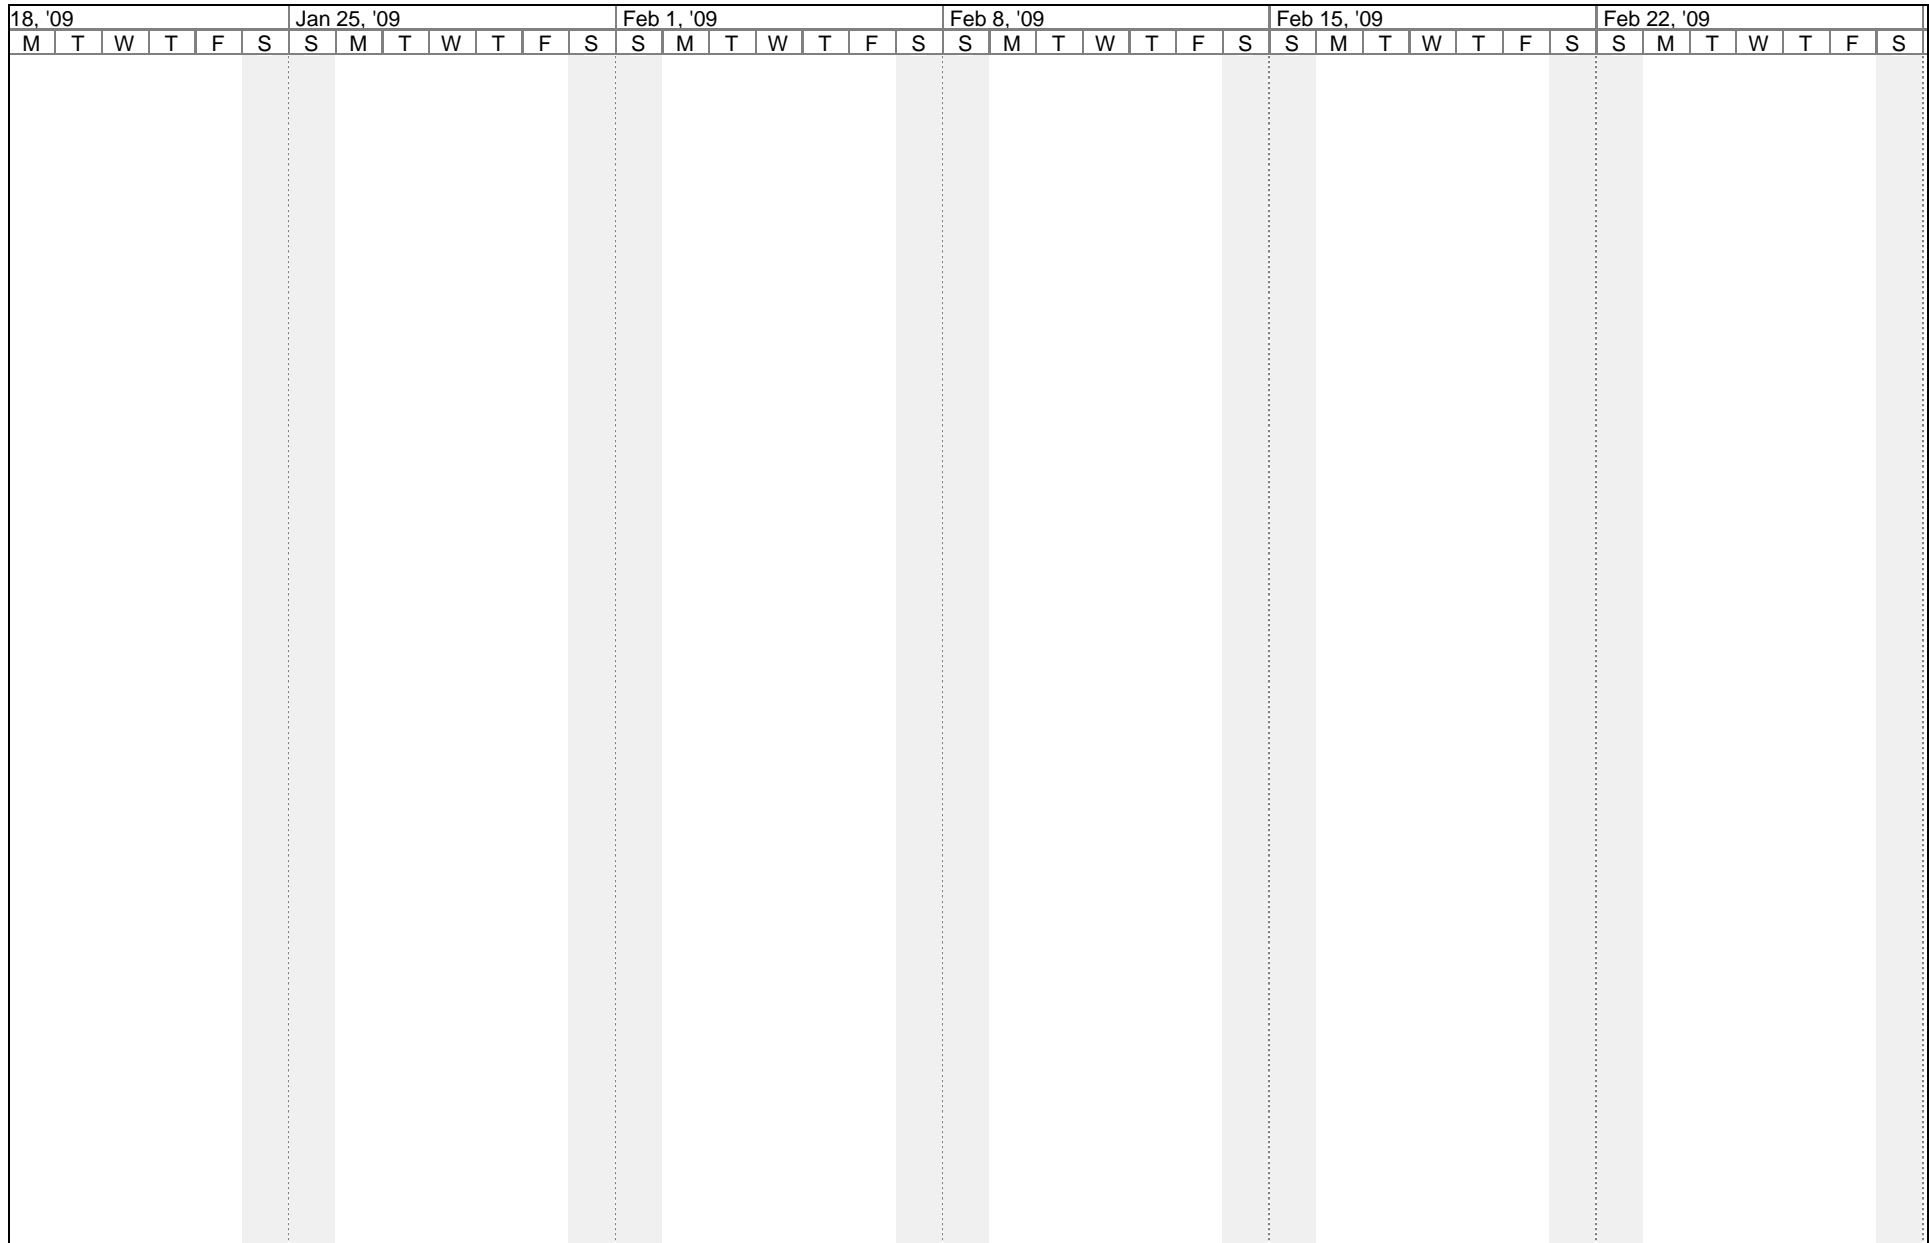
Project: MSD\_2quarter\_schedule  
Date: Thu 12/11/08










Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


					Dec 14, '08					Dec 21, '08					Dec 28, '08					Jan 4, '09					Jan 11, '09					Jan											
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	




Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 




Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

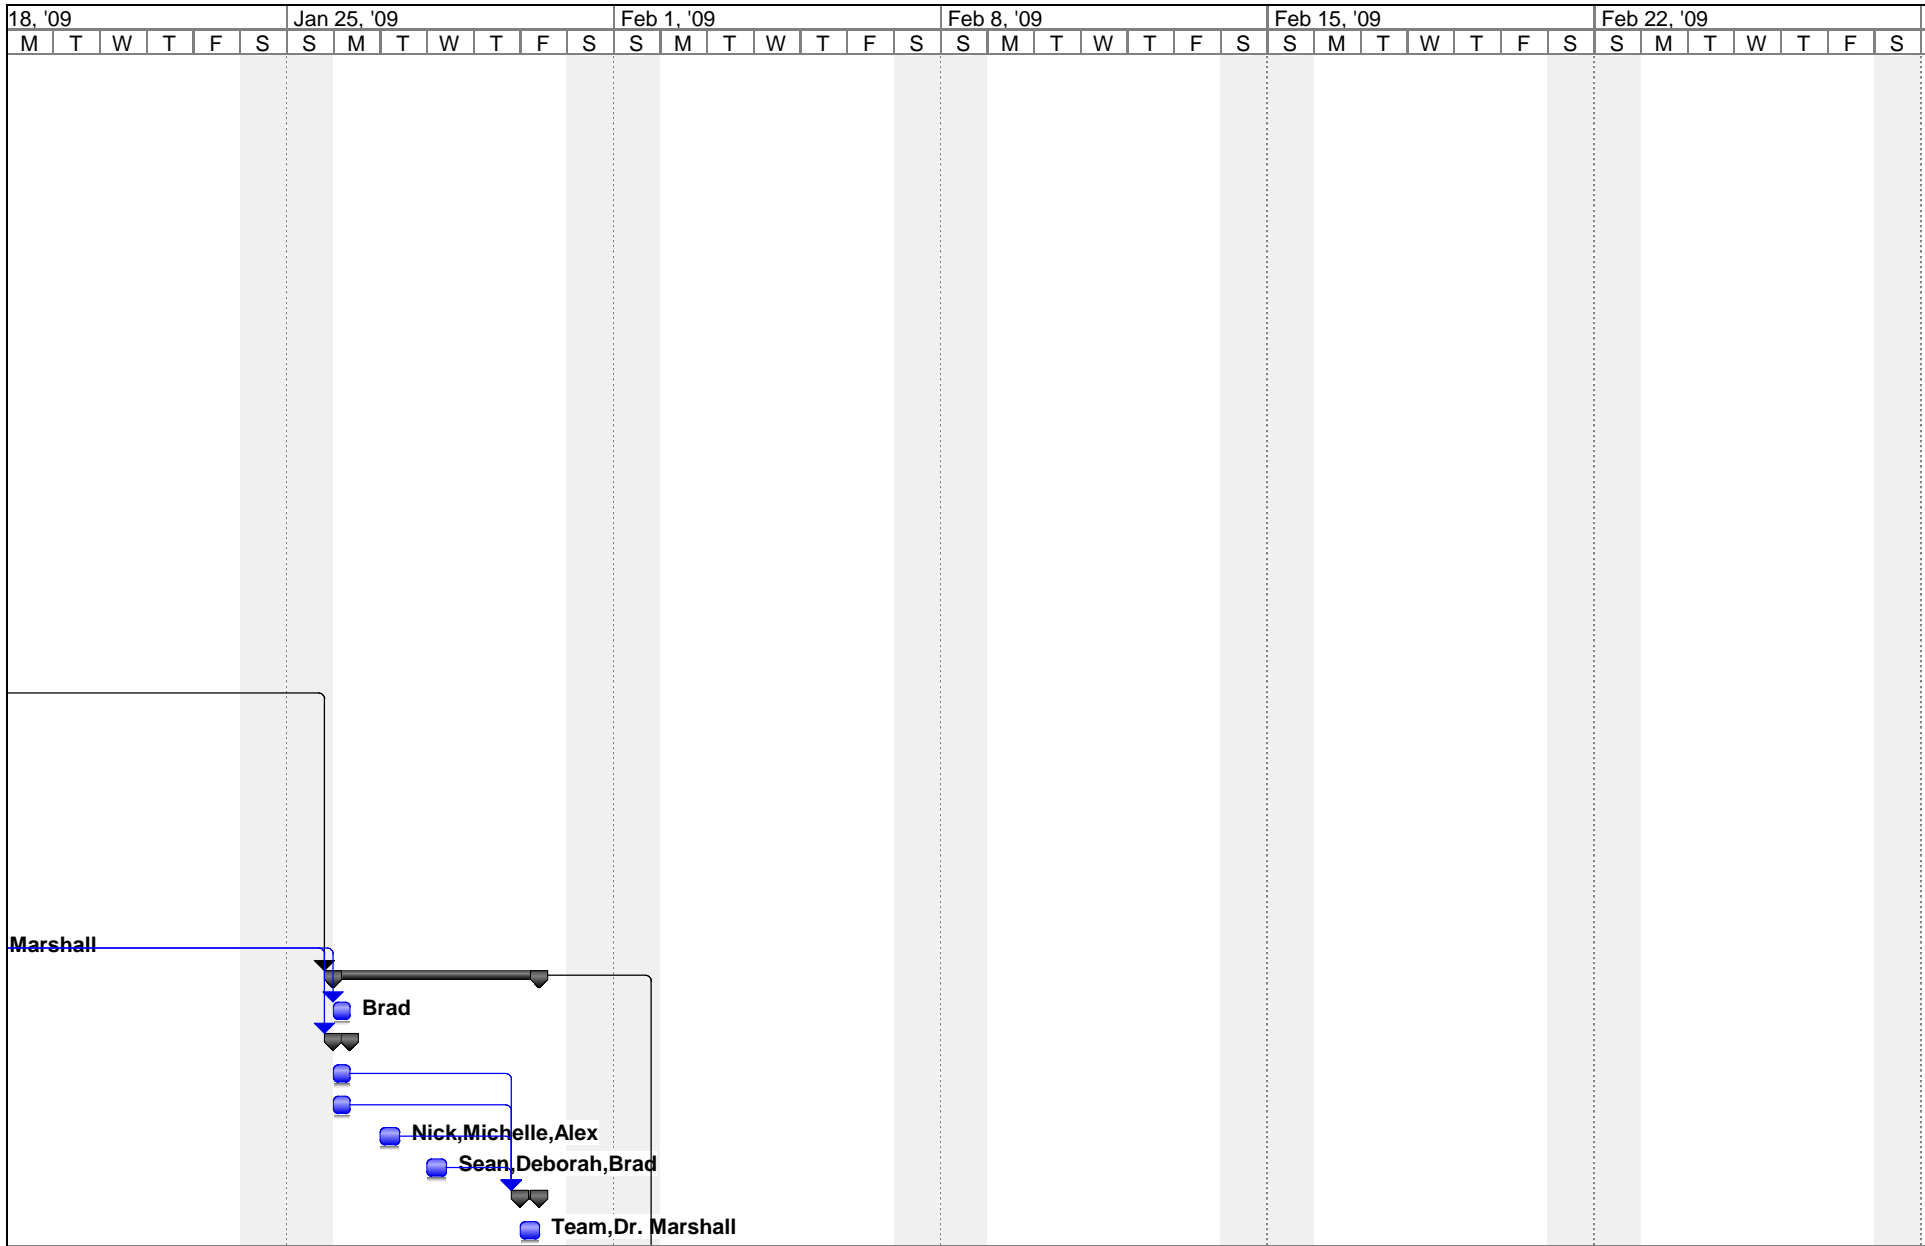

Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

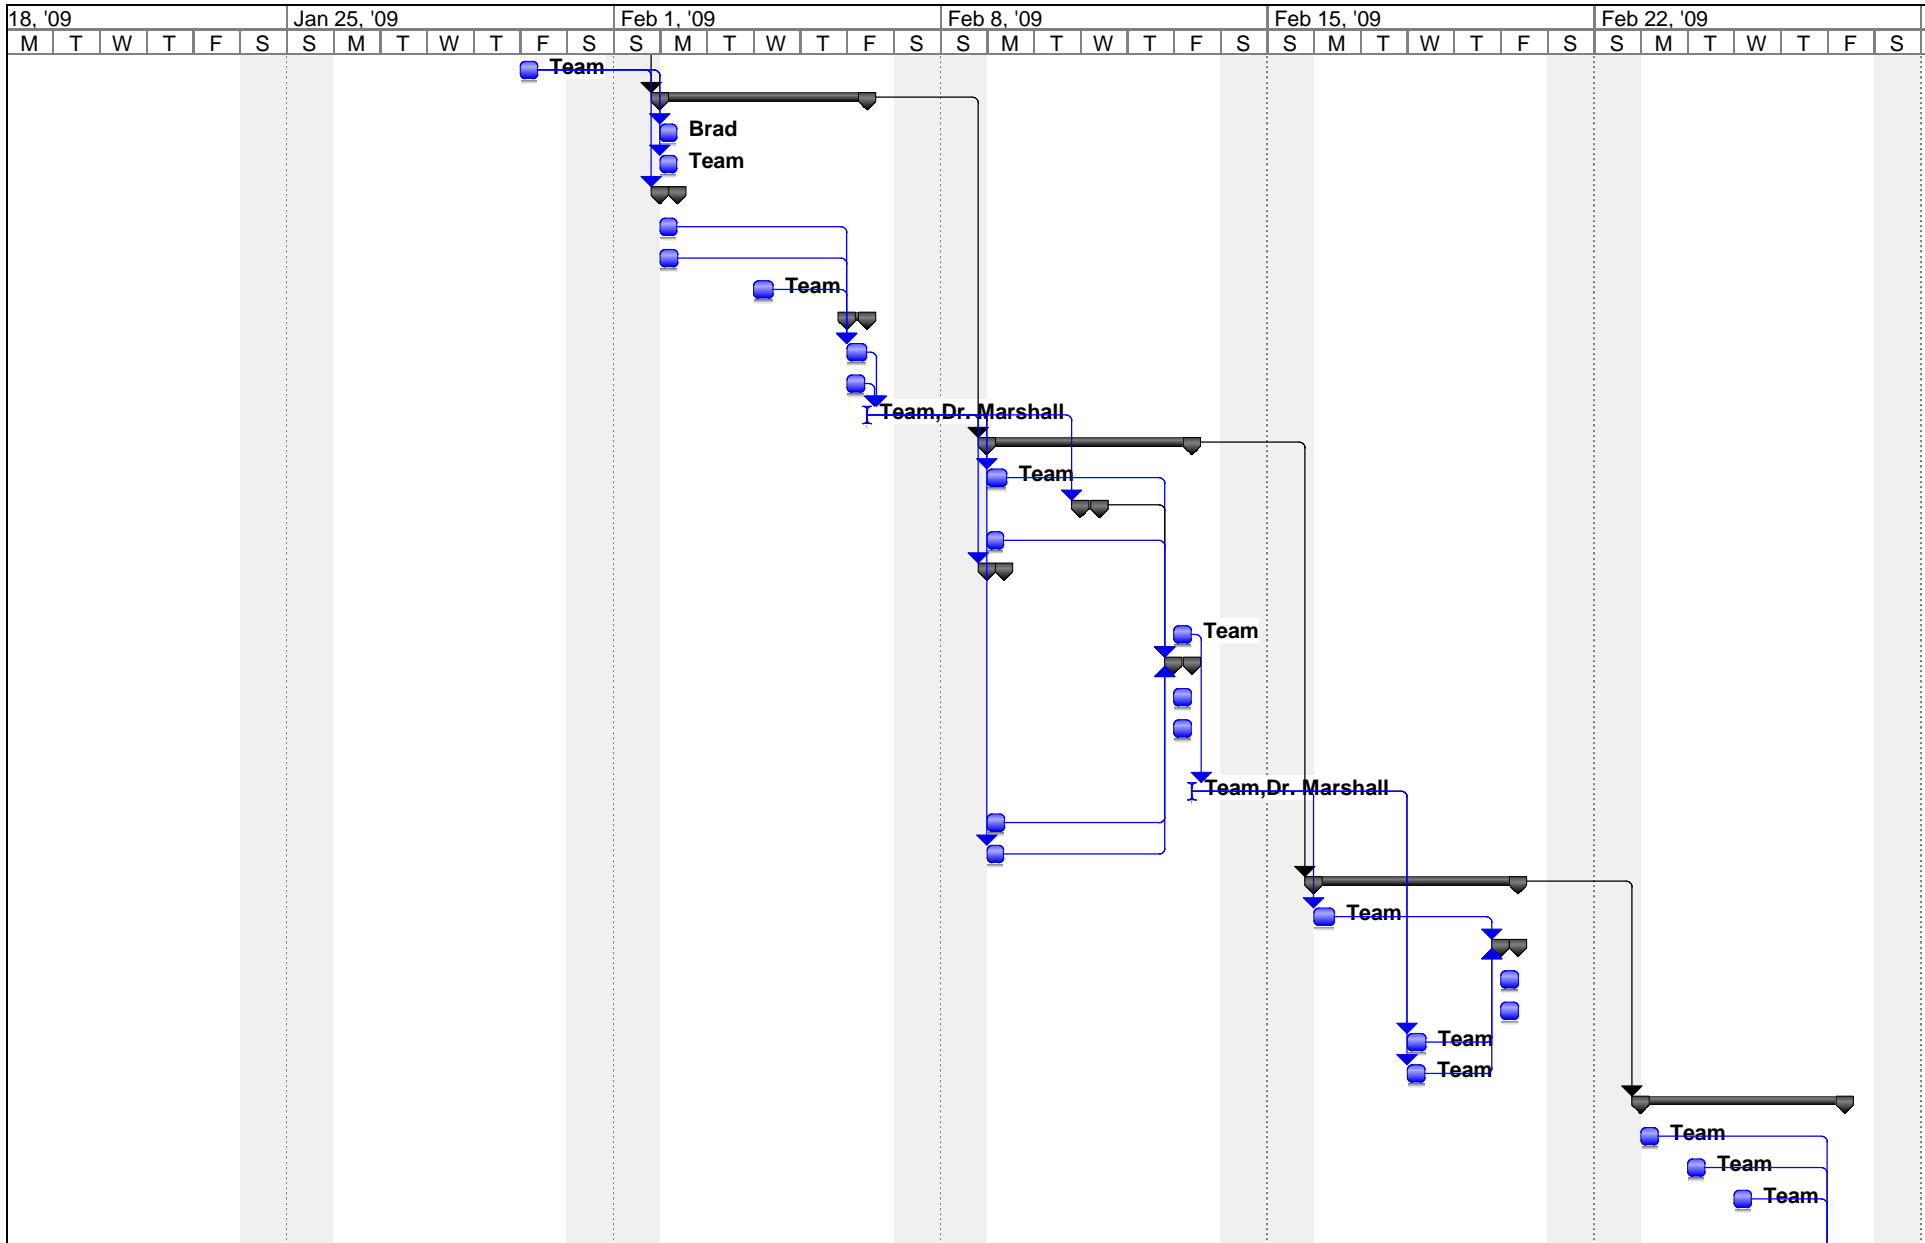

Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	












Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

18, '09							Jan 25, '09							Feb 1, '09							Feb 8, '09							Feb 15, '09							Feb 22, '09						
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	










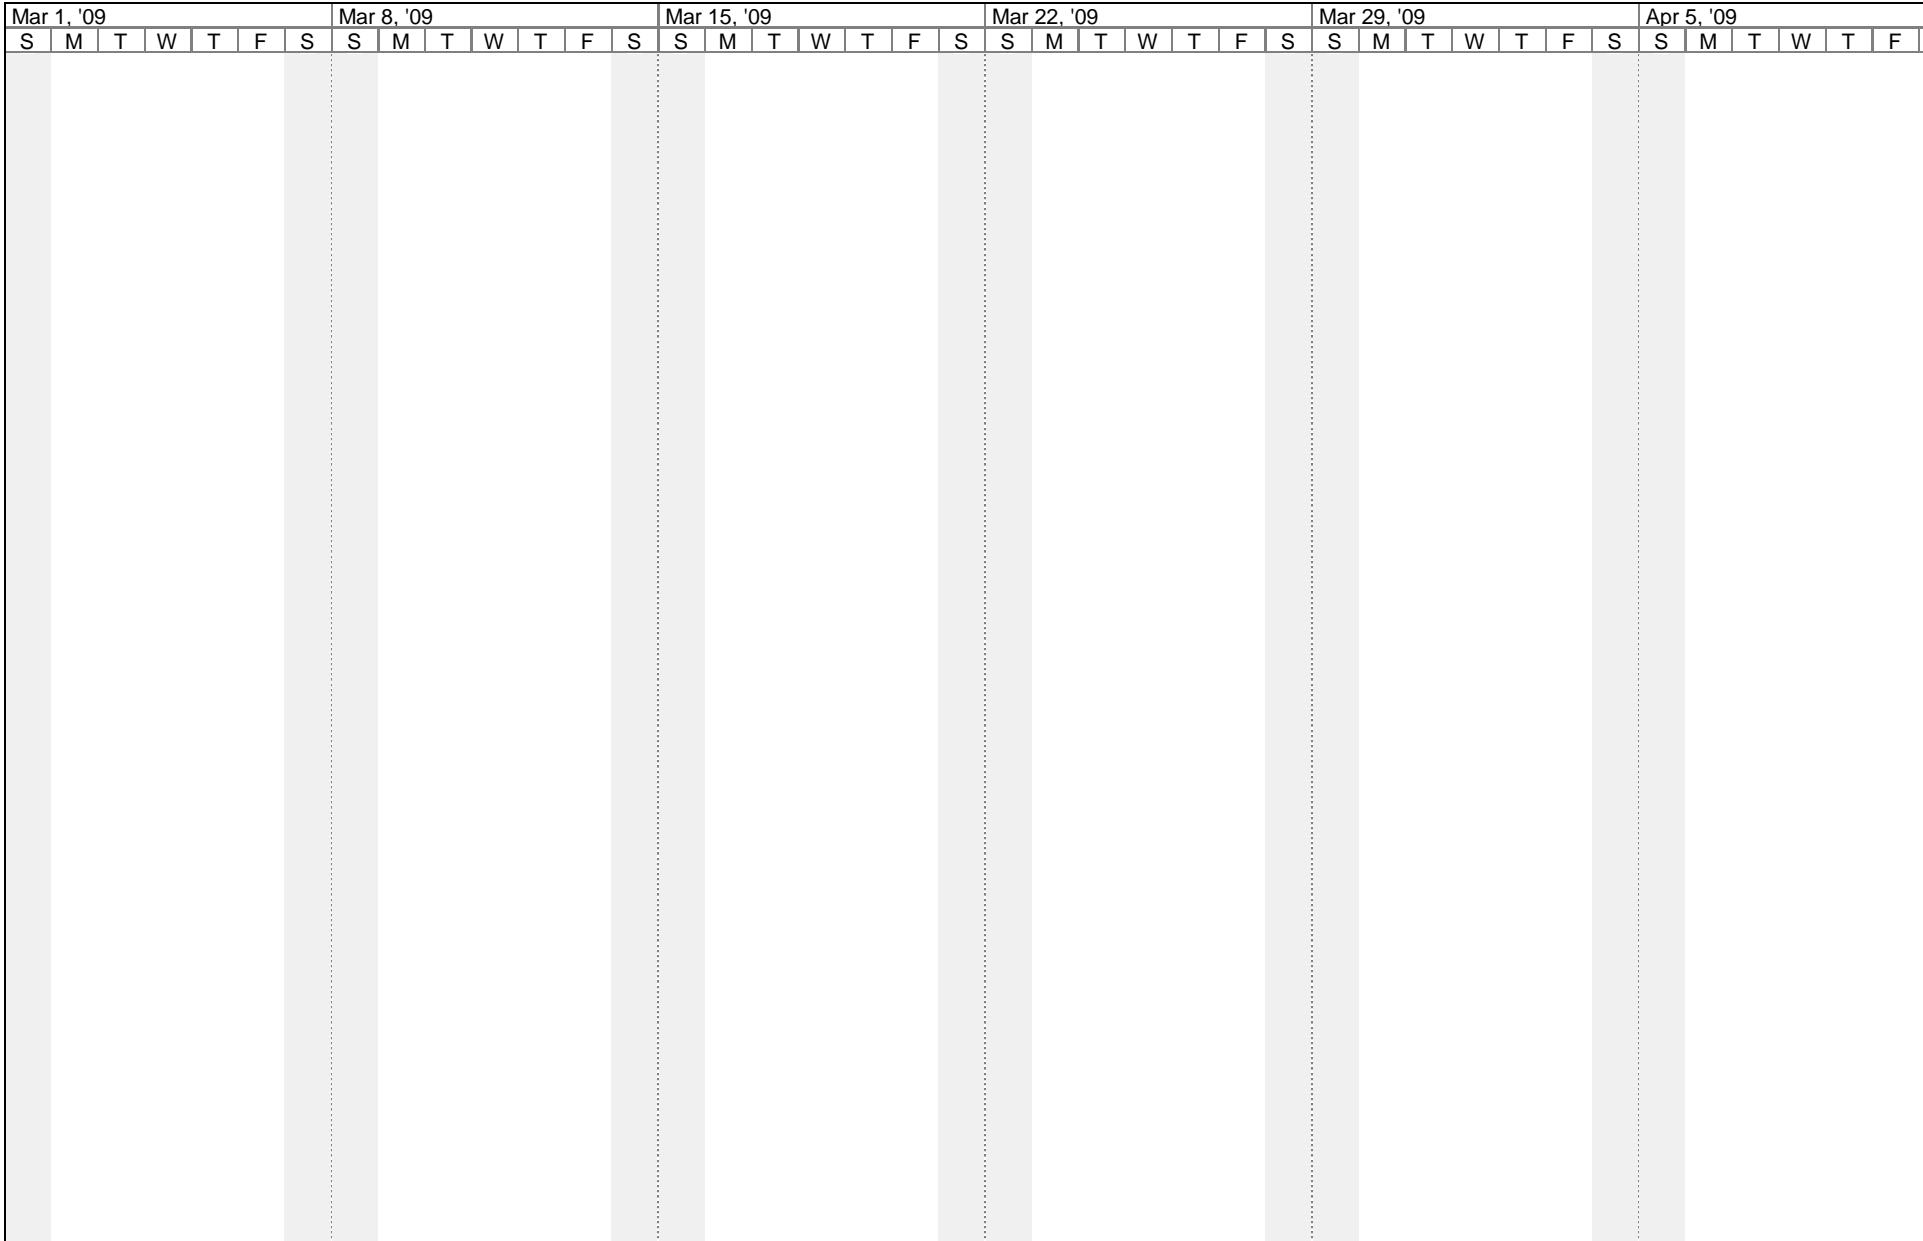


Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	





Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



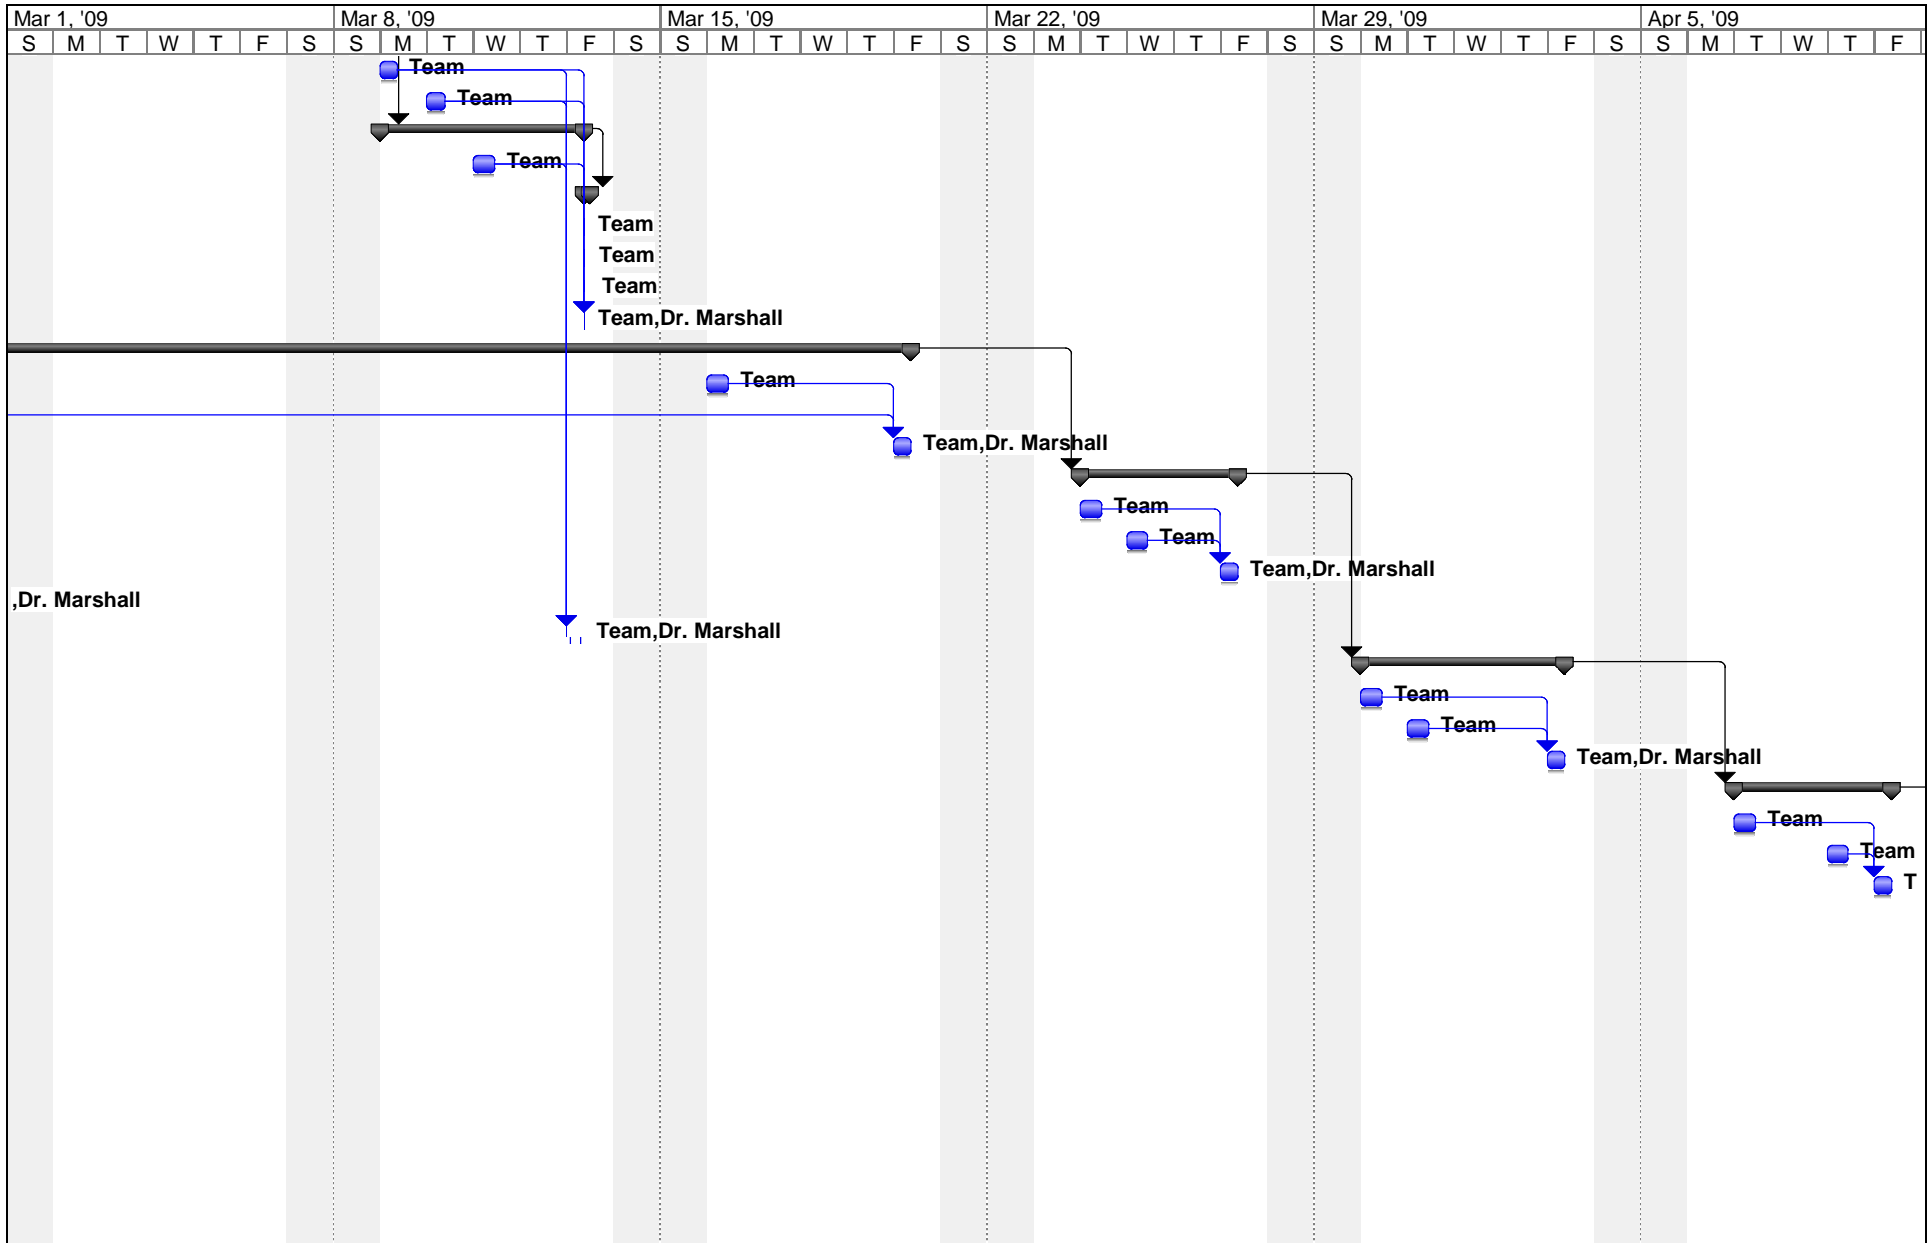










Project: MSD\_2quarter\_schedule  
 Date: Thu 12/11/08










Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


Mar 1, '09							Mar 8, '09							Mar 15, '09							Mar 22, '09							Mar 29, '09							Apr 5, '09						
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	









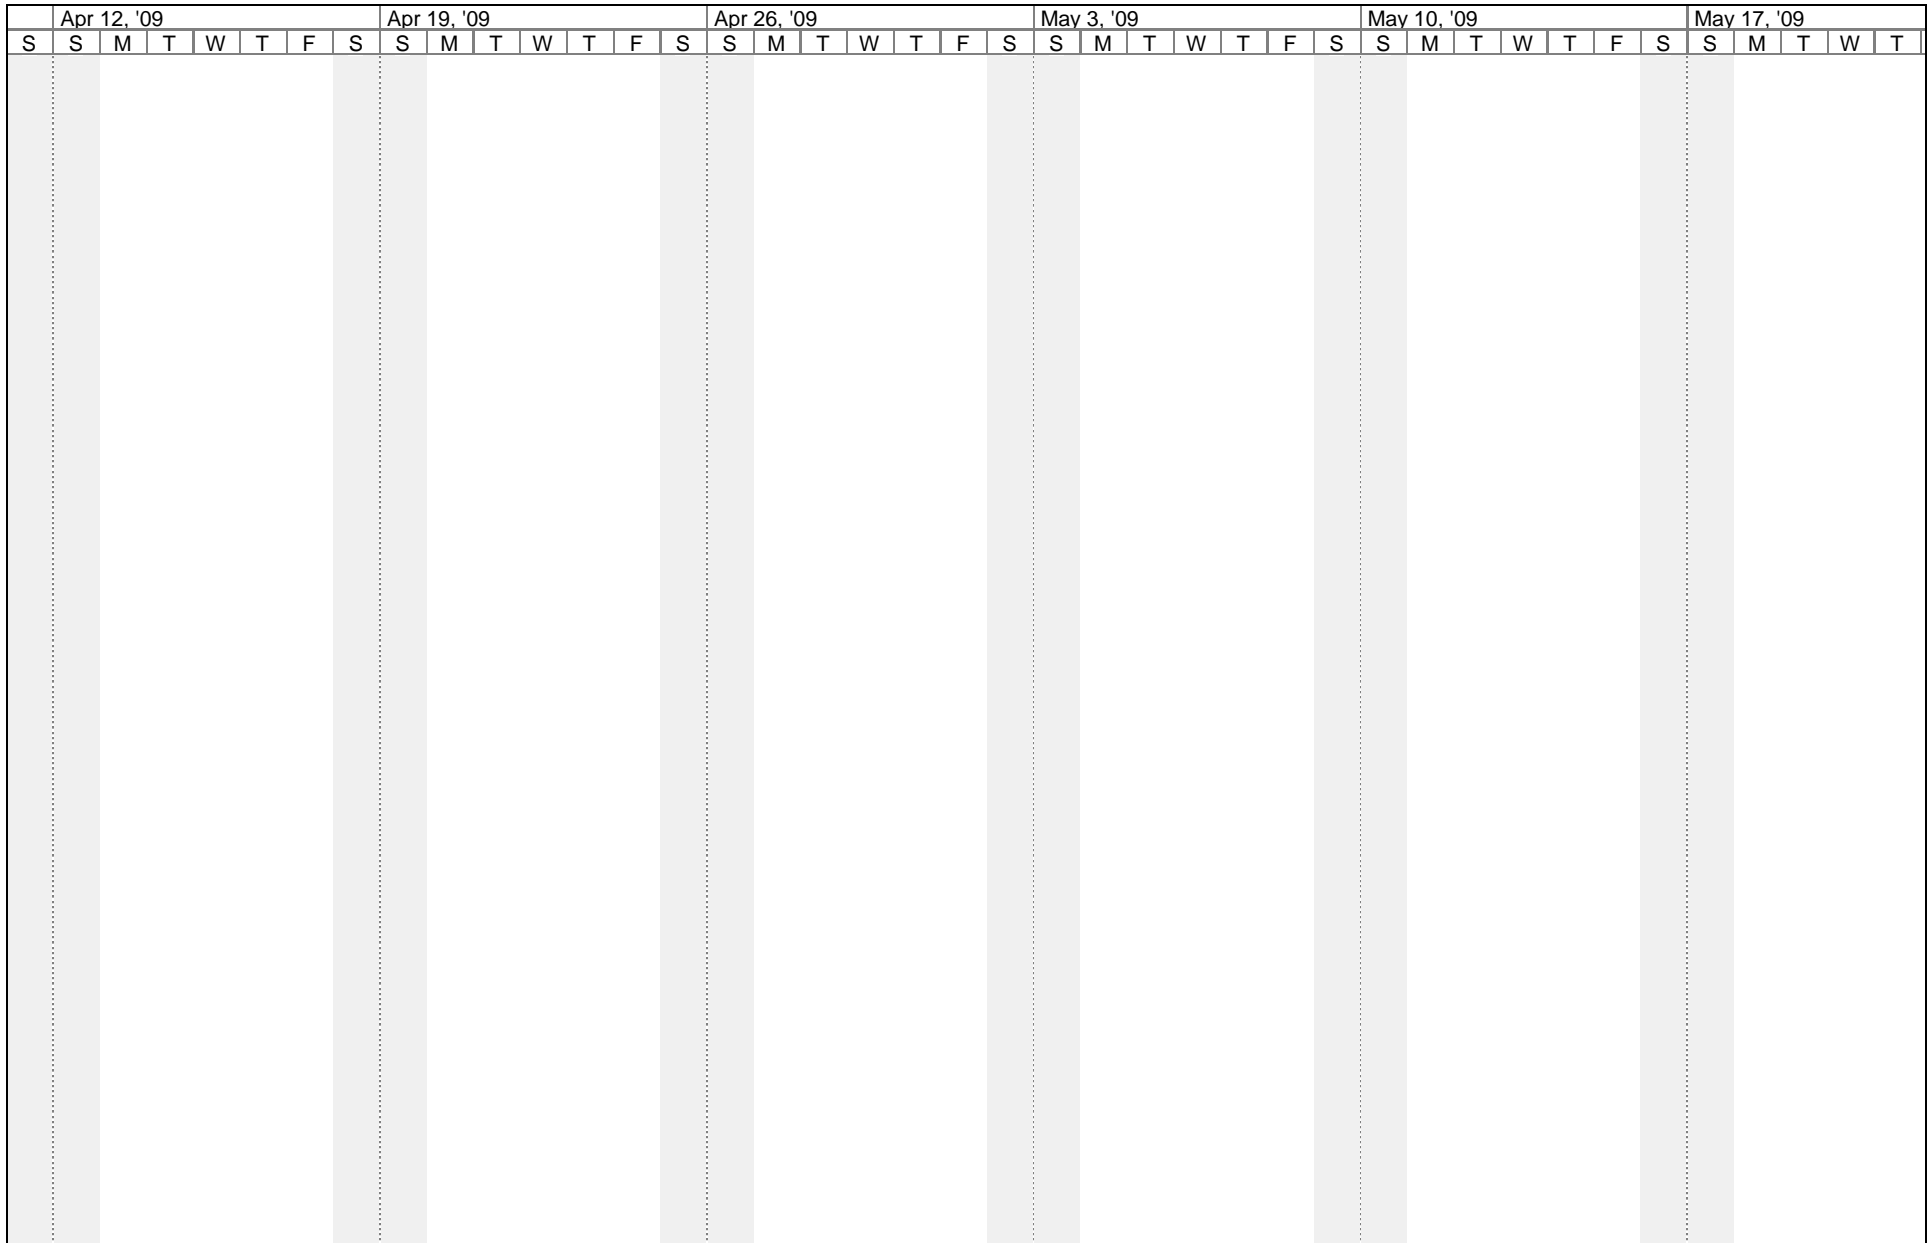


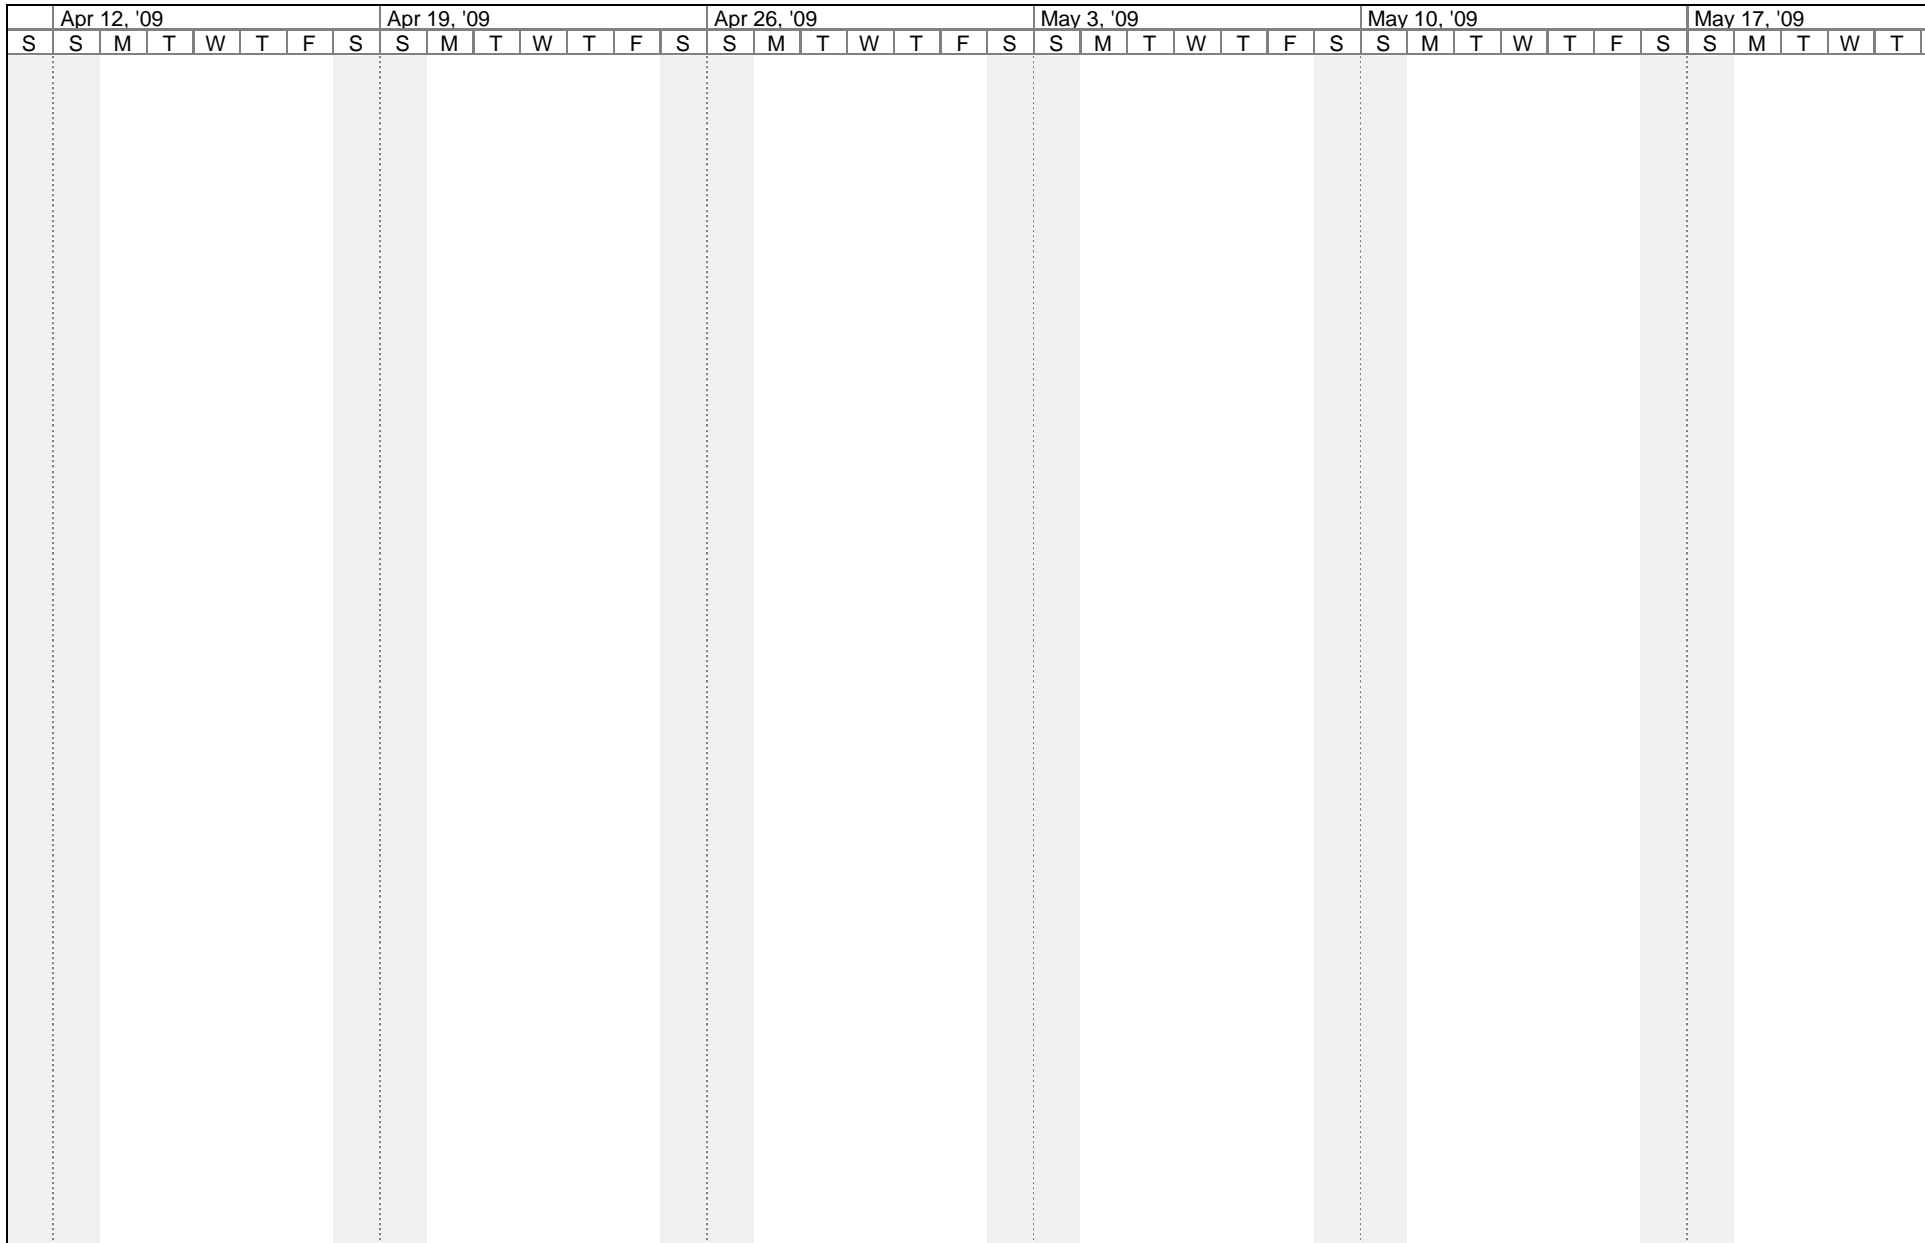
Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	












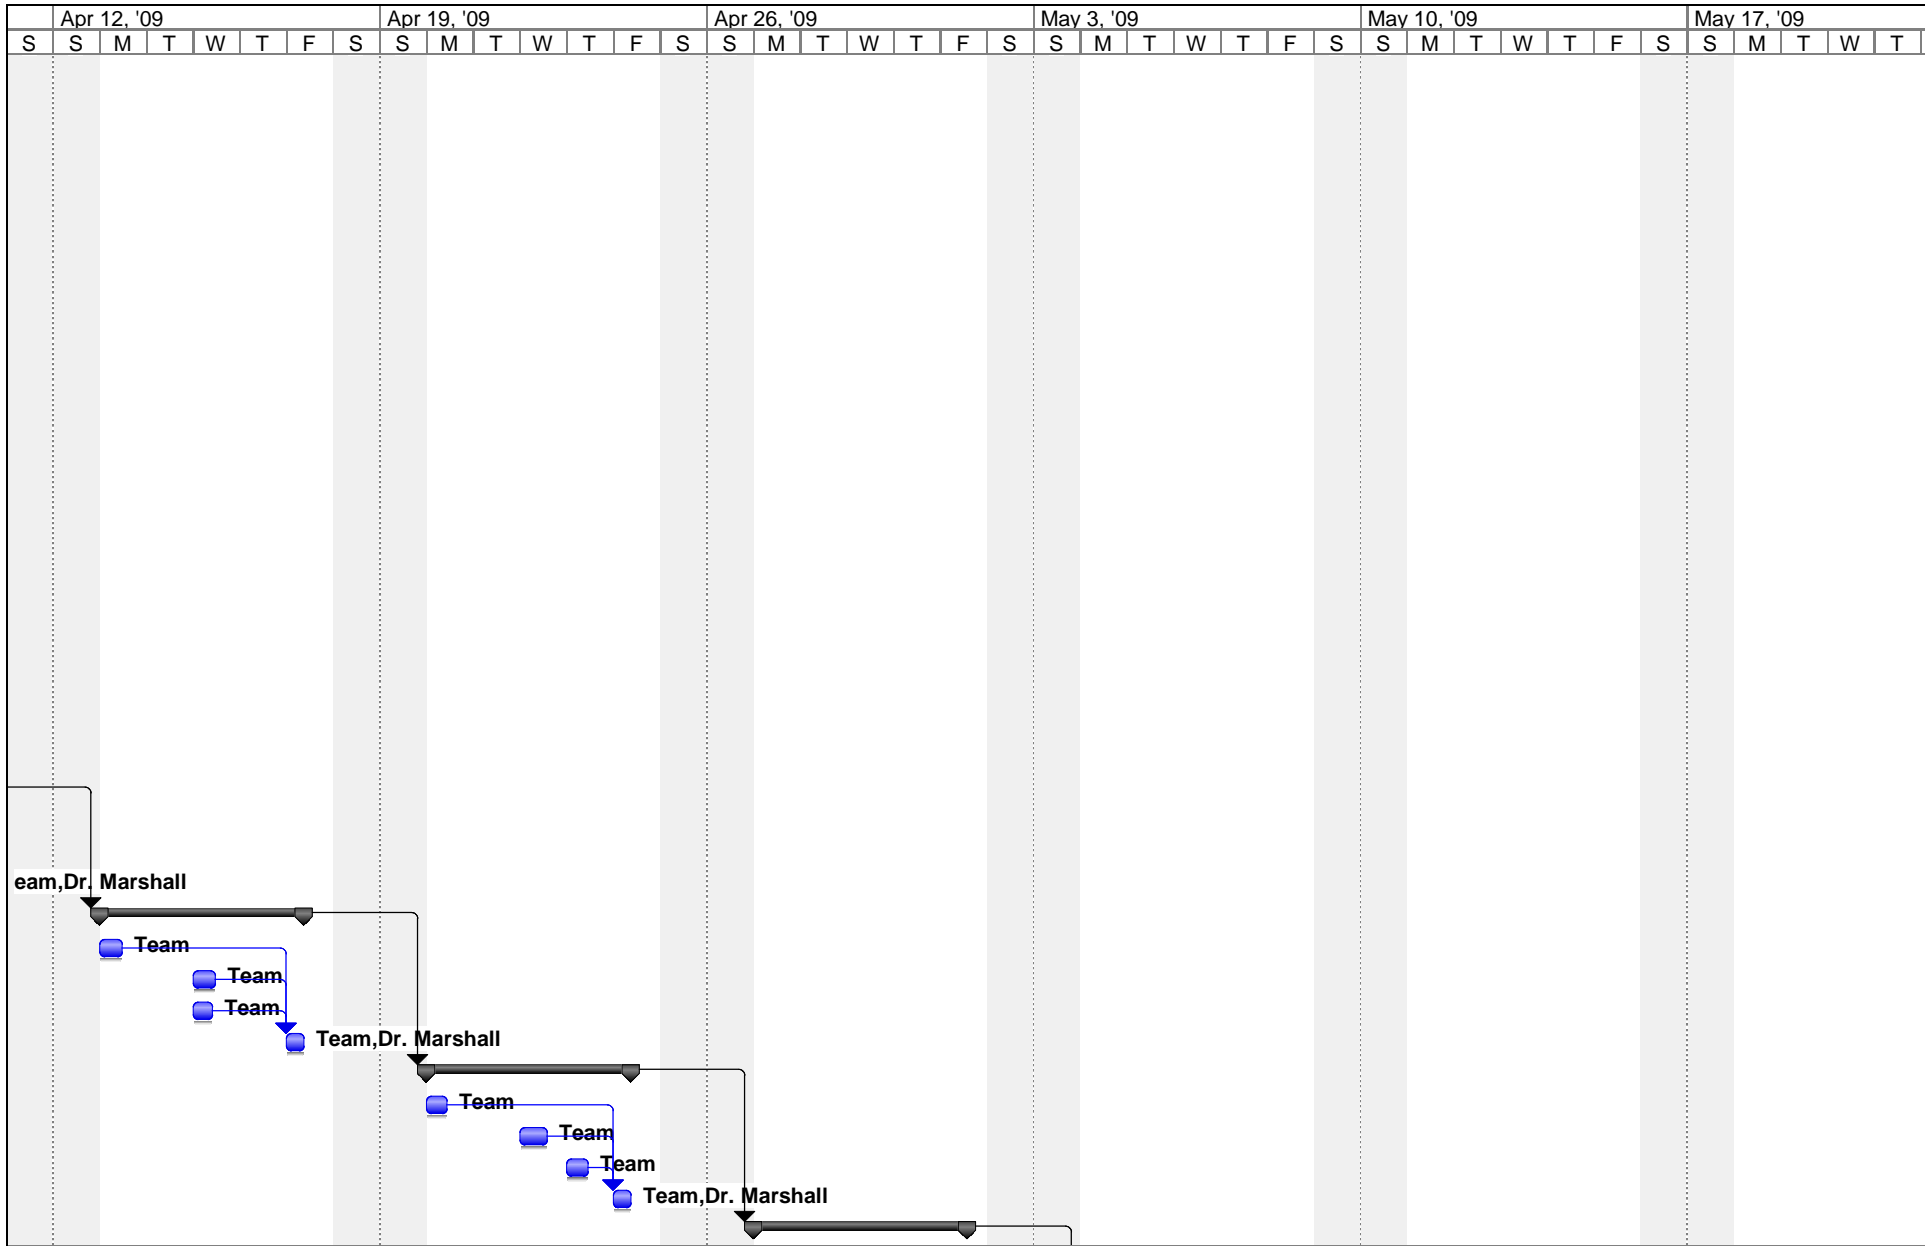
Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



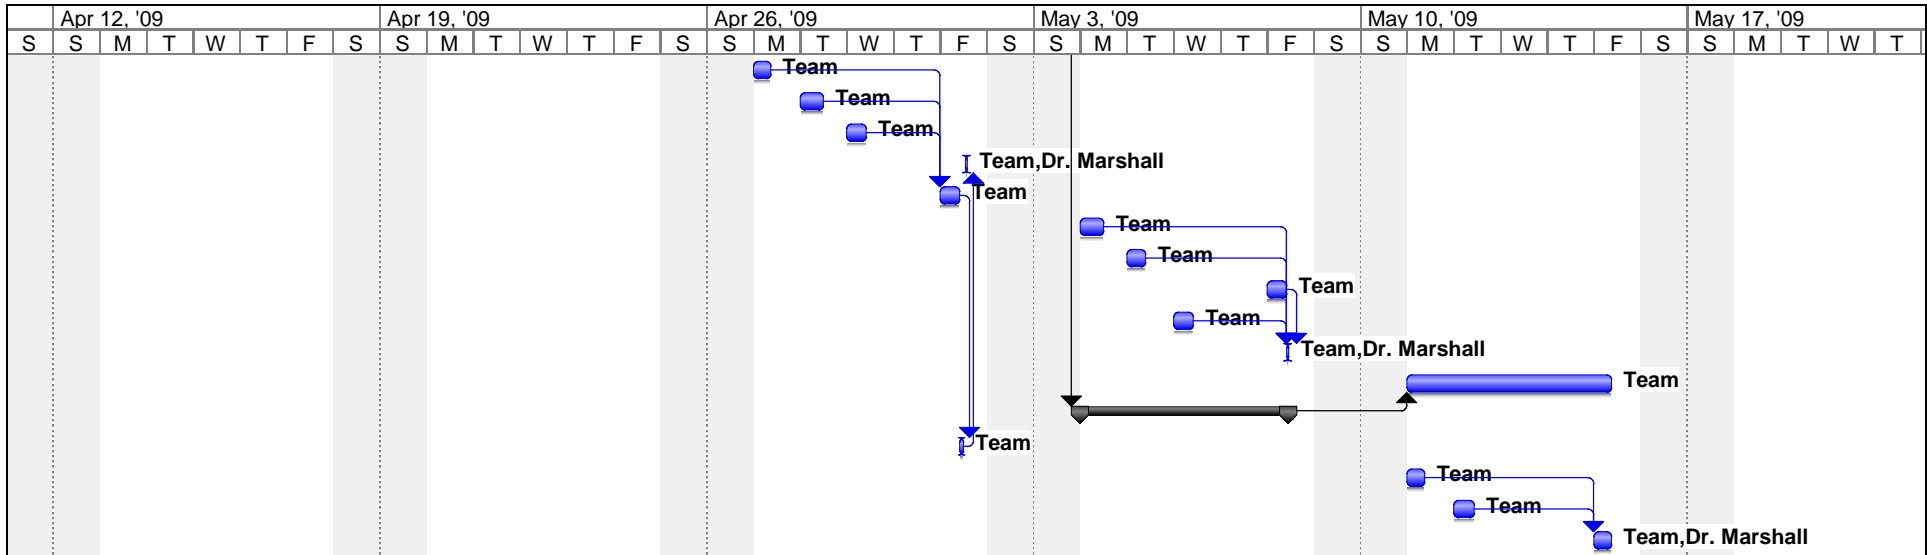

Project: MSD_2quarter_schedule Date: Thu 12/11/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
