

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
1	1 MSD II	93 days	Mon 1/26/15	Tue 5/19/15			95%
2							
3	1.1 Acquire all purchased materials	3 days	Tue 1/20/15	Thu 1/22/15		Mayer	100%
4	1.2 Verify Purchased materials	2 days	Mon 1/26/15	Tue 1/27/15			100%
5							
6	1.3 Assemble the Owl System	41 days	Mon 1/26/15	Fri 3/13/15	3,4		100%
41							
42	1.4 OWL Assembly Completed	1 day	Mon 3/16/15	Mon 3/16/15	6		100%
43	1.5 Update Mechanical drawing package with changes to layout and/or hardware	0 days	Mon 2/23/15	Fri 2/27/15	6	Partac	100%
44	1.6 Update Electrical drawing package with changes to layout and/or hardware	1 day	Mon 5/11/15	Mon 5/11/15	6	Mayer	100%
45							
46	1.7 Test programs for test plan	13 days	Tue 1/27/15	Tue 2/10/15			100%
53							
54	1.8 Test Components to the Test Plan	54 days	Tue 1/27/15	Mon 4/6/15			100%
62							
63	1.9 Create Motion Control Program	64 days	Wed 2/18/15	Fri 5/8/15	60		100%
72							
73	1.10 Assemble the Car Mount	5 days	Tue 1/20/15	Sun 1/25/15	43		100%
82							
83	1.11 Error measurement program	63 days	Thu 2/26/15	Fri 5/15/15	46		93%

December 1
11/23 | 12/7

Project: MSD II Project Plan(201
Date: Mon 5/11/15

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
84	1.11.1 Program the first draft of the error measurement program	17 days	Thu 2/26/15	Tue 3/17/15	56	Carey	100%
85	1.11.2 Test the error measurement program	0 days	Tue 3/17/15	Tue 3/17/15	84	Carey, (Misc)	100%
86	1.11.3 Determine issues and trouble shoot	1 day	Tue 3/17/15	Tue 3/17/15	85	Carey	100%
87	1.11.4 Edit the error measurement program	6 days	Tue 5/5/15	Mon 5/11/15	85		100%
88	1.11.5 Test the error measurement program	0 days	Tue 5/5/15	Mon 5/11/15	86,87	Carey, (Misc)	100%
89	1.11.6 Determine issues and trouble shoot	0 days	Tue 5/5/15	Mon 5/11/15	88	Carey	100%
90	1.11.7 Edit the error measurement program	3 days	Mon 5/11/15	Thu 5/14/15	88		0%
91	1.11.8 Test the motion control program	1 day	Mon 5/11/15	Fri 5/15/15	89,90	Carey, (Misc)	0%
92	1.11.9 Determine/choose what to point at	33 days	Mon 3/30/15	Tue 5/5/15			100%
93							
94	1.12 Test System to the Test Plan	40 days	Sat 4/11/15	Tue 5/26/15	6,54,73		25%
95	1.12.1 Conduct mount stability testing	0 days	Sat 4/11/15	Sat 4/11/15		Battery (Misc)	100%
96	1.12.2 Conduct system error testing	7 days	Tue 5/5/15	Tue 5/26/15	51	Battery (Misc)	50%
97	1.12.3 Conduct fade data testing	7 days	Mon 5/11/15	Sun 5/24/15	52	Battery (Misc)	0%
98							
99	1.13 System Testing Complete	0 days	Tue 5/26/15	Tue 5/26/15	94		0%
100							
101	1.14 Create Video Script	84 days	Thu 1/1/15	Wed 4/15/15			100%

December 1
11/23 | 12/7

Project: MSD II Project Plan(201
Date: Mon 5/11/15

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	Predecessor	Resource Names	% Complete
123							
124	1.15 Film video	10 days	Wed 4/15/15	Sun 4/26/15	101,6,7		100%
129							
130	1.16 Video Filming Completed	1 day	Sun 4/26/15	Sun 4/26/15	124		100%
131							
132	1.17 Edit Video	8 days	Sun 4/26/15	Sun 5/3/15	124		50%
145							
146	1.18 Deliver the Final Marketing Video	3 days	Mon 5/4/15	Wed 5/6/15	132		0%
152							
153	1.19 Technical paper	53 days	Fri 3/6/15	Tue 5/12/15	83,63		100%
193							
194	1.20 MSD Poster	15 days	Tue 4/7/15	Thu 4/23/15	83,63		100%
201							
202	1.21 Create User Manual	7 days	Mon 5/11/15	Mon 5/18/15	83,63		0%
203	1.21.1 Develop user manual template	0 days	Mon 5/11/15	Mon 5/11/15		Carey	100%
204	1.21.2 Create user manual	0 days	Mon 5/11/15	Mon 5/11/15	203	Carey	100%
205	1.21.3 Revise and Format user manual	1 day	Mon 5/11/15	Sun 5/17/15	204	Carey	0%
206	1.21.4 Submit user manual	1 day	Mon 5/18/15	Mon 5/18/15	205	Carey	0%
207							
208	1.22 Hand over project to spectracom	2 days	Thu 5/14/15	Fri 5/15/15	202,94		0%
209	1.22.1 Give all documents to spectracom	2 days	Thu 5/14/15	Fri 5/15/15		Partac	0%
210	1.22.2 Return/erase all proprietary information	1 day	Thu 5/14/15	Thu 5/14/15			0%

December 1
11/23 | 12/7

Project: MSD II Project Plan(201
Date: Mon 5/11/15

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
211							
212	1.23 Meet w/ Spectracom to discuss ... (fill in)	0.25 days	Thu 2/5/15	Thu 2/5/15			100%
213	1.24 Meet w/ Spectracom to discuss ... (fill in)	0.25 days	Thu 2/19/15	Thu 2/19/15			100%
214	1.25 Meet w/ Spectracom to discuss ... (fill in)	1 day	Wed 3/4/15	Wed 3/4/15			100%
215	1.26 Meet w/ Spectracom to discuss ... (fill in)	1 day	Wed 3/18/15	Wed 3/18/15			100%
216	1.27 Meet w/ Spectracom to discuss ... (fill in)	0.25 days	Thu 4/2/15	Thu 4/2/15			0%
217	1.28 Meet w/ Spectracom to discuss ... (fill in)	0.25 days	Thu 4/16/15	Thu 4/16/15			100%
218	1.29 Meet w/ Spectracom to discuss ... (fill in)	0.25 days	Thu 4/30/15	Thu 4/30/15			100%
219	1.30 Meet w/ Spectracom to discuss ... (fill in)	0.25 days	Thu 5/14/15	Thu 5/14/15			0%
220	1.31 IMAGINE RIT	0 days	Sat 5/2/15	Sat 5/2/15			100%
221	1.32 Present at IMAGINE RIT	1 day	Sat 5/2/15	Sat 5/2/15		Balenti	100%

December 1
11/23 12/7

Project: MSD II Project Plan(201
Date: Mon 5/11/15


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ber 1 | January 1 | February 1 | March 1 | April 1 | May 1
 12/7 | 12/21 | 1/4 | 1/18 | 2/1 | 2/15 | 3/1 | 3/15 | 3/29 | 4/12 | 4/26 | 5/10

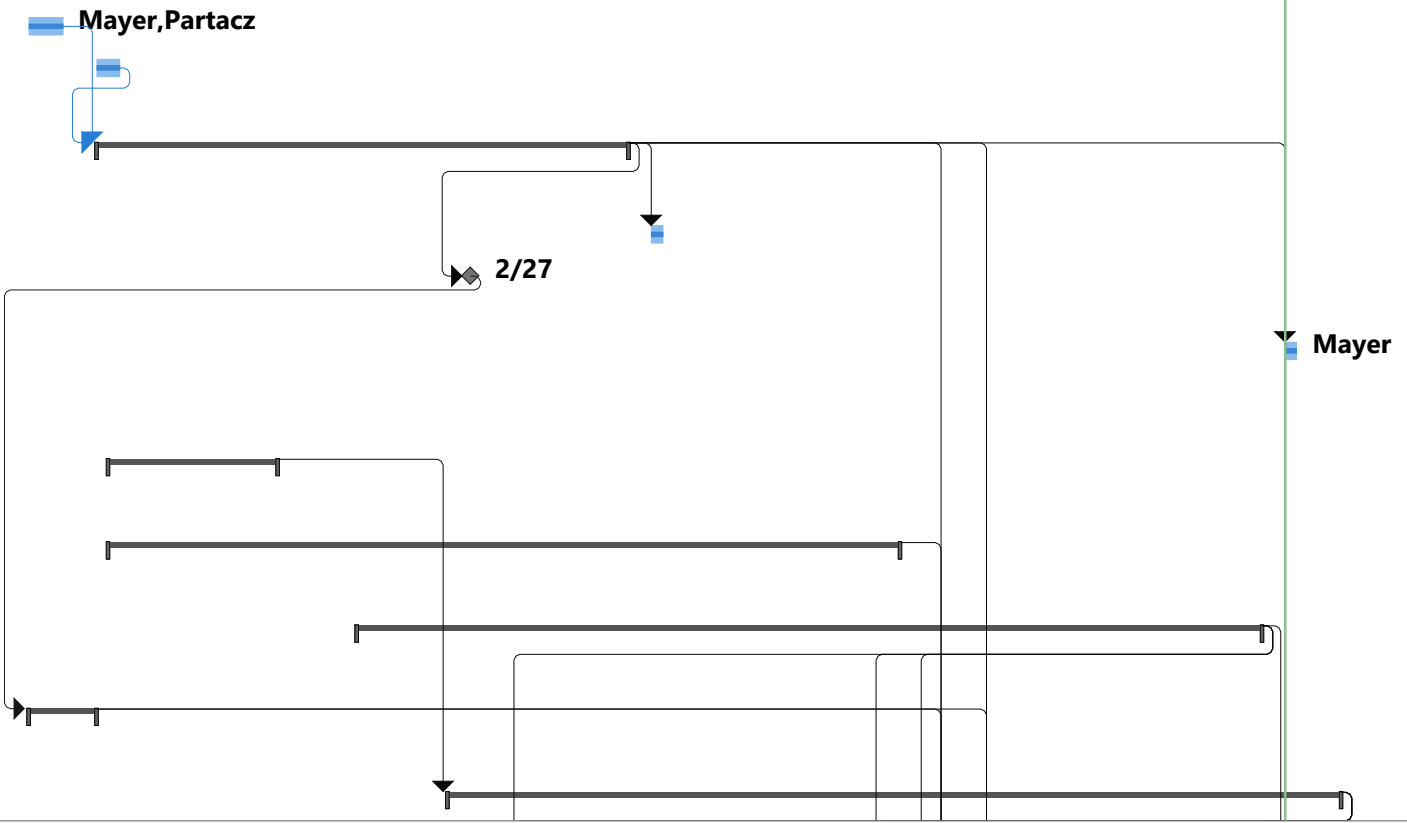


Project: MSD II Project Plan(201
 Date: Mon 5/11/15

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

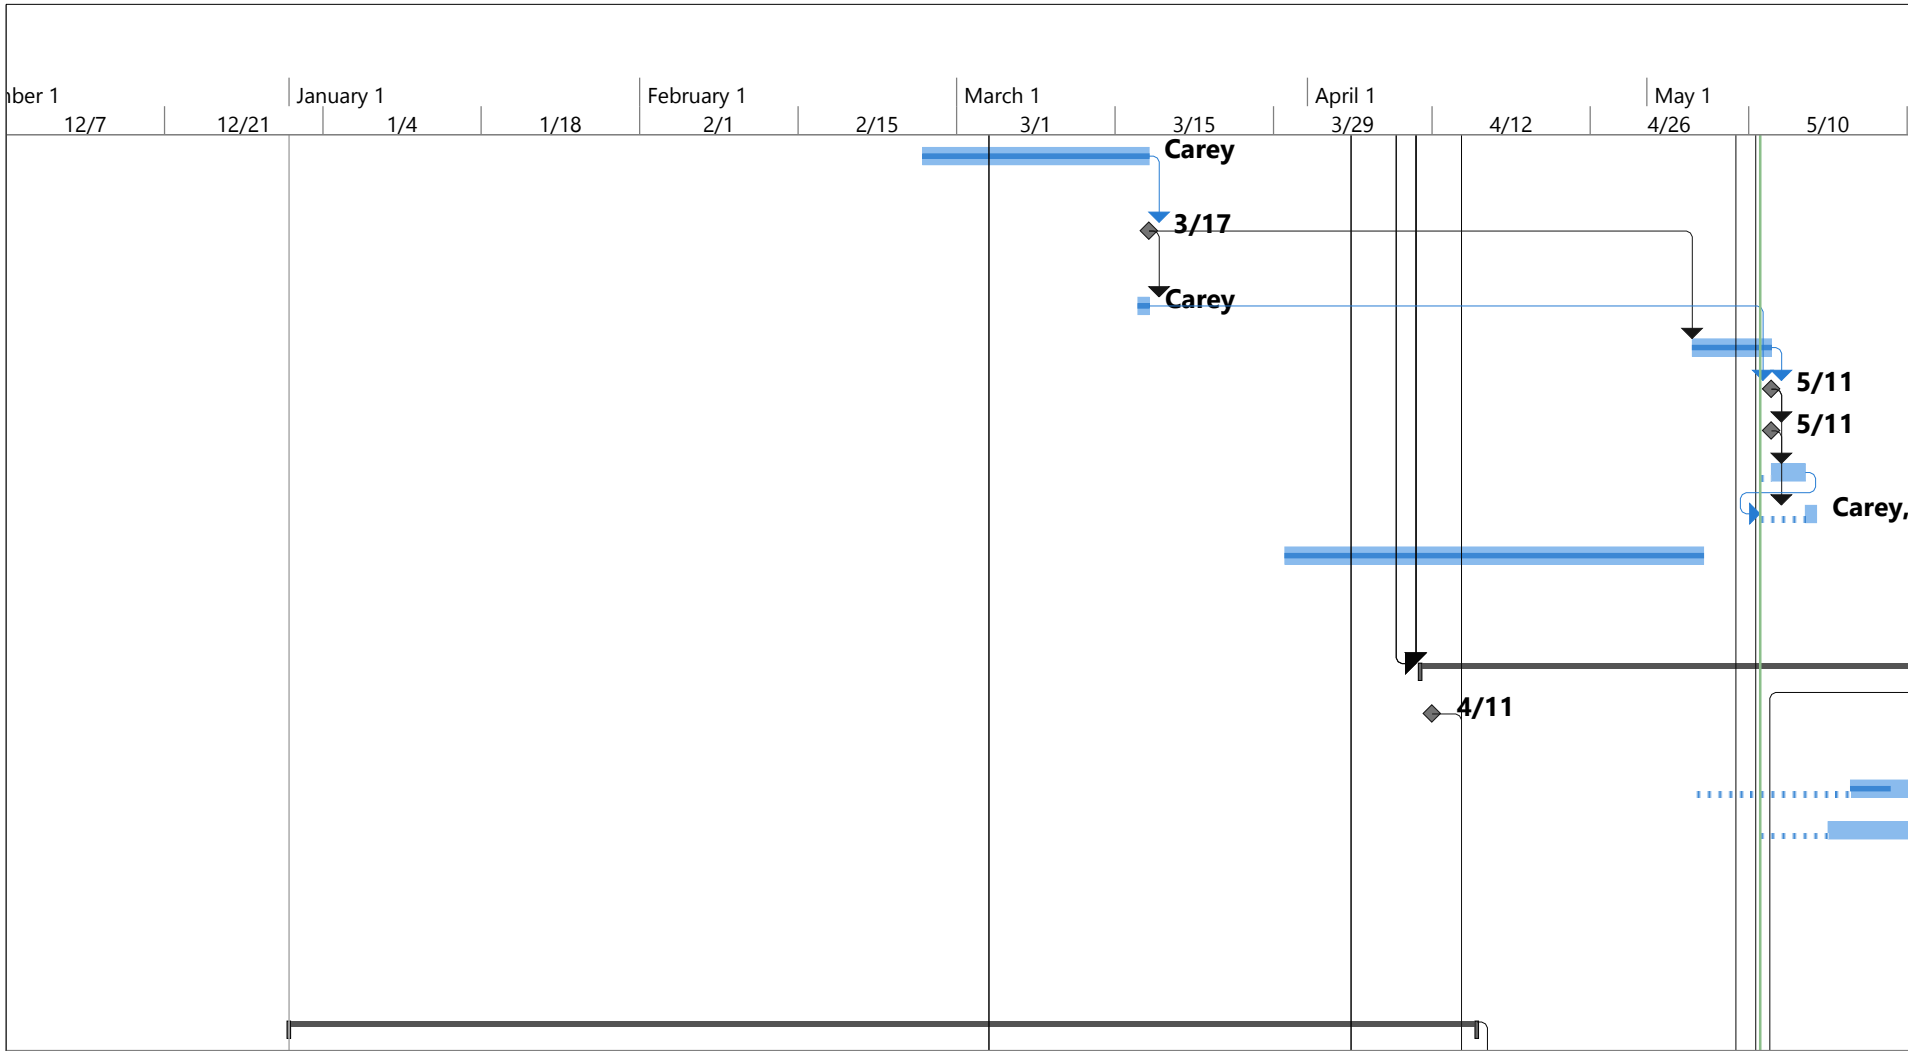


Project: MSD II Project Plan(201
Date: Mon 5/11/15

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

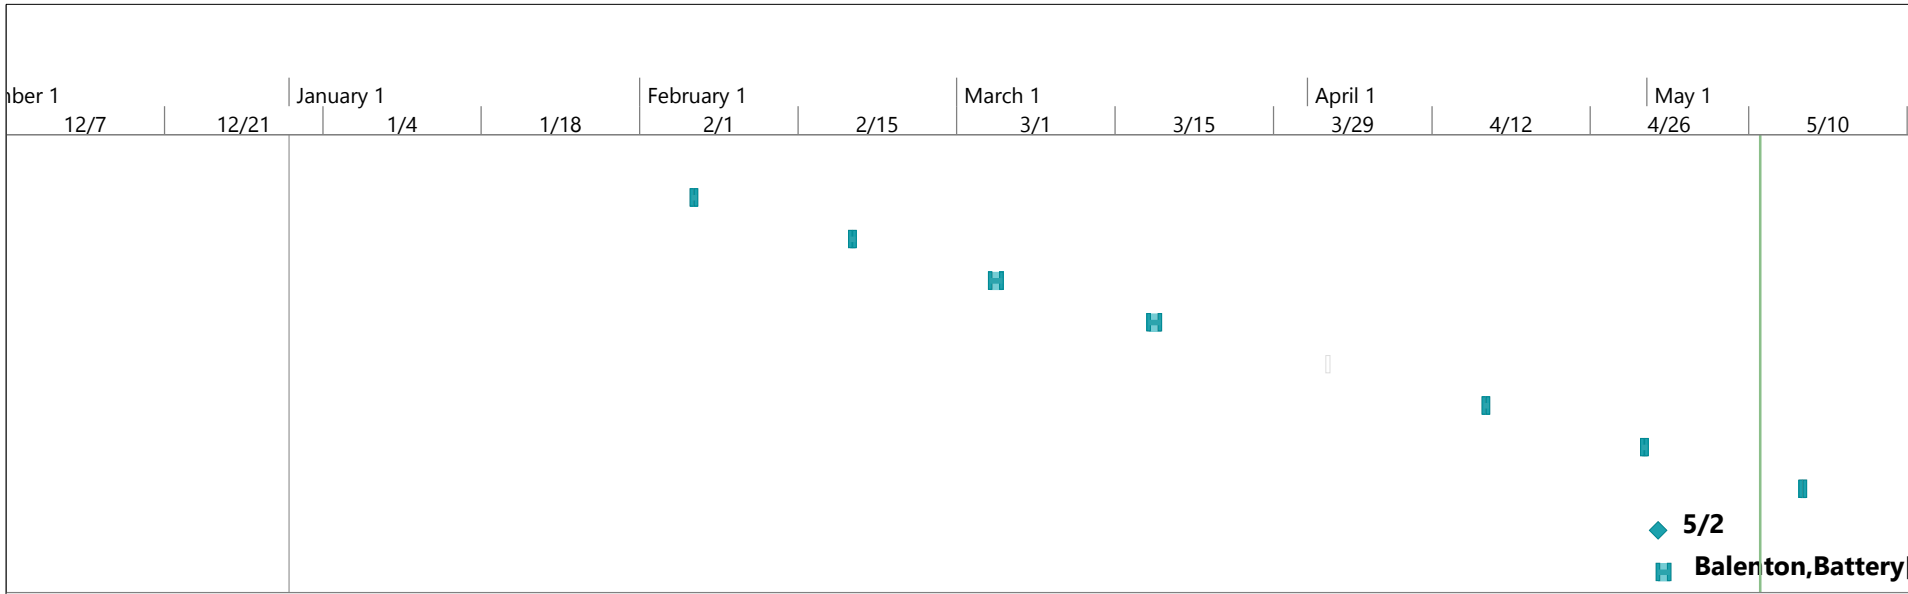


Project: MSD II Project Plan(201
Date: Mon 5/11/15

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

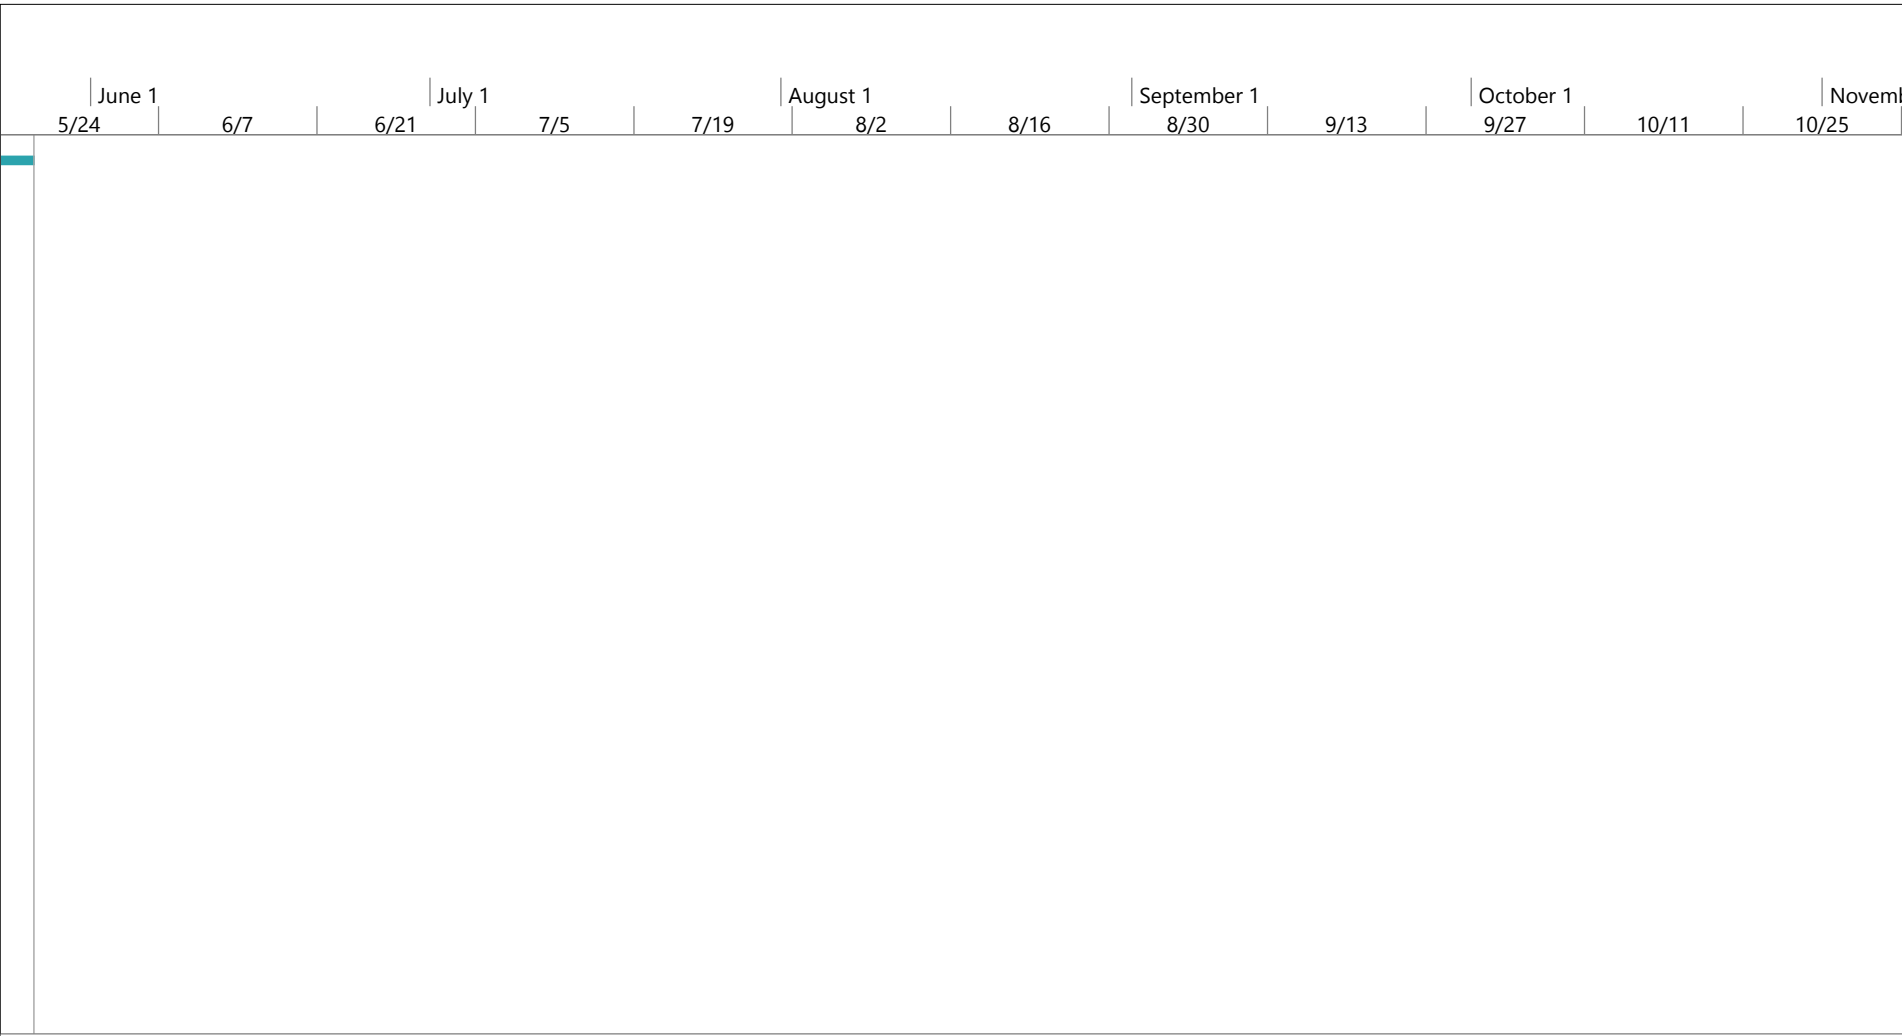


Project: MSD II Project Plan(201
Date: Mon 5/11/15

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

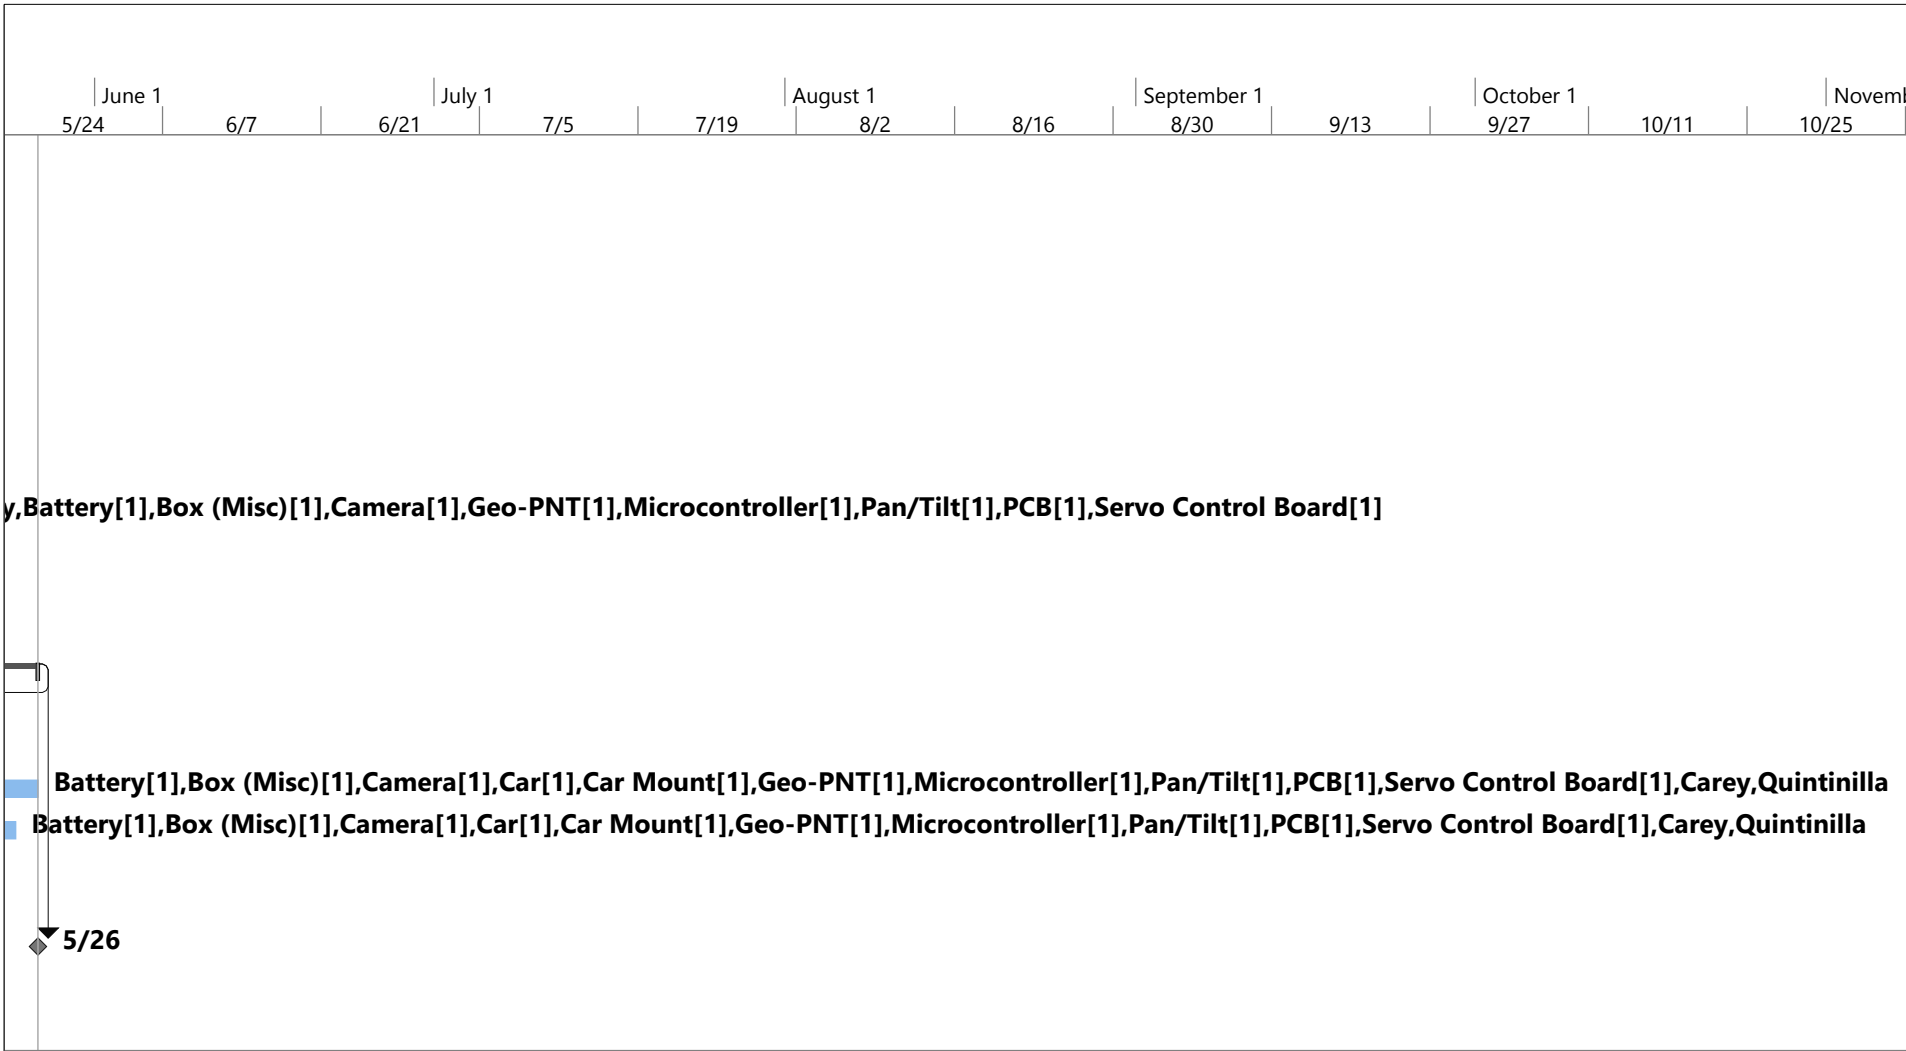

Project: MSD II Project Plan(201 Date: Mon 5/11/15	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



rey
rey
acz

Project: MSD II Project Plan(201
Date: Mon 5/11/15

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



y[1],Box (Misc)[1],Camera[1],Car Mount[1],Carey,Geo-PNT[1],Mayer,Microcontroller[1],Pan/Tilt[1],Partacz,PCB[1],Quintinilla,Servo Control Board[1]

Project: MSD II Project Plan(201
Date: Mon 5/11/15

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
