


ID	Task Mode	Task Name	Duration	Start	Finish	26, '18							Sep 2, '18							Sep 9
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	
1		W.A.R 3 Project	60 days?	Mon 8/27/18	Fri 11/16/18															
2		Problem Definition Phase	16 days?	Mon 8/27/18	Mon 9/17/18															
3		Problem Statement	1 day?	Mon 8/27/18	Mon 8/27/18															
4		Develop Use Cases	2 days	Tue 8/28/18	Wed 8/29/18															
5		Develop Interview Questions	2 days	Tue 8/28/18	Wed 8/29/18															
6		Interview Customer	1 day?	Fri 8/31/18	Fri 8/31/18															
7		Determine Customer Requiren	4 days	Fri 8/31/18	Wed 9/5/18															
8		Define Team Roles	2 days	Wed 9/5/18	Thu 9/6/18															
9		Define Team Norms and Value	2 days	Wed 9/5/18	Thu 9/6/18															
10		Benchmarking table	4 days	Wed 9/5/18	Mon 9/10/18															
11		Risk Management Matrix	2 days	Tue 9/11/18	Wed 9/12/18															
12		Draft Engineering Requiremen	2 days	Tue 9/11/18	Wed 9/12/18															
13		Problem Definition Review Pre	3 days	Thu 9/13/18	Mon 9/17/18															
14		Systems Design Phase	20 days	Tue 9/18/18	Mon 10/15/18															
15		Functional Decomposition	2 days	Tue 9/18/18	Wed 9/19/18															
16		Functional Analysis	2 days	Tue 9/18/18	Wed 9/19/18															
17		Morph Chart	2 days	Tue 9/18/18	Wed 9/19/18															
18		Concept Generation	5 days	Tue 9/18/18	Mon 9/24/18															
19		Hydraulic system																		
20		Frame structure																		
21		Seatbelt Mechanism																		
22		Transfer Process map																		
23		Select hybrid concept	4 days	Wed 9/19/18	Mon 9/24/18															

Project: MSD_19011 Date: Fri 9/14/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


ID	Task Mode	Task Name	Duration	Start	Finish	26, '18							Sep 2, '18							Sep 9
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	
24		Engineering analysis	2 days	Tue 9/25/18	Wed 9/26/18															
25		Systems Design Review Prep	13 days	Thu 9/27/18	Mon 10/15/18															
26		Preliminary Detailed Design Phase	23 days	Tue 10/16/18	Thu 11/15/18															
27		Subsystems Design	5 days	Tue 10/16/18	Mon 10/22/18															
28		Detailed Design & Component	2 days	Tue 10/23/18	Wed 10/24/18															
29		Design for Manufacture and Assembly	3 days	Thu 10/25/18	Mon 10/29/18															
30		Preliminary Detailed Design Review	13 days?	Tue 10/30/18	Thu 11/15/18															
31		Complete Detailed Design Phase		Fri 11/16/18																

Project: MSD_19011
Date: Fri 9/14/18

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

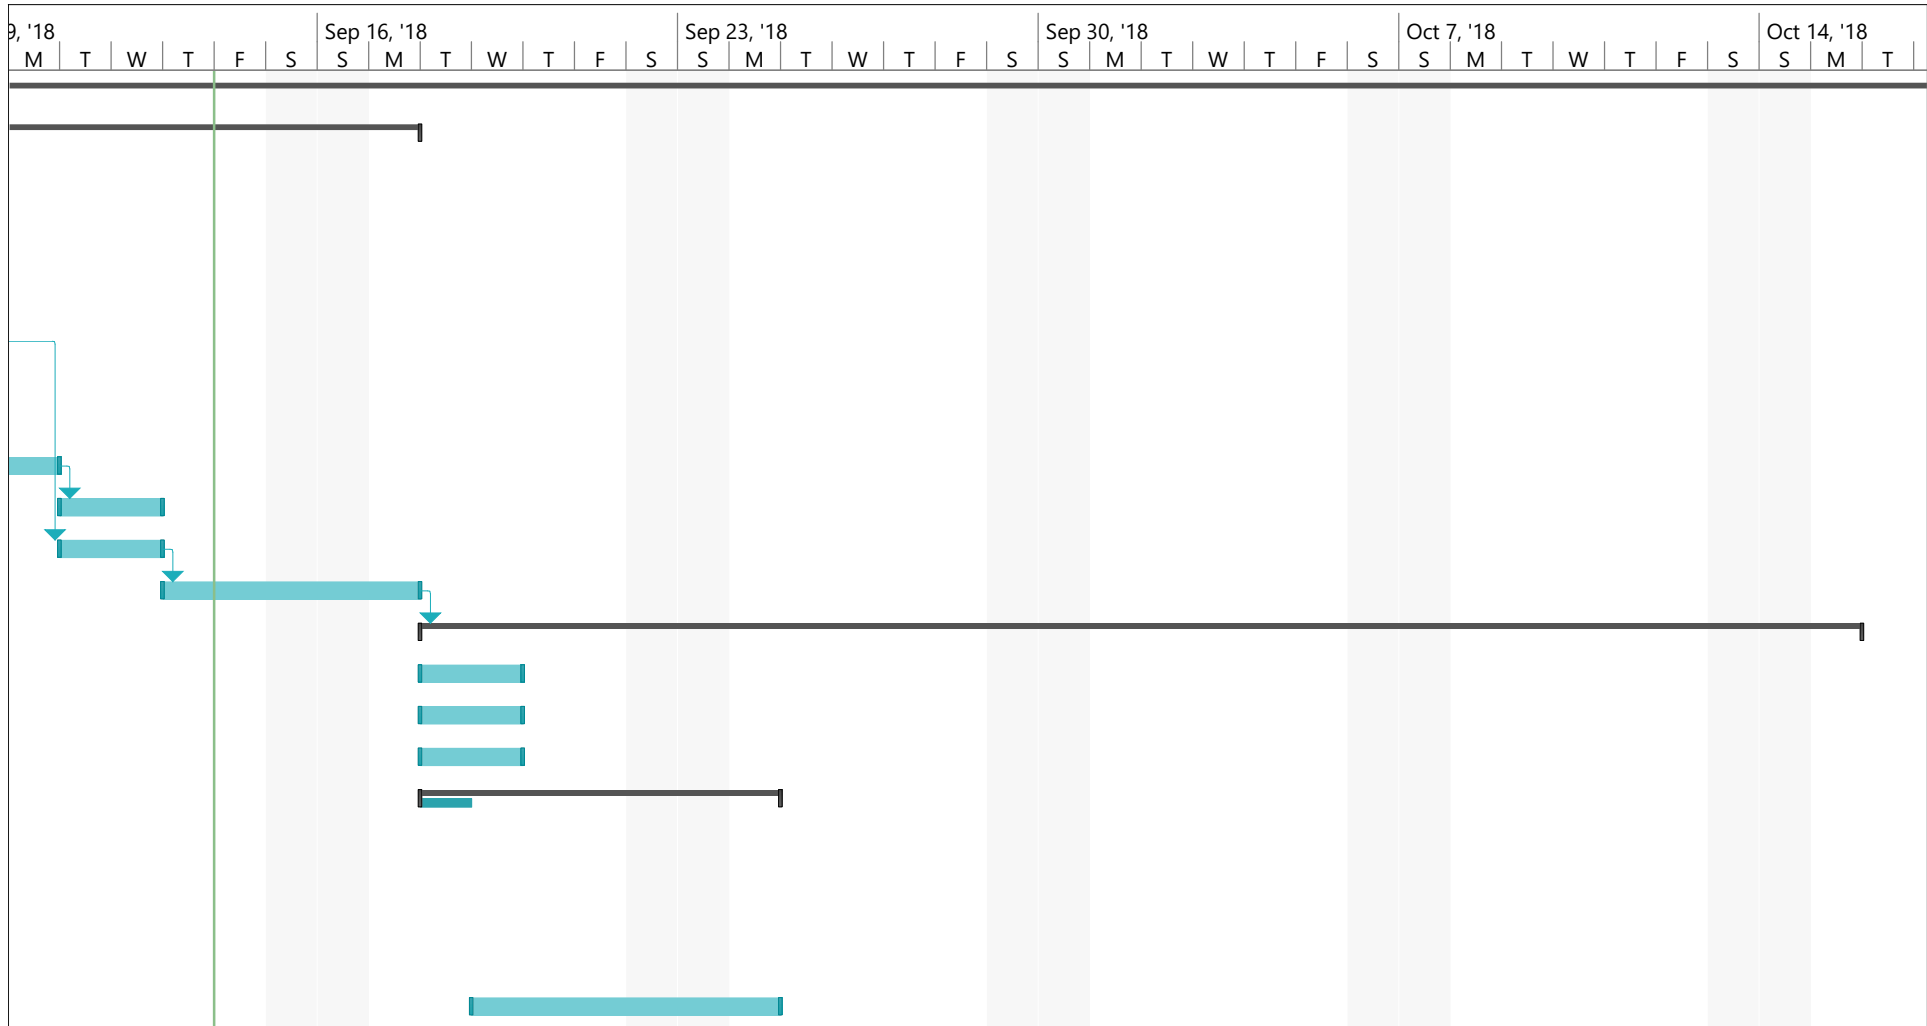

Project: MSD_19011 Date: Fri 9/14/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

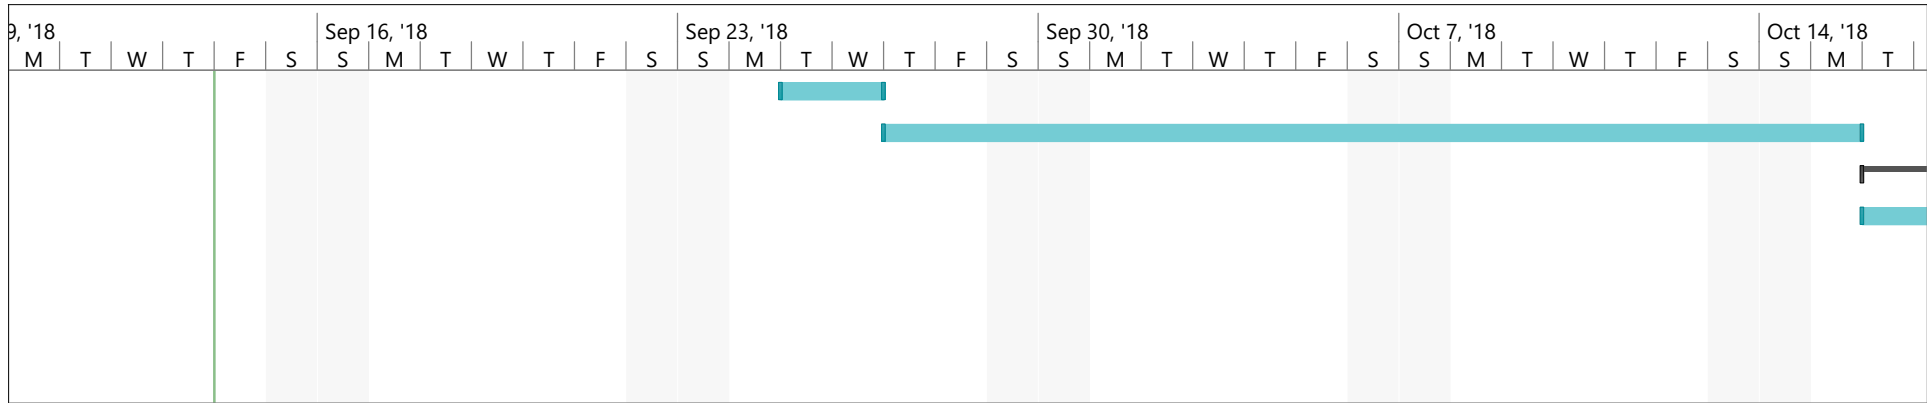


Project: MSD_19011
Date: Fri 9/14/18

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: MSD_19011
 Date: Fri 9/14/18

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

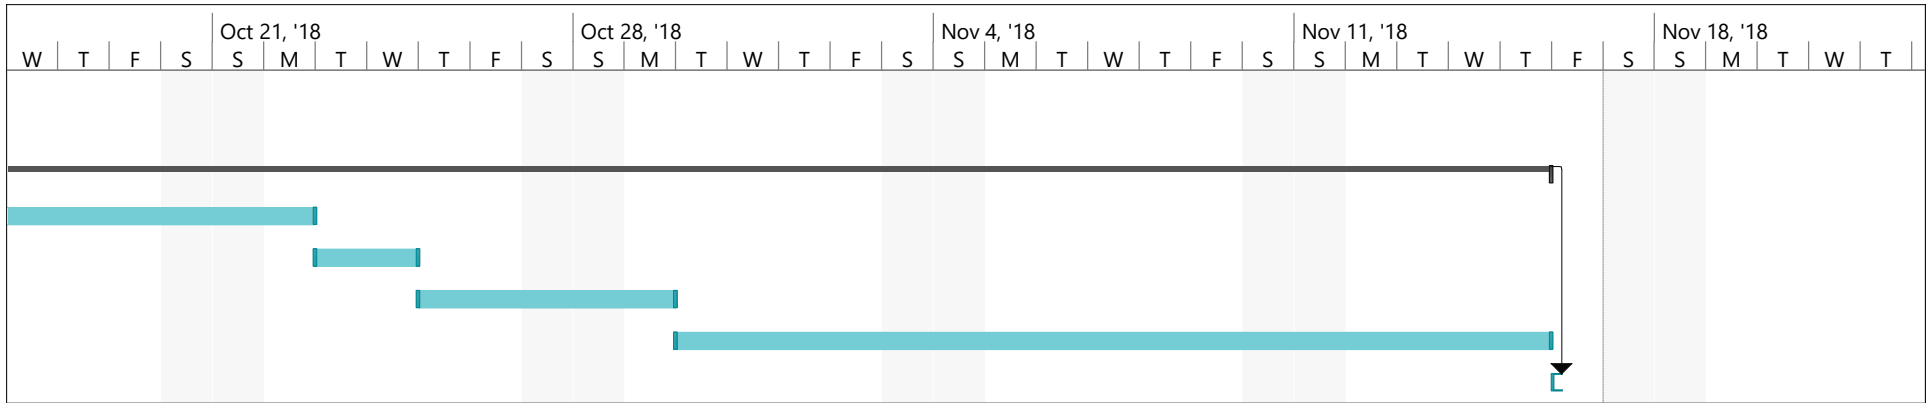

Project: MSD_19011
Date: Fri 9/14/18

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
