ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		Close MSD I Action Items	6 days	Fri 3/12/10	Fri 3/19/10		
2		Order Parts	8 days	Wed 3/10/10	Fri 3/19/10		
3		Test k-value	1 day	Fri 3/12/10	Fri 3/12/10		
4		Test Breaking Strength	1 day	Fri 3/19/10	Fri 3/19/10	3	
5		PCB Layout	6 days	Fri 3/26/10	Fri 4/2/10	2	
6		Build Electrical Prototype	5 days	Mon 4/5/10	Fri 4/9/10	5	
7		Test Electrical Prototype	5 days	Mon 4/12/10	Fri 4/16/10	6	
8		Test Electrical Circuit	1 day	Mon 4/19/10	Mon 4/19/10	7	
9		Meet With Customer	1 day	Mon 3/15/10	Mon 3/15/10		
10		Build Frame	20 days	Mon 3/22/10	Fri 4/16/10	2	
11		Detailed Test Plans	7 days	Fri 3/12/10	Mon 3/22/10		
12		Meet with Customer at RIT	1 day	Fri 4/16/10	Fri 4/16/10		
13		Test Frame	6 days	Mon 4/19/10	Mon 4/26/10	10,11	
14		Assemble and Test Tilt	6 days	Mon 4/19/10	Mon 4/26/10	10,11	
15		Assemble and Test Flywheel	6 days	Mon 4/19/10	Mon 4/26/10	10,11	
16		Assemble and Test Handlebars	6 days	Mon 4/19/10	Mon 4/26/10	10,11	
17		Wiring	5 days	Tue 4/20/10	Mon 4/26/10	10,8,11	
18		Imagine RIT (User Interface Stu	1 day	Sat 5/1/10	Sat 5/1/10	13,14,15,16,17	
19		Clinic Debute/User Interface Stu	1 day?	Mon 5/3/10	Mon 5/3/10	18	
20		Function and Performance Revi	1 day?	Fri 5/7/10	Fri 5/7/10	13,14,15,16,17,18,	
21		Bike Completed and Fully Teste	5 days	Mon 5/10/10	Fri 5/14/10	20	
22		Delivery of Bike	1 day?	Mon 5/17/10	Mon 5/17/10	21	
23		Instruction Manual	37 days	Fri 3/26/10	Fri 5/14/10		
24		Begin Paper	16 days	Mon 4/5/10	Mon 4/26/10		
25		75% Technical Paper	3 days	Tue 4/27/10	Thu 4/29/10	24	
26		Paper Exchange	1 day?	Fri 4/30/10	Fri 4/30/10	25	
27		100% Technical Paper	11 days	Sat 5/1/10	Fri 5/14/10	26	
28		Poster #1	5 days	Mon 4/26/10	Fri 4/30/10		
29		Poster #2	10 days	Mon 5/3/10	Fri 5/14/10	28	
30		Poster Session	1 day?	Fri 5/21/10	Fri 5/21/10	29	
31		Final Project Review	1 day?	Mon 5/17/10	Mon 5/17/10	27,29,21	

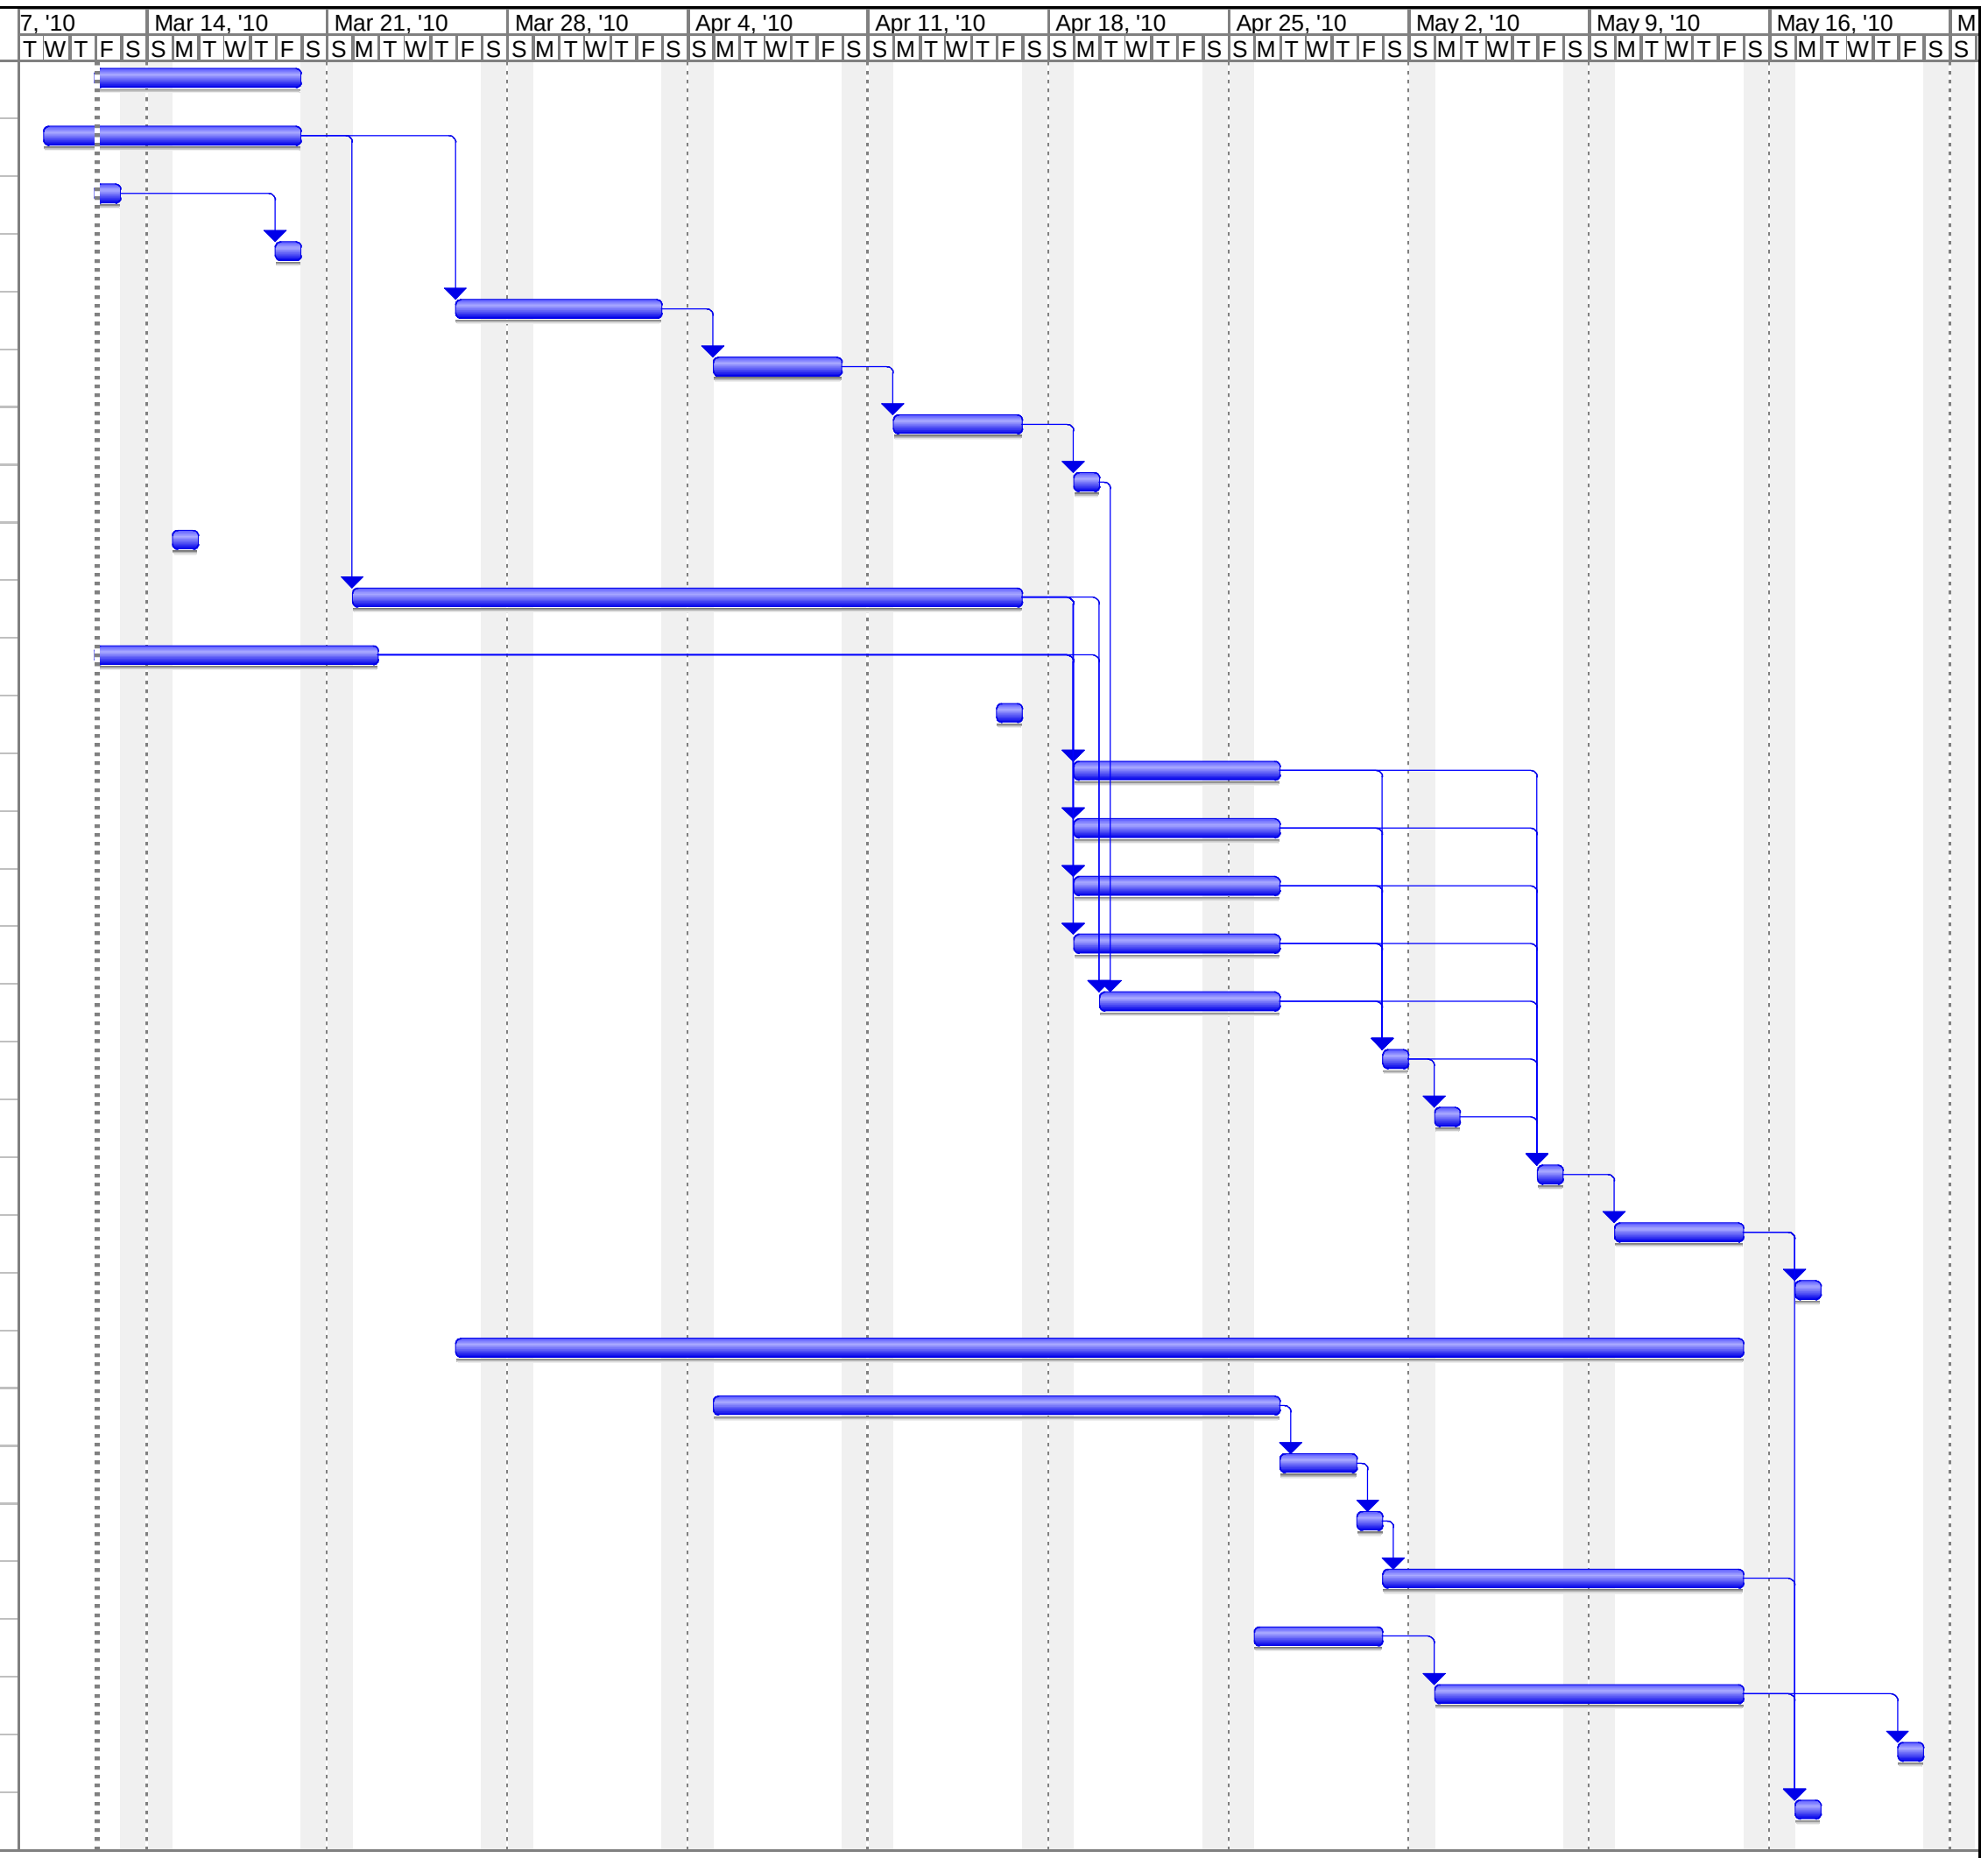

Project: MSD II Project Plan
Date: Fri 3/12/10

Task		Progress		Summary		External Tasks	
Split		Milestone		Project Summary		External Milestone	

Deadline
