ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	Regroup and review implementation plan for MSD 2	1 day?	Wed 12/1/10	Wed 12/1/10		
2	Review Meeting w/. John K.	1 day?	Thu 12/2/10	Thu 12/2/10	1	
3	Preparing checklists for Kaizen Event No. 1	1 day?	Thu 12/2/10	Thu 12/2/10	1	
4	Prepare large plan for Kaizen Event No. 1	1 day?	Thu 12/2/10	Thu 12/2/10	1	
5	Contacting appropriate management resources for Kaizen Event No. 1	1 day?	Fri 12/3/10	Fri 12/3/10	3,4	
6	Confirm that client will provide appropriate materials for Kaizen Event No. 1.	1 day?	Fri 12/3/10	Fri 12/3/10	3,4	
7	Confirm availability of 495's for Kaizen Event No. 1	1 day?	Fri 12/3/10	Fri 12/3/10		
8	Present detailed overview of Kaizen Event No. 1 to client.	1 day?	Fri 12/3/10	Fri 12/3/10		
9	Update Risk Analysis for MSD 2	2 days	Mon 12/6/10	Tue 12/7/10	1	
10	Complete pending action items from MSD 1	3 days	Fri 12/3/10	Tue 12/7/10	2	
11	Update Project plan as needed	1 day	Wed 12/8/10	Wed 12/8/10	10	
12	Obtain quotes from vendors for kits	1 day?	Thu 12/2/10	Thu 12/2/10	1	
13	Present the client with vendor options.	1 day?	Fri 12/3/10	Fri 12/3/10	12	
14	Make a decision on kit boxes to purchase	1 day?	Mon 12/6/10	Mon 12/6/10	13	
15	Briefing meeting with 495's Pre-Kaizen	0 days	Fri 12/10/10	Fri 12/10/10	6,7,8	
16	Kaizen Event No. 1	1 day?	Fri 12/10/10	Fri 12/10/10	15	
17	Debriefing meeting with 495's post-Kaizen	0 days	Fri 12/10/10	Fri 12/10/10		
18	Create communication plan from Kaizen changes	1 day?	Fri 12/10/10	Fri 12/10/10	17	
19	Walk the client through the improved area to present changes	0 days	Fri 12/10/10	Fri 12/10/10		
20	Debrief meeting on Kaizen event and accomplished goals	1 day?	Mon 12/13/10	Mon 12/13/10	19,18	
21	Follow-up meeting with John K regarding issues and concerns	1 day?	Tue 12/14/10	Tue 12/14/10	20	
22	Create progress package for DR	1 day?	Wed 12/15/10	Wed 12/15/10	21	
23	Follow-up action items post-Kaizen event	1 day?	Wed 12/15/10	Wed 12/15/10	18,20	
24	Check on implemented changes	2 days	Thu 12/16/10	Fri 12/17/10	23	
25	Act/Adjust accordingly to modify implementation as needed.	2 days	Mon 12/20/10	Tue 12/21/10	24,22	
26	Email communications to assess inspection area for 6S event	1 day?	Fri 12/17/10	Fri 12/17/10	16	
27	SKYPE Meeting to assess project needs	1 day?	Wed 12/22/10	Wed 12/22/10	25,26	
28	Prepare checklist for 6S event	1 day?	Mon 1/3/11	Mon 1/3/11	27	
29	Prepare large plan for 6S event	1 day?	Mon 1/3/11	Mon 1/3/11	26	
30	Contacting appropriate management resources for 6S Event	1 day?	Tue 1/4/11	Tue 1/4/11	28,29	
31	Confirm that client will provide requested materials for 6s Event	1 day?	Tue 1/4/11	Tue 1/4/11	28,29	
32	Confirm availability of 495's for 6S Event	1 day?	Wed 1/5/11	Wed 1/5/11	30	
33	Present detailed overview of 6S Event	1 day?	Wed 1/5/11	Wed 1/5/11	30,31	
34	Briefing meeting with 495's Pre-Kaizen	0 days	Fri 1/7/11	Fri 1/7/11	33	
35	6S Event	1 day?	Fri 1/7/11	Fri 1/7/11	34	
36	Debriefing meeting with 495's post-Kaizen	0 days	Fri 1/7/11	Fri 1/7/11	35	
37	Create communication plan from 6S Event	1 day?	Mon 1/10/11	Mon 1/10/11	36	
38	Walk the client through the improved area to present 6S improvements	0 days	Fri 1/7/11	Fri 1/7/11	36	
39	Check on implemented changes	1 day?	Wed 1/12/11	Wed 1/12/11	37,38	
40	Act/Adjust accordingly to modify implementation as needed.	2 days	Thu 1/13/11	Fri 1/14/11	39	
41	Assess Kaizen Event No. 2 opportunities	1 day?	Mon 1/10/11	Mon 1/10/11	35	
42	Preparing checklists for Kaizen Event No. 2	1 day?	Tue 1/11/11	Tue 1/11/11	41	
43	Prepare large plan for Kaizen Event No. 2	1 day?	Tue 1/11/11	Tue 1/11/11	41	
44	Kaizen No. 2 assessment	1 day?	Thu 1/13/11	Thu 1/13/11	43,42	
45	Contacting appropriate management resources for Event	1 day	Fri 1/14/11	Fri 1/14/11	44	
46	Culminate designs for kit pallets	1 day	Fri 1/14/11	Fri 1/14/11	44	
47	Obtain feedback for kit designs from manufacturing personnel	1 day	Fri 1/14/11	Fri 1/14/11	44	
48	Create a visible prototype for prefered kit design.	1 day	Mon 1/17/11	Mon 1/17/11	47	
49	Present updated schematics on selected kit design	1 day	Fri 1/21/11	Fri 1/21/11	48	
50	Confirm that client will provide appropriate materials for Event	1 day	Wed 1/19/11	Wed 1/19/11	45	
51	Confirm availability of 495's for Kaizen Event No. 2	1 day	Thu 1/20/11	Thu 1/20/11	50	
52	Briefing meeting with 495's Pre-Kaizen	1 day	Fri 1/21/11	Fri 1/21/11	51	
53	Visit to D.R. Cancelled due to weather complications	0 days	Fri 1/21/11	Fri 1/21/11	49,52	
54	Conference call with Dresser Rand to present proposed Kaizen ideas	0 days	Fri 1/21/11	Fri 1/21/11	53	
55	Obtain feedback and agreement on next steps for layout implementation.	1 day	Mon 1/24/11	Mon 1/24/11	54	
56	Dresser Rand starts implementation of RIT design.	2 days	Tue 1/25/11	Wed 1/26/11	55	
57	Feedback from floor personnel is obtained on Layout changes	0 days	Wed 1/26/11	Wed 1/26/11	56	
58	RIT adjusts layout design according to D.R. feedback.	1 day	Thu 1/27/11	Thu 1/27/11	57	
59	D.R. priorities changed, RIT design rejected, counter design proposed.	1 day	Fri 1/28/11	Fri 1/28/11	58	
60	Create an implementation plan for the new proposed design.	10 days	Mon 1/31/11	Fri 2/11/11	59	
61	Implementation plan and report presented to D.R.	0 days	Fri 2/11/11	Fri 2/11/11	60	
62	Incorporate DR feedback for final presentation	3 days	Mon 2/14/11	Wed 2/16/11	61	
63	Final Presentation.	1 day	Fri 2/18/11	Fri 2/18/11	62	

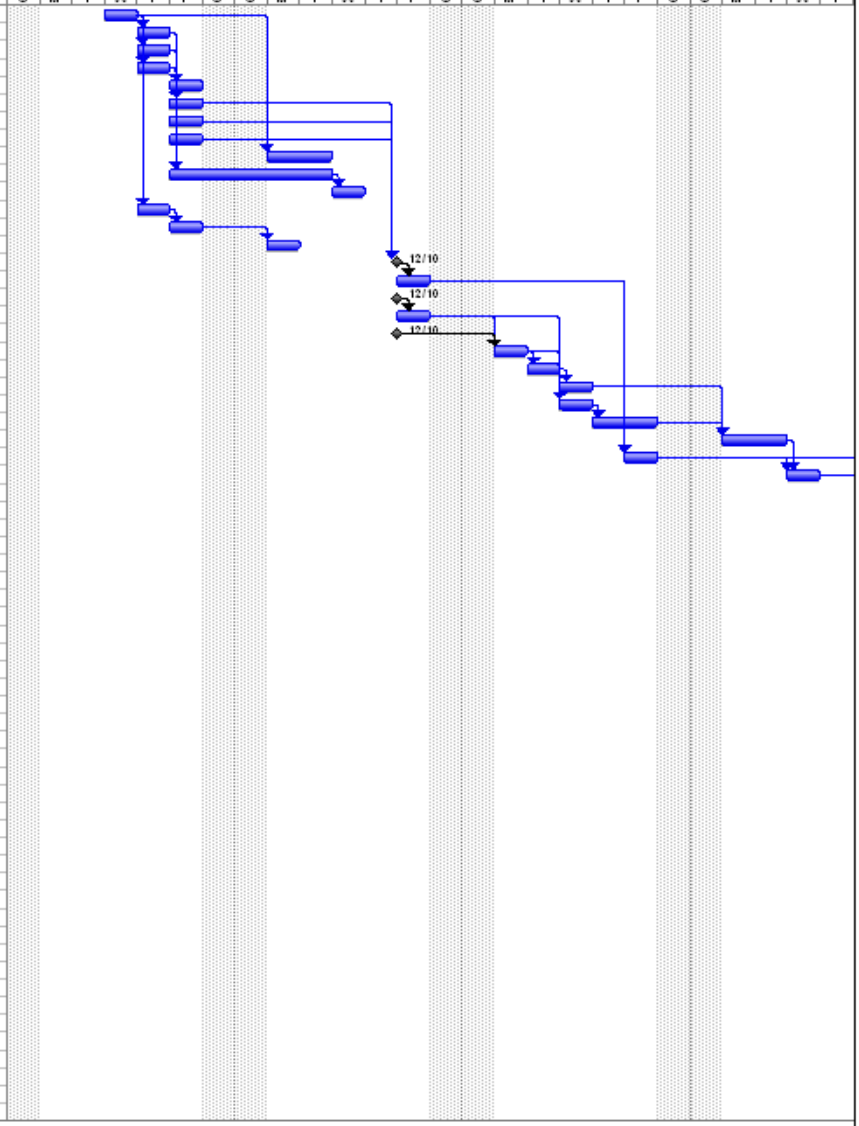

Project: MSD 2 Project Plan
Date: Mon 1/31/11

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

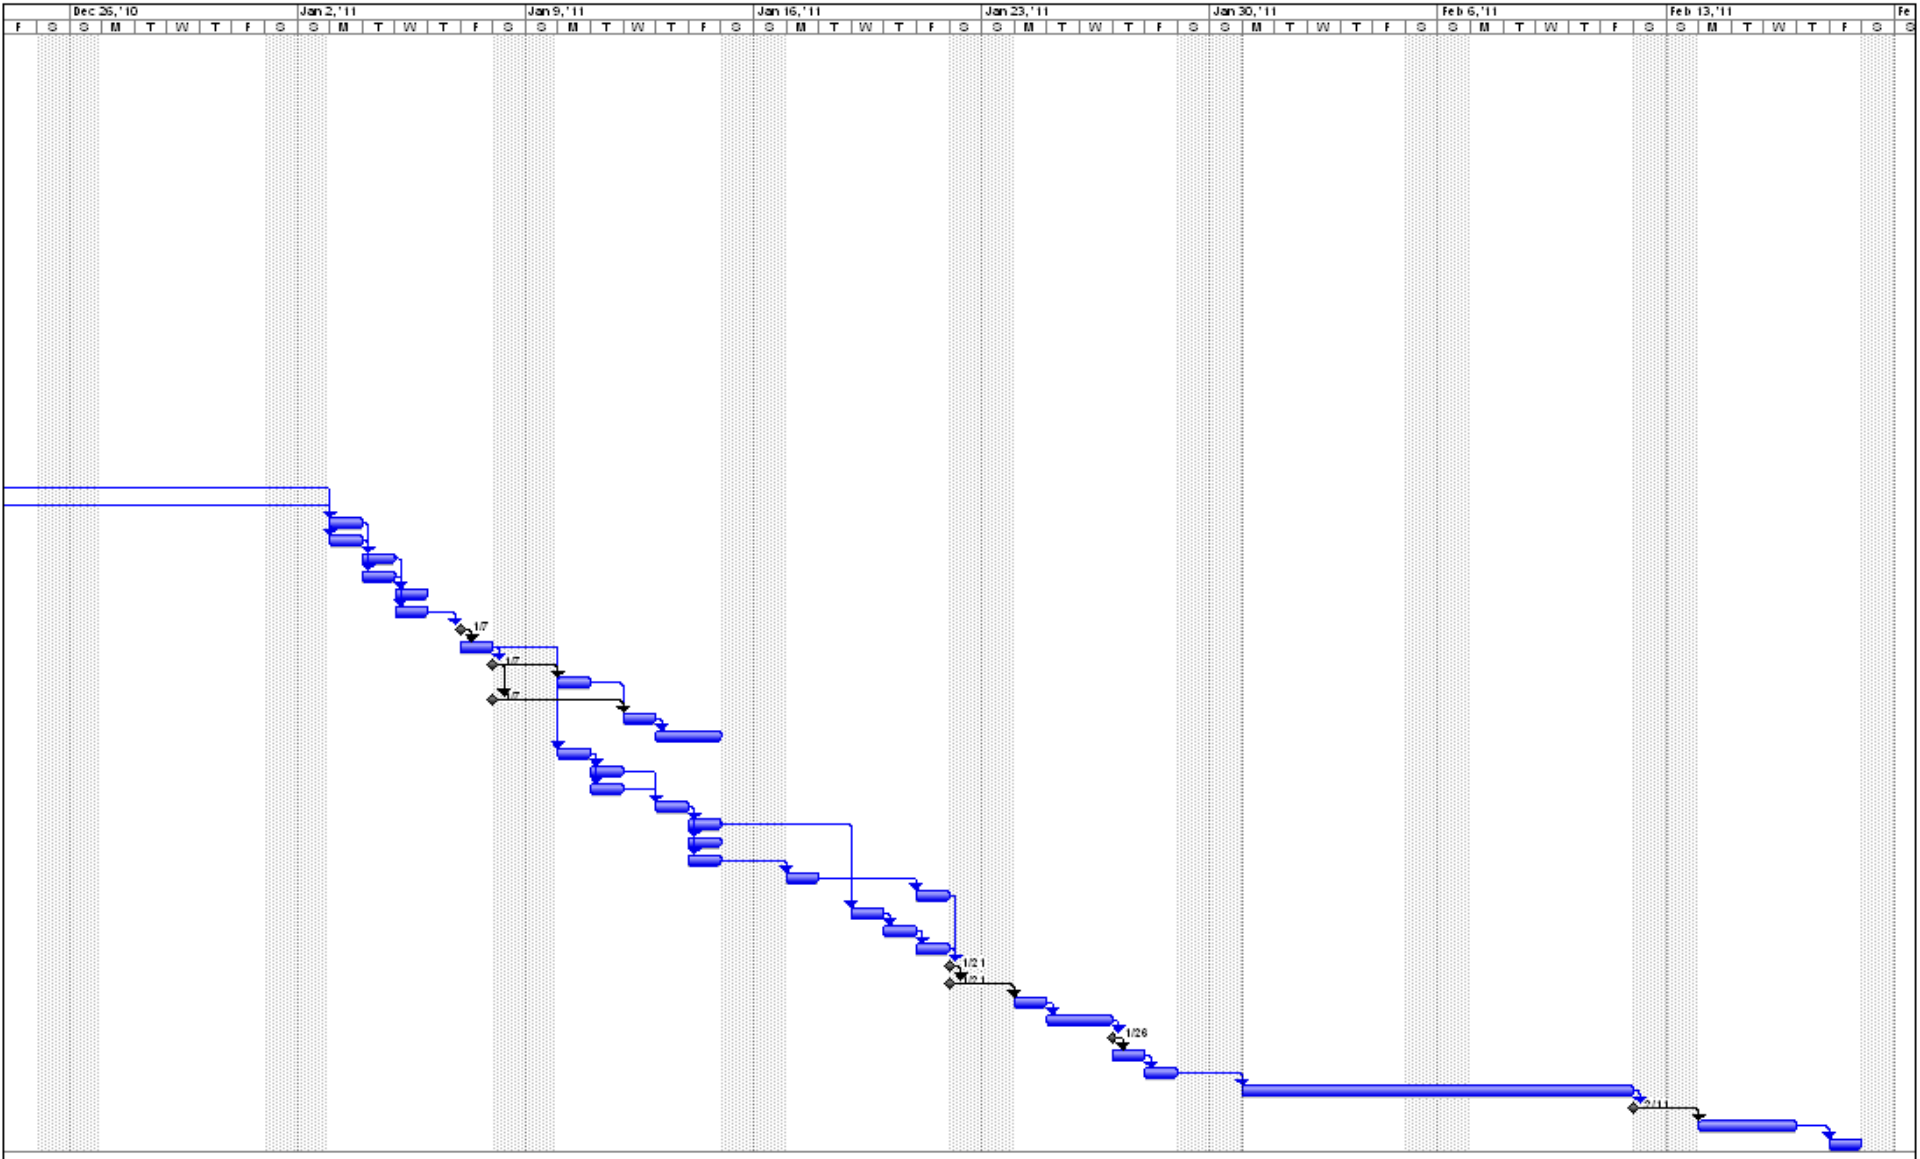

Project: MSD 2 Project Plan
Date: Mon 1/31/11

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
